

Midocean University
College of Business Administration
Master of Risk Management
Final project proposal
2023 - 2024



Risk management of oil and gas projects in Saudi Arabia

إدارة مخاطر مشاريع النفط والغاز في المملكة العربية السعودية

Research Supervisor:

Dr/ Walid Soliman.

Research group:

Maram Alrasheed (221001615) Team leader.

Ahmed Aleid (221000680).

Manahel Alarfaj (221001708).

Introduction

The Demand for Oil and Gas keeps rising around the world and energy sector in Saudi Arabia has the biggest focus in terms of supplying the high-quality products in timely manner and competitive costs. As the market demand keeps increasing, the number of Oil and gas Projects will increase also which, in turn, involves so many types of Risk that need to be monitored and managed to ensure safe Project delivery within the planned budget, quality and time. (Zand, E. D. ,2009)

There are some challenges in managing oil and gas Projects in Saudi Arabia due to the complexity of the resources required to build up the projects within specific scope and budget and plan. The more complex is the project, the more risks are expected to be encountered so it becomes a crucial at early stage of the project to develop a risk analysis and strategies to manage the risks during the entire cycle of the project.

Risk is defined as uncertainty of an event that can impact positively or negatively; therefore, management of the potential risk will assure the continuity of the development and project completion as planned.

Study problem

During the cycle of the projects, Risk management is a critical step that should be assessed and monitored because poor assessment on the risks and late corrective action taken will lead to failure of the project delivery and overrun on the budget. This research will outline the relative risks to oil and gas projects of companies in Saudi Arabia and evaluate the strategies applied to deal with those risks for project safe delivery.

The importance of studying

The target of this study is to identify the effective application of risk management on the project in Saudi oil and gas companies.

Objectives of the study

1. Identify significant risks related to projects of Oil and Gas Companies in Saudi Arabia.
2. Review risk factors in oil & gas projects, and perform risk assessment & analysis.
3. Outline the suitable Risk management strategies with proper application for projects of Oil and Gas Company in Saudi Arabia.
4. Study the efficiency of risk management tools applied on the projects and Identify risk response methods.
5. Provide findings, feedback, and recommendations as a result of this study.

Study questions, What when how why?

1. What are the risks that impact the timely project delivery in oil and gas projects?
2. What are the procedures used in the past and currently to manage risks of oil and gas projects?
3. What are the effective tools to be used for risk identification and management?
4. How to deliver oil & gas projects in time by applying risk management?

Theoretical premises of study

Applying risk management affects the delivery of oil & gas projects in Saudi Arabia, and determines their Success or failure.

Methodology and research methods

1. Review literature and previous studies to collect data and form a list of risk factors that affect projects of oil & gas.
2. Meeting and contacting experts in Saudi Arabia to discuss risks and issues affecting project delivery from their perspective and add them to the list.
3. Conduct a questionnaire survey, with experts, for more data collection and to complete the list of the considerable risks.
4. Analyze all gathered data to determine the most important risk factors of oil and gas projects in Saudi Arabia.
5. Apply risk management tools to control and manage risks.
6. Conduct a questionnaire survey, with experts, to measure the effectiveness of risk management on the project success in many aspects. (Qualitative method / Quantitative method).
7. State all results and describe the findings to give proper recommendations.

Study tools

1. Interviews
2. Questionnaires
3. online surveys
4. Data analysis

Fields of study

1. Risk Management.
2. Business Management.
3. Project Management.
4. Engineering.
5. Supply Chain Management

Previous studies and theoretical framework


Project Risk evaluation reaches to the level where it could be more reliable due to the methods that have been used to avoid the anticipated risks that might affect the project execution. Such as, FMEA and HAZOP and FTA . (Suda, K. A., Rani, N. S. A., Rahman, H. A., & Chen, W. 2015). A review on risks and project risks management: oil and gas industry. International Journal of Scientific Engineering, 6(8), 938-943. Implementation of these methods become a challenge to the oil and gas sector as there is a lack of awareness in the interfaces between the Project execution plan and Risk management plan. In Fact , Finalizing the Project plan and sequence of activities without linking the anticipated risks that might occur to each activity will lead to negative impact on both cost and schedule. Project stakeholders should finalize the anticipated risks in the risk profile and keep it updated and monitored. Training project team members on the methods developed to evaluate the risks in daily activities with frequent coaching sessions will make the team members responsible about their safe achievement of subjective tasks and sharing their thoughts and proposals on the best practice ways to complete certain job.

Proposed tab according to the time plan

1/ Time plan for the proposal:

Sr	Planned activities	Week 1	Week 2	Week 3	Week 4	Week 5
1	Team building					
2	Research Plan discussion					
3	Drafting the title and sourcing for references					
4	Drafting the proposal					
5	Finalizing the proposal					

2/ Time plan for the research:

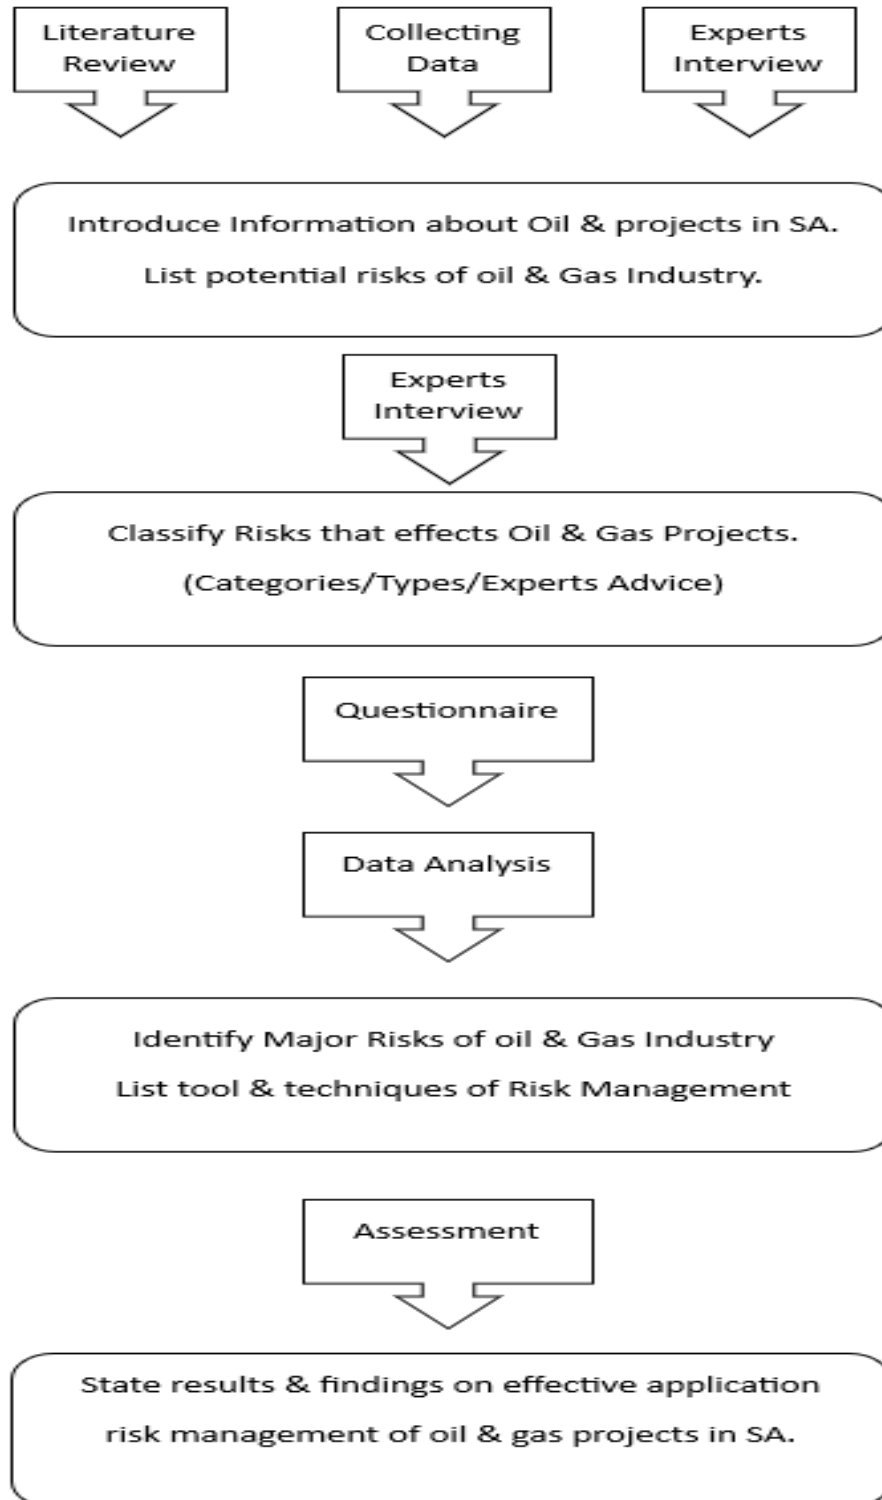

List of references and preliminary sources

- Zand, E. D. (2009). Risk analysis in oil and gas projects: a case study in the Middle East (Doctoral dissertation, Massachusetts Institute of Technology).
- Suda, K. A., Rani, N. S. A., Rahman, H. A., & Chen, W. (2015). A review on risks and project risks management: oil and gas industry. *International Journal of Scientific Engineering*, 6(8), 938-943.
- Kraidt, L, Shah, RK, Matipa, WM and Borthwick, F (2018) *An Analysis of the Critical Risk Factors in Oil and Gas Pipeline Projects using a Comprehensive Risk Management Framework*. In: ARCOM Conference Proceedings . pp. 360-369. (Association of Researchers in Construction Management 34th (ARCOM 4th), 03 September 2018 - 05 September 2018, Belfast).
- Rawat, A., Gupta, S. and Rao, T.J. (2023), "A review on prospective risks and mitigation for oil and gas projects: implication for Indian CGD companies", *International Journal of Energy Sector Management*, Vol. 17 No. 1, pp. 41-62.
- Saudi Aramco Annual Report 2022. pp. 70-72.
- Ahmad, N. K. W., de Brito, M. P., Rezaei, J., & Tavasszy, L. A. (2017). An integrative framework for sustainable supply chain management practices in the oil and gas industry. *Journal of Environmental Planning and Management*, 60(4), 577-601.
- Top risks facing the oil and gas industry in 2022 - and what you can do about it, *Seven keys to get your company ready for the unexpected*. KPMG International Limited.
- Osabutey, D., Obro-Adibo, G., Agbodohu, W., & Kumi, P. (2013). Analysis of risk management practices in the oil and gas industry in Ghana. Case study of Tema Oil Refinery (TOR). *European journal of business and management*, 5(29), 139-149.
- AlNoaimi, F. A., & Mazzuchi, T. A. (2021). Risk management application in an oil and gas company for projects. *International Journal of Business Ethics and Governance*, 1-30.

- Bigliani, R. (2013). Reducing risk in oil and gas operations. *IDC Energy Insights*, (May), 1-15.
- Lenkova, O. V. (2018). Risk management of oil and gas company in terms of strategic transformations. *Espacios*, 39(6), 30-30.
- Rogers, V. C., & Ethridge, J. R. (2016). Enterprise Risk Management in the Oil and Gas Industry: An Analysis of Selected Fortune 500 Oil and Gas Companies' Reaction in 2009 and 2010. *American Journal of Business Education*, 9(1), 23–30.
- Al-Qubaisi, S. S., & Ajmal, M. (2018). Determinants of operational efficiency in the oil and gas sector. *Benchmarking: An International Journal*, 25(9), 3357–3385.
- A.Kassem, M., Khoiry, M. A., & Hamzah, N. (2019). Risk factors in oil and gas construction projects in developing countries: a case study. *International Journal of Energy Sector Management*, 13(4), 846–861.
- Chima, C. M. (2007). Supply-chain management issues in the oil and gas industry. *Journal of business & economics research (JBER)*, 5(6).
- Sarfaraz, A.H., Yazdi, A.K., Hanne, T., Hosseini, R.S., & Moradi, M.R. (2022). A Decision Support System for Evaluating Success Factors of Projects in the Oil and Gas Industry. *Mathematical Problems in Engineering*.
- Chen, W. (2015). A Review on Risks and Project Management: Oil and Gas Industry.
- Abubakar, T.S. (2014). A study of sustainability in the oil and gas supply chain.
- Quintino, A., Lourenço, J.C., & Catalão-Lopes, M. (2022). An Integrated Risk Management Model for an Oil and Gas Company. *International Journal of Economics and Statistics*.
- Sargsyan, G., Slaydon, J., Venta, E.R., Colon, R., & Latiolais, P. (2020). Analysis of Risk Management Practices of the Oil and Gas Industry in Southeast Texas During Hurricane Harvey. *Journal of Applied Business and Economics*.

Hatefi, M.A. (2018). Assessment of Risk Factors of a Completed Oil and Gas Project, with the Use of a Hybrid EVM-SAW Method.

Kassem, M.A., Khoiry, M.A., & Hamzah, N. (2020). Assessment of the effect of external risk factors on the success of an oil and gas construction project. *Engineering, Construction and Architectural Management*, 27, 2767-2793.

Kraidl, L. (2020). DEVELOPMENT OF AN INTEGRATED RISK MANAGEMENT FRAMEWORK FOR OIL AND GAS PIPELINE PROJECTS.

Muralidhar, K. (2010). Enterprise risk management in the Middle East oil industry. *International Journal of Energy Sector Management*, 4, 59-86.

Pinha, D.C., & Ahluwalia, R.S. (2018). Flexible resource management and its effect on project cost and duration. *Journal of Industrial Engineering International*, 15, 119-133.

Bickel, J.E., & Bratvold, R.B. (2008). From Uncertainty Quantification to Decision Making in the Oil and Gas Industry. *Energy Exploration & Exploitation*, 26, 311 - 325.

Annamalah, S., Raman, M., Marthandan, G., & Logeswaran, A.K. (2018). Implementation of Enterprise Risk Management (ERM) Framework in Enhancing Business Performances in Oil and Gas Sector. *Economies*, 6, 4.

Elhoush, R. (2017). Investigation into the current project risk management practices within the Libyan oil and gas industry.

Zuofa, T., & Ochieng, E.G. (2014). Issues in Risk Management: the Perspectives of Managers in Nigeria's Oil and Gas Industry. *International journal of engineering research and technology*, 3.

Abdoul Nasser, A.H., Ndalila, P.D., Mawugbe, E.A., Emmanuel Kouame, M., Arthur Paterne, M., & Li, Y. (2021). Mitigation of Risks Associated with Gas Pipeline Failure by Using Quantitative Risk

Management Approach: A Descriptive Study on Gas Industry. *Journal of Marine Science and Engineering*.

Karami, M., Samimi, A., & Jafari, M.S. (2020). Necessity to Study of Risk Management in Oil and Gas Industries (Case Study: Oil Projects).

Egboga, I., & Worlu, G. (2020). PROJECT RISK AVOIDANCE AND PROJECT EXECUTION IN NIGERIA OIL AND GAS INDUSTRY [PENGHINDARAN RISIKO PROYEK DAN PELAKSANAAN PROYEK DI INDUSTRI MINYAK DAN GAS di NIGERIA]. *DeReMa (Development Research of Management): Jurnal Manajemen*, 15, 171-182.

Khadem, M., Piya, S., & Shamsuzzoha, A.H. (2018). Quantitative risk management in gas injection project: a case study from Oman oil and gas industry. *Journal of Industrial Engineering International*, 14, 637-654.

Mahmoud Aboelkheir, I.M. (2022). Review of Literature on Political Risks to the Operations of Large Oil & Gas Companies and Their Mitigation in Yemen. *Cognizance Journal of Multidisciplinary Studies*.

Kassem, M.A., Khoiry, M.A., & Hamzah, N. (2019). Risk factors in oil and gas construction projects in developing countries: a case study. *International Journal of Energy Sector Management*.

Kassem, M.A. (2022). Risk Management Assessment in Oil and Gas Construction Projects Using Structural Equation Modeling (PLS-SEM). *Gases*.

Kalia, V.K., & Müller, R.M. (2015). Risk Management at Board Level : A Practical Guide for Board Members.

Kadam, P.P. (2021). Risk Management in Oil and Gas (EPC) Industry. *International Journal for Research in Applied Science and Engineering Technology*.

Saptarini, D., & Nainggolan, Y.A. (2022). Risk Management in Oil and Gas Field Development Project with Marginal Resources: A Case in Mature Field in East Kalimantan. *European Journal of Business and Management Research*.

Richard, E.M., & Paschal, W.B. (2022). Risk Management in Upstream Oil and Gas Businesses in Tanzania. *Business Management Review*.

Zemenkova, M.Y., Zemenkov, Y.D., Gladenko, A., & Chizhevskaya, E. (2020). Risk management of oil and gas transportation facilities based on reliability indicators monitoring. *IOP Conference Series: Materials Science and Engineering*, 952.

Nova, N.R., Wiguna, I.P., & Nadjadji, A. (2019). Risk management system model to improve the reputation of oil and gas companies in the Java island - Indonesia. *MATEC Web of Conferences*.
