



جامعة الجميع الذكية
EVERYONE'S SMART UNIVERSITY

Everyone's Smart University

Project (Spring 2021)

Student Name	أحمد عبدالله العسكري	اسم الطالب
Students I.D	2021200657	الرقم الجامعي

Section

Master

Date

Thursday

18 / 03 / 2021.

Course Code

(PMG510)

Project Risk Management

Instructions:

- اخر موعد للتسليم هو يوم السبت 2021-05-08 في تمام الساعة ٩ مساءً.
- الإجابة متاحة باللغة الإنجليزية أو اللغة العربية مع مراعاة أن تكون المصطلحات العلمية باللغة الانجليزية.
- يتم تسليم المشروع في صيغة ملف . pdf مع الالتزام نموذج الجامعة ولن تقبل أي مستندات أخرى.
- يجب مراعاة أقسام البحث الرئيسية (مقدمة Introduction، دراسات علمية سابقة Literature Review، طريقة البحث Methodology، النتائج والمناقشة Results and Discussion ، وأخيراً المراجع References . وان كان هناك ملحقات Appendices يتم إضافتها)
- يجب الالتزام بـ Theme موحد كما يلي:
- حجم الخط 12.
- نوع الخط Arial.
- لون الخط أسود.
- المسافة بين الأسطر 1.5 line spacing
- عدد صفحات البحث (لا يقل عن ثلاث صفحات ولا يزيد عن ست صفحات).

Instructor's Name: Eng. Mosaab M. Hamed

Project:

Risk Identification and Analysis (Based on the project you chose in APM)

The objective of this report is to identify project risks, prepare a risk probability matrix, and carry out an analysis of selected risks. Referring to the project you select in **Advanced projects management APM course**, your task is to prepare a risk management plan that identifies potential risks in **the selected stage of the project** and identify risk management strategies.

From the course content and readings, you know that the overall purpose of risk planning is to anticipate possible risk events and be ready to take appropriate action when risk events occur—to eliminate or reduce negative impacts on the project.

You may wish to begin this exercise with a brainstorming about potential risks to get candidate risks “on the table” for consideration. And then identify and refine that wording for risks that have some realistic chance of occurring in this stage. For example, potential weather problems present a real obstacle to completing field data collection by the planned completion date. It is also an issue that the project manager will ultimately have to plan for, as opposed to other issues such as a major disaster (e.g., your office burning down), is not a high-enough probability event that requires much time in planning. As described below, you will select several of the identified risks and carry out a risk analysis.

You will use the distilled list of risks to make a risk probability/impact matrix. The matrix will have at least three categories (high/medium/low) for probability and impact.

Remember that it is important to name risks effectively—use words that describe the risk event and point to the impact on the project (e.g., “injury of field technician disrupts data installation work”).

After completion of the risk matrix, document a risk analysis for the selected risks. This detailed documentation for that selected risk will include:

- a description of the risk and potential impacts (schedule, quality of work, cost, etc.) on the project.
- indicators or triggers that would be monitored to help identify the risk as early as possible.
- specific risk response strategies to take.

Using probability and impact matrix calculate the **Expected Monetary Value (EMV)** for all risks that have the impact in terms of cost \$\$.

Best of luck...

المشروع:

التعرف على المخاطر وتحليلها (بحث مبني على مشروعك الذي اخترته في مادة ادارة المشاريع المتقدمة)

الغرض من هذا التقرير هو التعرف على المخاطر المحيطة بالمرحلة التي تختارها المرحلة من مراحل مشروعك (نفس المرحلة التي اخترت التطرق لها في مشروعك لمادة إدارة المشاريع المتقدمة Advanced project management) حيث أن مهمتك هي تحضير خطة متكاملة لإدارة المخاطر تشمل التعريف بالمخاطر المحتملة التي تحيط بتلك المرحلة وتحضير مصفوفة احتمالية المخاطر ومن ثم القيام بالتحليل لهذه المخاطر المختارة وتحديد استراتيجيات ادارة المخاطر المناسبة لكل خطر على حدة.

من محتويات المقرر والمصادر الأخرى المتاحة أصبحت تعلم الآن أن الغرض العام لمرحلة التخطيط للمخاطر هي توقع أحداث المخاطر المحتملة والتجهز لاتخاذ ردة الفعل المناسبة عند وقوع الخطر – لمنع أو تقليل الآثار السلبية على المشروع.

قد تحبذ بداية هذا البحث بعصف ذهني عن ماهية المخاطر التي قد تحيط بتلك المرحلة من مراحل مشروعك, وذلك للحصول على قائمة بتلك المخاطر. ومن ثم تحديد وتصفية هذه القائمة للوصول إلى قائمة مختصرة بالمخاطر التي لها فرصة واقعية أكبر في الحدوث. على سبيل المثال: المشاكل الجوية المتوقعة والتي تمثل عقبة حقيقية أمام اكتمال جمع البيانات من المواقع في أو قبل الوقت المحدد، هذه تعتبر مشكلة على مدير المشاريع أن يضعها في الحسبان. من ناحية أخرى، فإن المخاطر غير الواقعية مثل الكوارث الطبيعية والأعاصير (تلك التي تسبب حريقاً بمكتبك وفقدان الأوراق المهمة) ليست لها احتمالية وقوع عالية وبالتالي لاتستدعي تضيق الكثير من الوقت في التخطيط لها. كما سيتبين لك، ستقوم باختيار عدة مخاطر من تلك التي قمت بالتعرف عليها لتحليلها.

ستقوم باستخدام هذه القائمة المختصرة لعمل مصفوفة المخاطر (الاحتمالية/الأثر). المصفوفة ستحتوي على الأقل على ثلاث تصنيفات (عالي/متوسط/منخفض) للإحتمالية والأثر.

لاتنس استخدام أسماء تصف طبيعة المخاطر بصورة فعالة – قم باستخدام كلمات تصف الحادثة الخطرة وتشير الى أثرها على المشروع (مثل: إصابة أحد الفنيين في الموقع مما يؤثر على أعمال التركيب).

بعد انتهاءك من مصفوفة المخاطر، قم بتوثيق تحليلك للمخاطر المختارة. هذا التسجيل المفصل للمخاطر يجب أن يتضمن:

- وصف للخطر واثاره المحتملة (الجدولة، جودة العمل، التكلفة، الخ)
- المؤشرات والمحفزات التي يجب مراقبتها للمساعدة في التعرف على هذا الخطر قبل وقوعه
- تفصيل للاستجابة المقترحة للتصدي لهذا الخطر

باستخدام مصفوفة الاحتمالات والتأثير ، احسب **القيمة النقدية المتوقعة (EMV)** لجميع المخاطر التي لها تأثير من حيث التكلفة \$\$.

مع تمنياتي بالتوفيق..

Risks of buying a used house

Introduction

Nowadays, housing and owning your own house is a big challenge and concern for anyone worldwide. Besides the high prices of buying new homes, we could face other problems such as bad houses infrastructures, architecture mistakes, and other crucial factors.

I planed to buy I used the house for many reasons. The most important reason is to reduce the certainty of lousy infrastructure, after three to five years of building homes all inadequate infrastructure will appear in it will be easy to discover it comparing to new houses also the prices of used houses is lower compared to new homes.

My concern was finding a good use house in a good neighborhood with a reasonable price and good infrastructure.

I found the house and did here the risk assessment.

Methodology

Here I will go through a process like 8Rs and 4Ts, which will help to find the risk's probabilities and its impacts. Brainstorming is the first step to identify all the possible risks. I will make a list of them.

Table 1

No.	List of Risks
1	Choose the wrong house
2	Choose the wrong neighborhood
3	The price of a house is too high

4	Bad infrastrucuter
5	The cost of the restoration is high
6	The prices of lands will decrease after buying the house

Now we have a list of risks, we will make a risks matrix (determine the probability and impact of each risk), which will go after that to the risk register. (low = 0 to 0.29, medium = 0.3 to 0.69, high = 0.7 to 1).

Table 2

No.	List of Risks	Probability	impact
1	Choos the wrong house	0.2	0.8
2	Choose the wrong neighbourhood	0.69	0.7
3	The price of a house is too high	0.29	0.3
4	Bad infrastrucuter	0.69	1
5	Cost of the restoration is high	0.5	0.8
6	The prices of lands will decrease after buying the house	0.69	0.29

After collecting and evaluating the risks, it's time to assess the severity to start thinking about the response plans for each risk and try to mitigate the impact. For calculating the

severity, we used Risks Matrix and Bow-Tie to find the response plan. **Figure1**

Pr ob abi lity	0.7-1	high	high	medium
	0.3-0.69	high	medium	low
	0-0.29	medium	low	low
		0.7-1	0.3-0.69	0-0.29
		Impact		

Figure2

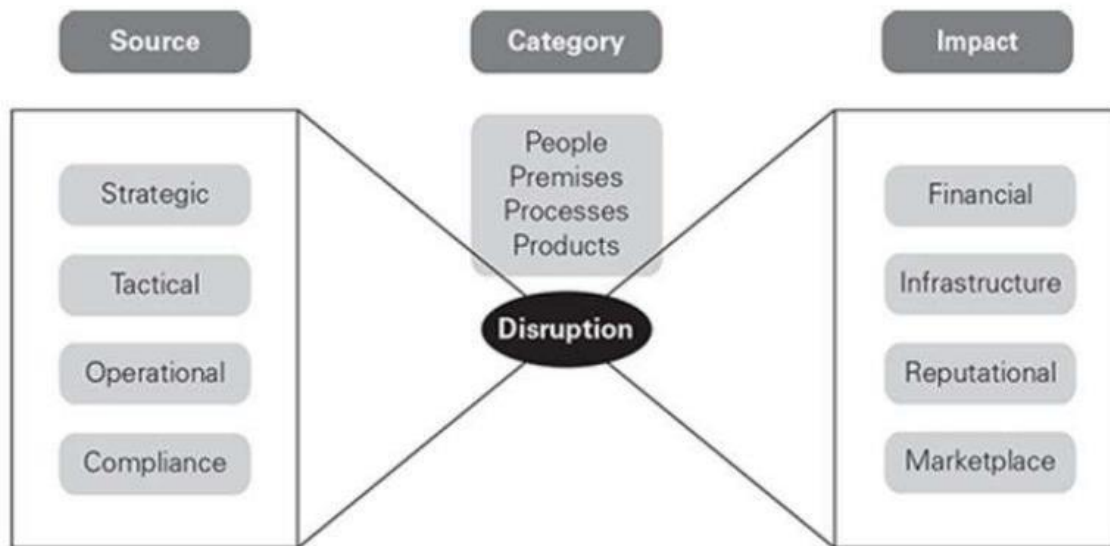


Table 3

No.	List of Risks	Probability	impact	Severity	Response plan	Mitigate Action
1	Choose the wrong house	0.2	0.8	High	Asking the advice of an expert before buying any house.	Ask the previous owner to reduce the price or do all renewal work inside the house.

2	Choose the wrong neighbourhood	0.69	0.7	High	Ask and research before giving the final decision of buying the house	Try to build go relation with the people there and look for a new home if possible
3	The price of the house is too high	0.29	0.3	Medium	Make sure I buy the right price involve experts to evaluate the price.	Start the negotiating with the owner to reduce the price.
4	Bad infrastrucuter	0.69	1	High	Consult an agency to diagnoses the house and discover any issues	Ask from the owner and the legislation agencies to study the cost and cut it from the total price
5	The cost of the restoration is high	0.5	0.8	High	Consult an agency to diagnoses the house and discover any issues and the prices of the renewal	Do the most critical fixation
6	The prices of lands will decrease after buying the house	0.69	0.29	low	We can not expect the future, so no need to plan for any interventions because I will stay at the house	No need for any mitigations

Discussion

In (Table 3) we can see the result of the reposing plan and how to mitigate the risk. It is important to note that we should be aware of all dangers but shouldn't waste time on risks with green color. It is better to focus on orange and red risks because they have a higher probability and huge impact.

References

