



جامعة الجميع الذكية
EVERYONE'S SMART UNIVERSITY

Everyone's Smart University

Project (Spring 2021)

Student Name	أسعد همام عبدالاله ياقتي	اسم الطالب
Students I.D	2021201900	الرقم الجامعي

Section

Course

Code

Thursday

Master

Date

18 / 03 / 2021.

(PMG506)

Advanced project Management

Instructions:

- اخر موعد للتسليم هو يوم الخميس 2021-05-29 في تمام الساعة 9 مساءً.
- الإجابة متاحة باللغة الإنجليزية أو اللغة العربية مع مراعاة أن تكون المصطلحات العلمية باللغة الانجليزية.
- يتم تسليم المشروع في صيغة ملف pdf مع الالتزام نموذج الجامعة ولن تقبل أي مستندات أخرى.
- يجب مراعاة أقسام البحث الرئيسية (مقدمة Introduction، دراسات علمية سابقة Literature Review، طريقة البحث Methodology، النتائج والمناقشة Results and Discussion، وأخيراً المراجع References. وان كان هناك ملحقات Appendices يتم إضافتها)
- يجب الالتزام بـ Theme موحد كما يلي:
- حجم الخط 12.
- نوع الخط Arial.
- لون الخط أسود.
- المسافة بين الأسطر 1.5 line spacing

• عدد صفحات البحث (لا يقل عن ثلاث صفحات ولا يزيد عن ست صفحات).

Instructor's Name: ~~Eng. Amaal Aburumman~~ **Eng. Dr. Akram M. S. Ali**

Project:

You are required to document your role in administering a project. The project may be set in a business, social, sporting, or family environment but must be of a significant size and scale. If you do not have an actual project to write about you may complete the project hypothetically. **This report will be between three to six pages in length.** This is a significant research project.

Your report must address ~~each~~ **ONE** of the following issues:

1. Identify and describe the purpose, scope, and objectives of the project. **Display this information using an appropriate tool.**
2. Describe how the team is given an outline of the project.
3. Describe the strategies that are going to be set up to maintain communication with the team members.
4. Describe the tools that are going to be used to monitor the goals, time frames or milestones.
5. Identify project milestones and activities. **Display this information using an appropriate tool.**
6. Create a budget and link the costs to the key milestones for a project.
7. Describe how you are going to divide tasks and resources amongst a project team. **Display this information using an appropriate tool.**
8. Briefly describe how the progress will be monitored.
9. How are current project records maintained? Who has responsibility for this? provide some recommendations on how this process could be improved.
10. Describe the current procedure for finalizing projects. Create your own procedure and identify how you will evaluate the success of the project.
11. Legislation that may affect the project including health and safety, and anti-discrimination legislation.

Best of luck...

المشروع:

مطلوب منك توثيق دورك في إدارة مشروع. قد يتم تعيين المشروع في بيئة تجارية أو اجتماعية أو رياضية أو عائلية ولكن يجب أن يكون بحجم مناسب. إذا لم يكن لديك مشروع فعلي لتكتب عنه ، فيمكنك إكمال المشروع افتراضياً. سيكون هذا التقرير من ثلاث إلى ست صفحات .

يجب أن يعالج تقريرك كل من **احد** القضايا التالية:

1. تحديد ووصف الغرض والنطاق والأهداف من المشروع. اعرض هذه المعلومات باستخدام أداة مناسبة.
2. صف كيف يتم إعطاء الفريق مخططاً تفصيلياً للمشروع.
3. وصف الاستراتيجيات التي سيتم وضعها للحفاظ على التواصل مع أعضاء الفريق.
4. صف الأدوات التي سيتم استخدامها لرصد الأهداف أو الأطر الزمنية أو المعالم.
5. تحديد معالم المشروع والأنشطة. اعرض هذه المعلومات باستخدام أداة مناسبة.
6. إنشاء موازنة وربط التكاليف بالمعالم الرئيسية للمشروع.
7. صف كيف ستقوم بتقسيم المهام والموارد بين فريق المشروع. اعرض هذه المعلومات باستخدام أداة مناسبة.
8. صف بإيجاز كيف سيتم رصد التقدم.
9. كيف يتم الاحتفاظ بسجلات المشروع الحالية؟ من المسؤول عن هذا؟ تقديم بعض التوصيات حول كيفية تحسين هذه العملية.
10. وصف الإجراء الحالي لإنهاء المشاريع. قم بإنشاء الإجراء الخاص بك وحدد كيفية تقييم نجاح المشروع.
11. التشريعات التي قد تؤثر على المشروع بما في ذلك الصحة والسلامة ، وتشريعات مكافحة التمييز.

مع تمنياتي بالتوفيق..

Point 8 : is discussed in this report.

Flower shop

Introduction:

In this research, I am going to talk about my own project that I spent a lot of time planning it. It is about a flower shop, I started this project two years ago after planning everything, identifying the objective, setting schedules and budget, and of course identifying the possible risks that I may face.

Now I am in the execution phase and personally I am the project manager of it.

In this report I am going to identify the ways how to monitor and control the project progress.

For the definition and the importance of monitoring that happen at all phases in the project life cycle we can say that

“In the project life cycle, the project monitoring and control phase happens in tandem with the execution phase. Project management monitoring and controlling involves actively reviewing the status of your project as it proceeds, evaluating potential obstacles, and implementing necessary changes.”

“During this phase, organizations need to juggle several responsibilities, including keeping to the schedule, staying within budget, avoiding scope creep, and managing risk.”

Controlling costs is a very important part of managing project. However, differences in orders or going away from scope may cause risk in budget. In monitoring and controlling phase, remember to clearly and consistently track and report updates to your projected budget.

Quality control remember that all your deliverables should satisfy your customers.


Method:

To track your project control , we have many tools to use as review meetings , bar charts , S curve and many more.

In this report I am going to use the bar charts in order to track one month of performance in my flower shop .



Basically I set the budget in the schedule and I need to compare it with the work performed and costs.

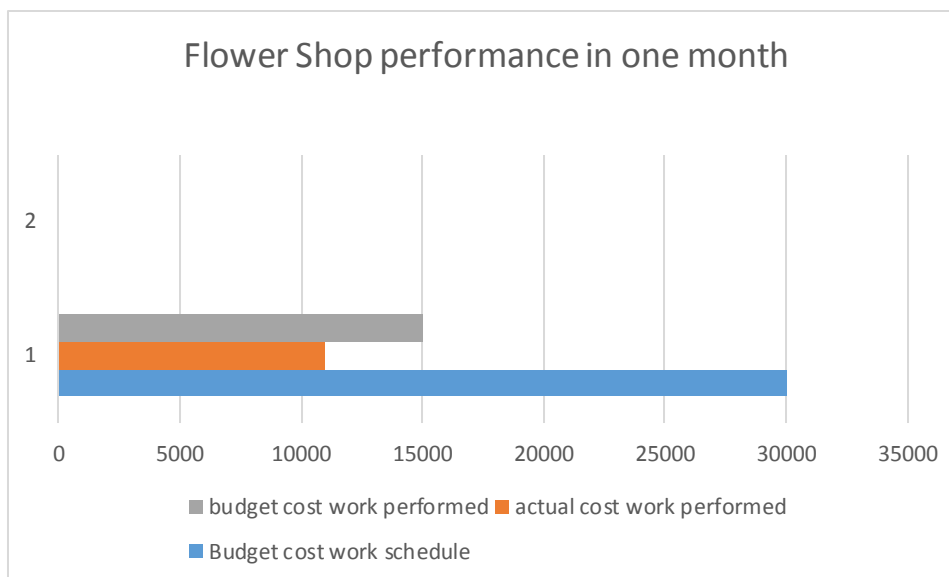

We can the cost variance clearly here in the cost as shown in the bar charts

Results and discussion:

To calculate the CV : $BCWP - ACWP = 15000 - 11000 = 4000$ which is good for the project.

To calculate the SV : $BCWP - BCWS = 15000 - 30000 = -15000$ which is a problem in the project performance and progress and we need to track this quickly and address this issue In order to get the project back on track.

Reference:

<https://www.workfront.com/project-management/life-cycle/monitoring-controlling>
