



مجموعة جامعة
الجميع الذكية
للتعليم القابضة

MIDOCEAN
UNIVERSITY

Project Governance

Lecture 8

PMG 424

Ch8 – Governance of Portfolios

Prepared by
Dr Hakem Sharari

www.midocean.ae

Learning Outcomes

- Clarifying the logic behind developing project portfolios.
- Discussing a project portfolio as a governance structure.
- Highlighting the types of decisions made in project portfolios.
- Understanding the role of portfolio optimization strategies.
- Explaining the different measures of project portfolio performance.

The Logic of Portfolios

- A project may consist of a larger or smaller number of ongoing projects being run simultaneously.
- As these projects typically compete for a finite number of often scarce resources, they need to be governed.
- In this case, the focus is on:
 - Ensuring **effectiveness** by ‘doing the right projects’.
 - Ensuring **efficiency** by ‘doing projects right’.

**Whereas Effectiveness Is Achieved Through Project Portfolios, Efficiency Is
Achieved Through Project Programs**

What is a Project Portfolio

- The **project portfolio** is a grouping of projects and programs by similar skills or resource needs, prioritized by their contribution to corporate strategy and managed together to optimize contribution to strategic objectives.
- **Project portfolio management** is concerned with managing competing needs for scarce skills and resources of the various projects in the portfolio.

Effectiveness and Project Portfolios

- **Effectiveness** is achieved through **selection and prioritization** of projects (portfolios) that contribute most to corporate strategy.
- They create the highest value for the corporation and therefore constitute the most economic use of scarce resources.
- This need for **effectiveness** has led to the **development of the project portfolio approach**.

Decisions on Portfolios

- The board of directors makes the decision on **whether** and **how** to use programs and portfolios to implementing the project-based organizational works.
- This decision determines the framework for managers to **decide on the types of projects** in which the organization is going to engage.

Decisions on Portfolios

- The **project-based part of the organizational works** is typically governed by management decisions on:
 - whether, when and how to **share resources** across projects;
 - whether to pursue **higher level goals** which need to be accomplished through several interlinked projects;
 - or whether to focus on **smaller goals** accomplished by **individual projects**.

Possible Governance Structures

Previous Management Decisions
Lead To Four Possible
Governance Structures For
Project-based Organizations

Resources	shared	Portfolio of projects	Hybrid organization
	Not shared	Multi-project organization	Program of projects
		unrelated	related
		Objectives	

Multi-project Organizations

- A multi-project organization is meant to **maximizing the return on individual projects**.
- Projects in this type of organization are **very diverse** and have **little or nothing in common**, thus there are no synergies of objectives or resource usage.
- In such projects, **external resources** with **very specific skill sets** may be used for just the **duration** of a contracted project.

Portfolios of Projects

- A portfolio of projects is meant to **maximizing the effectiveness** by using existing skill sets and contributions to strategic objectives.
- Such organizations group their projects based on **availability of skill sets** and prioritize their projects to maximize their strategic objectives.
- The objectives of projects in a portfolio **do Not necessarily have to be related** to each other; key is **commonality of skill sets** required.

Programs of Projects

- A programs of projects is meant to **maximizing efficiency**.
- Such organizations emphasize synergies stemming from **combining several individual** project objectives **into a larger overall objective**.
- In this type of organization, **skill sets needed may vary significantly** between the individual programs.


Hybrid Organizations

- A hybrid organization is meant to **balancing maximization of effectiveness and efficiency** through a combination of program and portfolio approaches.
- Such organizations achieve their strategic objectives by combining **sharing of skill** sets through portfolios and **relating project objectives** through programs.

Performance of Governance Structures

- **Corporate performance** varies greatly according to **the choice of governance structure**.
- The hybrid organization structure of combining and balancing programs and portfolios is **statistically more successful** than other three approaches.
- The multi-project approach achieves the **lowest** level of performance, while either the programs or portfolios achieve **moderate** performance.

Performance of Governance Structures

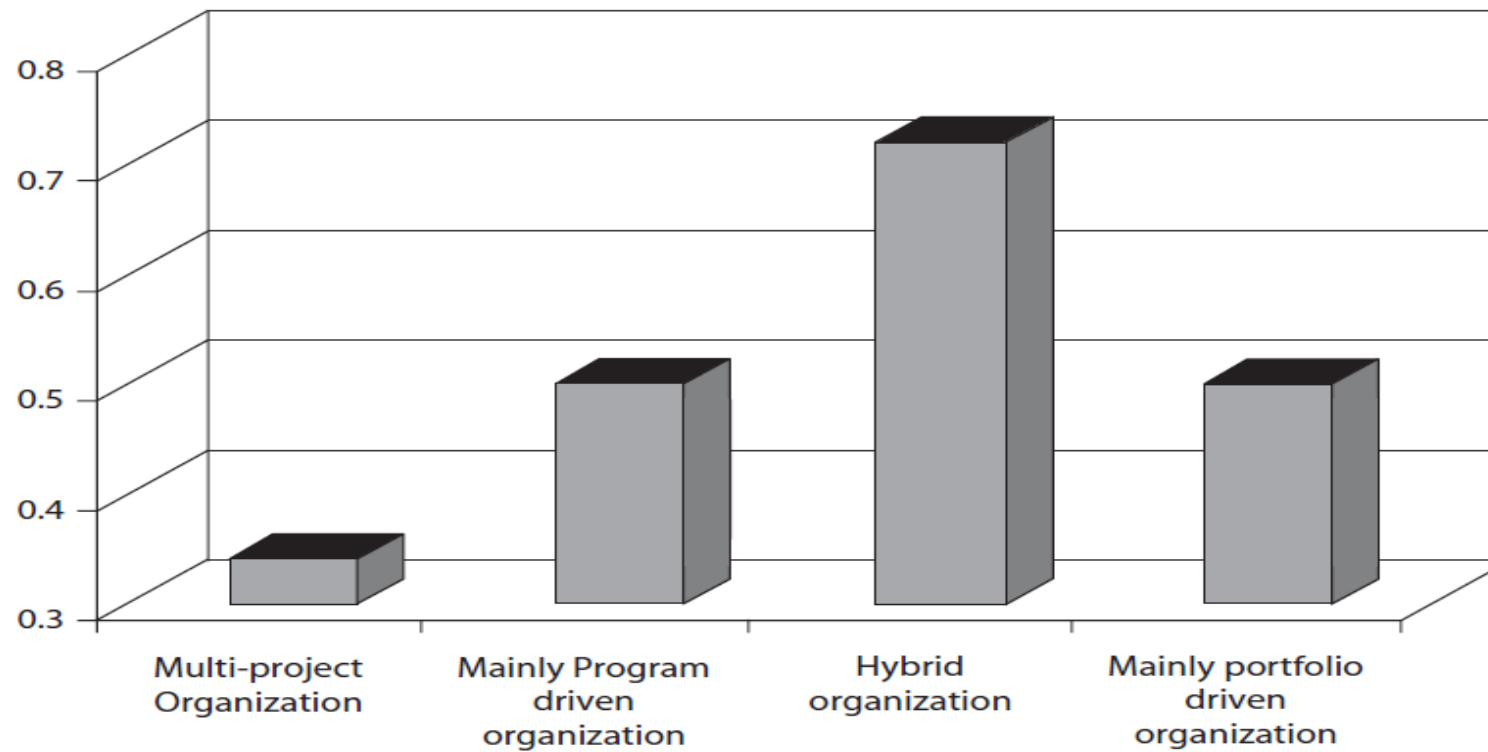

**The Hybrid Approach Balances Both Efficiency and Effectiveness When
Deciding Which Projects To Take On and Which Ones To Drop**

Why Portfolios?

- The objective of project portfolio governance is to ensure that the **best projects** are **selected**; that is, those that will achieve their strategic objectives:
 - in the shortest possible time; and
 - within the constraints of available skills and resources.


Why Portfolios?

- Projects and programs in any given portfolio are screened, selected, prioritized and scheduled based on getting **the highest possible throughput of the ‘best’ projects** for the organization.
- The term **‘throughput’** implies ensuring the greatest number of the best projects implemented by the organization in the shortest possible amount of time.
- The term **‘best’** implies that a large number of good projects might be preferable to a smaller number of excellent projects as the overall throughput will be greater.

Portfolio Management

- **Effective portfolio management** requires a proper communication structure that allows information to flow from portfolios to projects and back again.
- Portfolio managers often communicate portfolio decisions to line or middle management, sponsors (and steering groups).
- Tactical PMOs collect and aggregate project performance and report to the portfolio level.

Portfolio Management

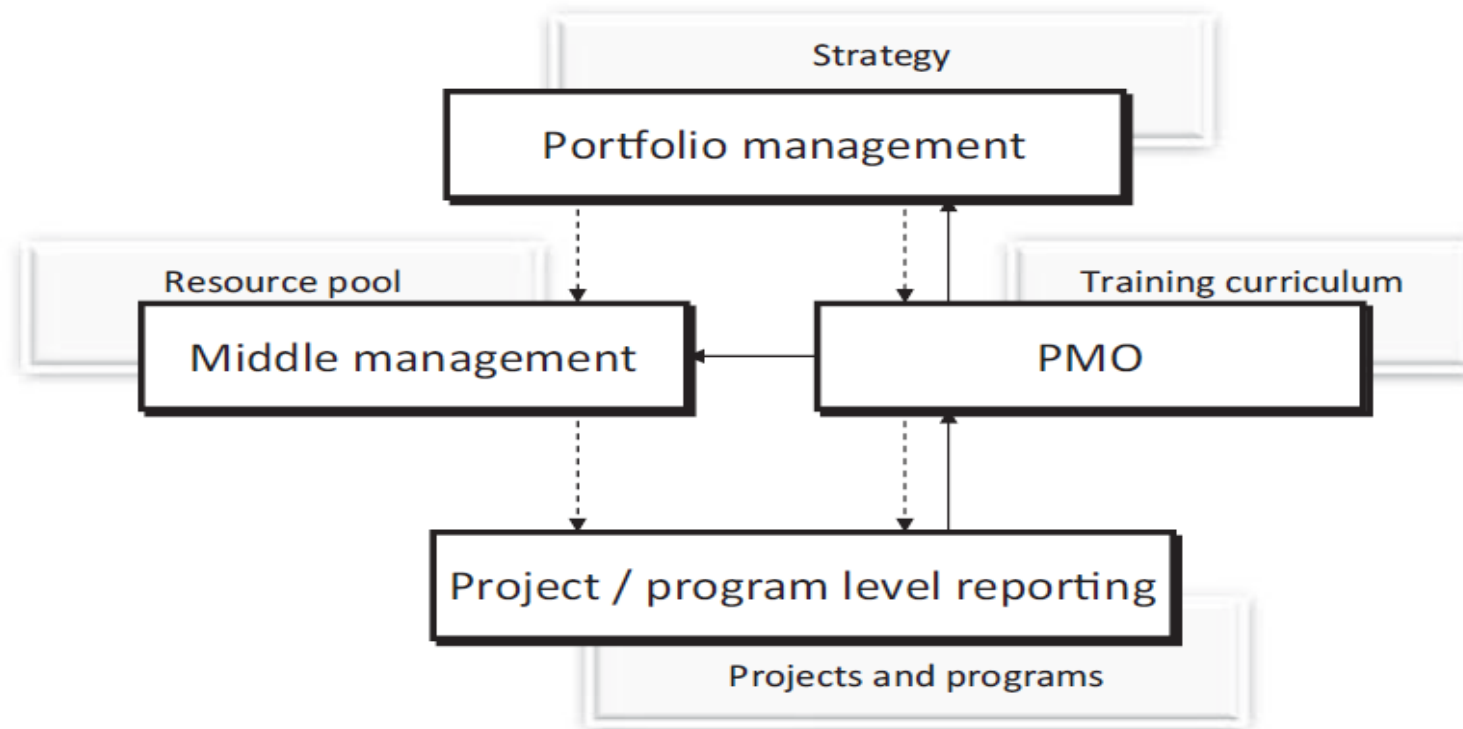

Portfolio Management Objectives

- An important purpose of project portfolio governance is to **achieve the objectives for each portfolio**, which should be derived from the **organization's strategy**.
- These portfolio objectives provide the framework for decision-making within the portfolio.

Portfolio Management Objectives

- Portfolio objectives vary depending upon whether the corporation is **shareholder- or stakeholder** oriented.
- Achieving these objectives involves careful **selection and prioritization** of projects within each portfolio to ensure their alignment with its objectives.

Portfolio Optimization Strategies

- There are **three most often used portfolio optimization strategies** that are either used alone or in combination with each other:
1. Value Maximization.
 2. Balancing.
 3. Strategic Alignment.

Value Maximization Strategy

- In this strategy, projects are selected into the portfolio if they **reach a certain threshold value**; often financial such as Return on Investment (ROI).
- The strategy is **criticized** as being too numbers focused and for **Not factoring in the more qualitative benefits** of each project.
- Corporations that use this as a standalone strategy are seen to perform the **worst** in their industry.

Balancing Strategy

- Projects are selected into the portfolio based on a **balanced weighted measure** of **several parameters** (similar way to an investment fund):
- Examples are:
 - distribution of high versus low-risk projects.
 - distribution of short-term versus long-term projects.

Balancing Strategy

- The balancing matrix uses a number of two-dimensional graphs for each parameter to visualize the relative positions of projects against each other, allowing managers to select the most desirable balance of projects.
- The strategy is **criticized for lack of guidance** on the balancing parameters and weighting criteria.
- Corporations that use this as a standalone strategy are seen to be **more successful** in their industry than those who use Value Maximization as a standalone strategy.

Strategic Alignment Strategy

- This strategy assigns a **budget** value to each **strategic objective** of the corporation; it is also called the **strategic bucket approach**.
- When a project is considered for the portfolio, it is tested against the objectives of each bucket (that is, the strategic goal).
- If the project supports one of the buckets or goals, then it is funded out of the relevant bucket.

Strategic Alignment Strategy

- This strategy requires **detailed planning**, based on a long-term view anticipating future business trends.
- This strategy is often **criticized** for being too **hypothetical** (requires developing hypothesis on future trends).
- Corporations that use this as a standalone strategy are seen to be **the most successful** in their industry.

Choice of Strategy

- The **choice of portfolio optimization** strategy is related to the **orientations** of corporations.
- While corporations that are **shareholder-oriented** use the **Value Maximization** strategy, corporations that are **stakeholder-oriented** use the **Balancing** strategy.
- Corporations that are **both** shareholder- and stakeholder-oriented use the **Strategic Alignment** strategy, as it is contingent on the corporation's strategy.

Roles and Authorities of Portfolio Managers

- Governance of project portfolios also includes deciding on the roles, authorities and decisions on the degree to which the portfolio management process is formalized (or the portfolio manager is engaged).
- **Roles and authorities** assigned to the **portfolio managers** include:
 1. Business management roles and authorities.
 2. Portfolio decision roles and authorities.
 3. Portfolio maintenance roles and authorities.

Roles and Authorities of Portfolio Managers

➤ **Business management roles and authorities:**

- Participation in corporate business planning.
- Special emphasis on contributing to planning for changes in required skill sets and resources.
- Procurement of the agreed-upon quantity and quality of skill sets.

Roles and Authorities of Portfolio Managers

- **Portfolio decision roles and authorities:**
 - Determination of roles.
 - Naming of individuals with the authority to identify, prioritize and select projects within the portfolio.
 - Includes responsibility and authority to start, suspend or terminate projects from within a portfolio.

Roles and Authorities of Portfolio Managers

➤ **Portfolio maintenance roles and authorities:**

- Collection and aggregation of reports.
- Participation in steering groups and project/program plan reviews.
- Identification of bad projects and associated initiation of reviews, handling of issues and so on.
- Coaching of project managers.
- General improvement of organizational processes.

**The Degree To Which the Portfolio Management Process Is Formalized Is
Influenced By the Complexity of the Decision-making Process In the
Organization**

Measuring Portfolio Performance

- **Portfolio performance** is measured using **three groups** of performance variables:
1. Achievement of desired portfolio results: these are aggregated project level measures (customer satisfaction, achieved time, cost, quality).
 2. Achievement of project/program purpose: these show how well the projects and programs have fulfilled their purpose (effectiveness of project selection).
 3. Balancing priorities: these are business level measures (resource retention, timely implementation of programs and stakeholder satisfaction).

**The Three Groups of Measures For Portfolio Performance Should Be Assessed
At Each Portfolio Reporting Cycle**

Conclusions

- The project portfolio is a grouping of projects and programs by similar skills or resource needs, aiming to contribute to a strategic objective.
- Project portfolio management is concerned with managing competing needs for scarce skills and resources of the various projects in the portfolio.

Conclusions

- Whereas efficiency is achieved through project programs, effectiveness is achieved through project portfolios.
- Effectiveness is achieved through selection and prioritization of projects (portfolios) that contribute most to corporate strategy.

Conclusions

- The board of directors makes the decision on whether and how to use programs and portfolios as an approach to implementing the project-based works.
- This decision determines the framework for managers to decide on the types of projects in which the organization is going to engage.

Conclusions

- The hybrid approach of combining and balancing programs and portfolios is statistically more successful than other three approaches.
- The multi-project approach achieves the lowest level of performance, while either the programs or portfolios achieve moderate performance.

Conclusions

- The three portfolio optimization strategies are Value Maximization, Balancing, and Strategic Alignment.
- The choice of portfolio optimization strategy is related to the orientations of corporations (shareholder or stakeholder).


Task 1

- Find an internationally successful company, and discuss how their portfolio optimization strategies and decisions have contributed to their favourable performance?

Task 2

- Find a local company in which the portfolio management process is formalized, and discuss how formalization impacted the roles and authorities of the portfolio manager?

Reference

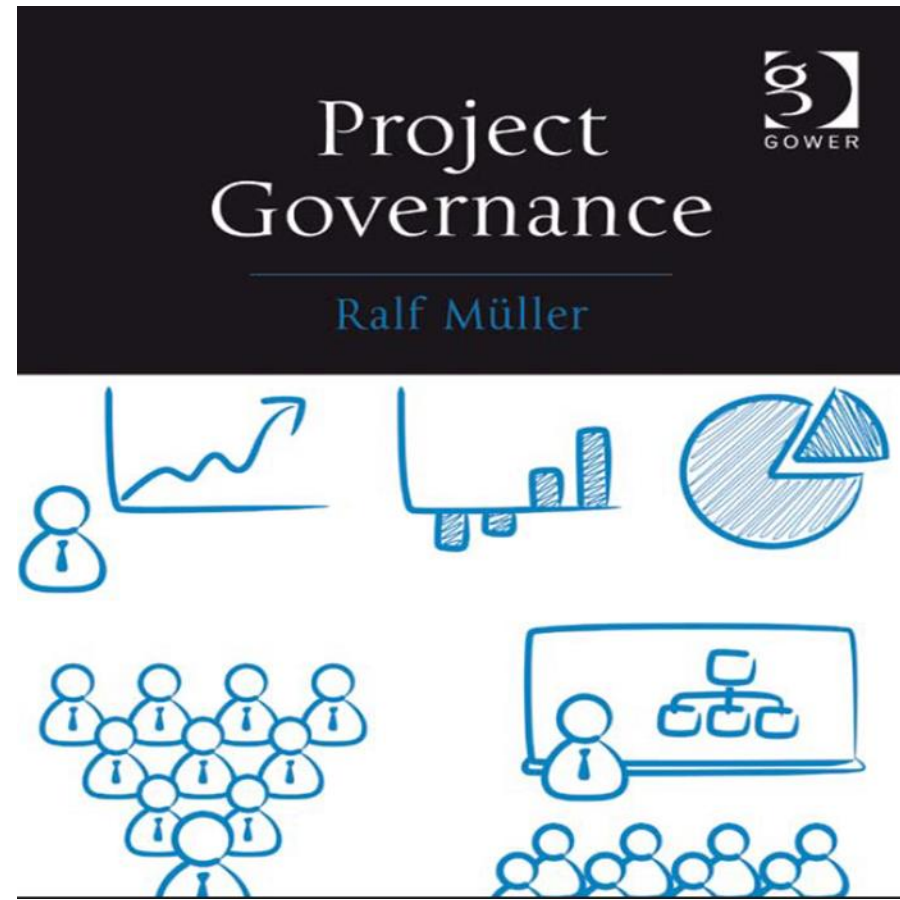



مجموعة جامعة
الجميع الذكية
للتعليم القابضة

MIDOCEAN
UNIVERSITY

Ch5_Q20

Thank You

