

# **Final Project 1**

Code: MGM 496-PMG496

## **Project Template**

Faculty of Management  
Midocean University

**Midocean University**

**Faculty of Management**

**Department/ Specialization .....**



**Project title**

**The Role of Risk Management in Project Success in Oil  
and Gas Projects**

**Student name**

**Radi Ali Sulail**

**Graduation Project – 1**

**Faculty of Management - Midocean University**

**Supervisor**

**Dr. Abdulrahman Nadir**

**Faculty member- Faculty of management- Midocean University**

**July 28, 2025**

## Table of Contents

|                                                                                 |                                     |
|---------------------------------------------------------------------------------|-------------------------------------|
| 1. Chapter 1: Introduction .....                                                | 3                                   |
| 1.1. Research Background.....                                                   | 4                                   |
| 1.2. Research Problem.....                                                      | 7                                   |
| 1.2.1. Theoretical Gaps .....                                                   | 7                                   |
| 1.2.2. Practical Gaps .....                                                     | 7                                   |
| 1.3. Research Significance .....                                                | 8                                   |
| 1.3.1. At the theoretical level .....                                           | 8                                   |
| 1.3.2. At the practical level .....                                             | 8                                   |
| 1.4. Research Questions .....                                                   | 8                                   |
| 1.5. Research Objectives .....                                                  | 9                                   |
| 1.6. Research Hypotheses.....                                                   | 9                                   |
| 1.7. Research Model.....                                                        | 10                                  |
| 1.8. Research Methodology.....                                                  | 10                                  |
| 1.9. Scope of The Study .....                                                   | 10                                  |
| 1.10. The Suggested Project Structure.....                                      | 11                                  |
| 2. Chapter 2: Literature Review .....                                           | <b>Error! Bookmark not defined.</b> |
| 2.1. Introduction .....                                                         | <b>Error! Bookmark not defined.</b> |
| 2.2. The independent variable .....                                             | <b>Error! Bookmark not defined.</b> |
| 2.3. The dependent variable .....                                               | <b>Error! Bookmark not defined.</b> |
| 2.4. The relationship between the independent and the dependent variables ..... | <b>Error! Bookmark not defined.</b> |
| 2.5. Conclusion.....                                                            | <b>Error! Bookmark not defined.</b> |
| References.....                                                                 | <b>Error! Bookmark not defined.</b> |

# **1. Chapter 1: Introduction**

## 1.1. Research Background

The oil and gas industry are widely recognized as one of the most complex and challenging industries in the world. It operates in an environment characterized by high levels of uncertainty, volatility, and risk. From exploration to production, companies involved in oil and gas projects constantly face numerous technical, operational, financial, and environmental risks that could significantly impact project outcomes. As a result, managing these risks has become a critical element in ensuring the success of projects within this sector. Risk management is no longer seen as an optional process but rather as a core component of project management strategies aimed at minimizing uncertainties and enhancing the likelihood of project success.

Over the past few decades, the global energy sector has witnessed significant transformations driven by technological advancements, environmental regulations, and geopolitical dynamics. Oil and gas projects, particularly in upstream exploration and drilling activities, involve massive financial investments, stringent health and safety requirements, and complex logistical operations. In addition to these factors, projects are often conducted in remote locations under harsh environmental conditions, further increasing the risk exposure. Any failure in effectively managing risks can result in project delays, budget overruns, safety incidents, and sometimes even complete project failure. Therefore, understanding how risk management influences project success has become an increasingly relevant and essential area of study.

Despite the availability of various risk management frameworks and methodologies, many oil and gas projects continue to suffer from unexpected challenges that negatively impact performance. While some companies have integrated risk management into their organizational culture, others still approach it as a compliance requirement rather than a proactive management tool. This gap between theory and practice raises critical questions about the real effectiveness of risk management processes in driving successful project outcomes. Furthermore, while much of the existing literature on project management addresses risk management from

a general perspective, there is a limited focus on the unique nature of risks in the oil and gas sector, especially in regions like the Middle East, where operational conditions, regulatory environments, and geopolitical factors present distinctive challenges.

Risk management in project management is typically structured into several key stages: risk identification, risk analysis, risk response planning, and risk monitoring and control. Each of these stages plays a vital role in ensuring that potential threats are properly understood and addressed before they can escalate into major issues. Risk identification involves recognizing potential internal and external risks that may affect the project. Risk analysis assesses the likelihood and potential impact of each risk, prioritizing them based on their severity. Risk response planning focuses on developing strategies to mitigate, transfer, accept, or avoid risks. Finally, risk monitoring ensures that identified risks are tracked throughout the project lifecycle, and any emerging risks are promptly addressed.

The failure to properly execute any of these stages can jeopardize the entire project. For example, if certain risks are not identified during the planning phase, they may cause unexpected disruptions later in the execution phase. Similarly, if risk responses are inadequately planned or implemented, the project could face serious cost overruns or safety incidents. Therefore, effective risk management is directly linked to achieving project success, which is typically measured in terms of delivering the project within the defined scope, budget, schedule, and quality standards while maintaining safety and stakeholder satisfaction.

In the context of the oil and gas industry, project success is particularly critical due to the high stakes involved. The failure of a single drilling project can lead to millions of dollars in financial losses, reputational damage, environmental harm, and even legal consequences. For instance, historical cases like the Deepwater Horizon disaster serve as stark reminders of what can go wrong when risk management is insufficient or poorly executed. Although not every project carries risks of that magnitude, even routine drilling operations face challenges such as equipment failure, well control issues, cost escalation, logistical delays, and fluctuating market conditions.

The importance of risk management has been further amplified by recent global challenges, including supply chain disruptions, fluctuating oil prices, and the push towards sustainable energy transitions. Companies are under

increasing pressure to optimize operational efficiency while maintaining stringent safety and environmental standards. As a result, effective risk management is not only about preventing negative outcomes but also about creating value by enabling better decision-making, improving stakeholder confidence, and enhancing the overall resilience of projects.

This study seeks to contribute to the ongoing discourse on the role of risk management in project success, focusing specifically on oil and gas projects. By examining how risk management practices influence key project performance indicators—such as cost, time, quality, and safety—this research aims to bridge the gap between theoretical models and practical applications in the field. Furthermore, this study will highlight the importance of embedding a risk-aware culture within organizations, where risk management is viewed as an integral part of project planning and execution rather than a reactive process.

Additionally, this research is particularly relevant to the Middle East region, where the oil and gas industry plays a pivotal role in the economy. Projects in this region are often characterized by unique operational challenges, including extreme weather conditions, remote work sites, cross-border logistics, and evolving regulatory landscapes. Despite the wealth of experience in the region's oil and gas sector, there is limited academic research that specifically examines how risk management practices contribute to project success within this context. Therefore, this study seeks to fill that gap by providing empirical insights that can inform both practitioners and scholars.

In summary, the increasing complexity of oil and gas projects necessitates a comprehensive approach to risk management that goes beyond compliance and documentation. Effective risk management should be seen as a strategic enabler of project success, contributing not only to risk mitigation but also to enhancing overall project performance. This research aims to explore the extent to which risk management practices—particularly risk identification, analysis, response, and monitoring—directly influence the success of oil and gas projects. The findings are expected to offer practical recommendations for improving project outcomes, fostering a risk-aware culture, and ultimately ensuring the long-term sustainability and profitability of projects within this critical industry.

## **1.2. Research Problem**

Although risk management is widely recognized as a critical component of project management, many oil and gas projects continue to experience failures due to poor risk management practices. There is often a gap between the theoretical frameworks of risk management and their practical application in real projects.

### **1.2.1. Theoretical Gaps**

Existing literature emphasizes risk management models but often lacks empirical studies specific to the oil and gas sector, particularly in regions like the Middle East where operational risks are unique

### **1.2.2. Practical Gaps**

In practice, project managers may not fully implement risk management processes due to lack of training, resources, or organizational support. This leads to unforeseen challenges affecting the success of projects in terms of cost, time, and safety

- **Main Research Problem:**

To what extent does effective risk management influence the success of oil and gas projects?

### **1.3. Research Significance**

#### **1.3.1. At the theoretical level**

This study contributes to the existing body of knowledge by providing empirical evidence on the relationship between risk management and project success in the oil and gas sector

#### **1.3.2. At the practical level**

The findings will benefit project managers, engineers, and decision-makers in the oil and gas industry by offering practical insights into how risk management can improve project outcomes.

### **1.4. Research Questions**

1. How does risk identification affect the success of oil and gas projects?

2. How does risk analysis contribute to better project outcomes?
3. What is the impact of risk response planning on project performance?
4. How does continuous risk monitoring influence project success?


## **1.5. Research Objectives**

- To examine the relationship between risk identification and project success.
- To assess how risk analysis influences project outcomes.
- To evaluate the impact of risk response planning on project performance.
- To analyze the role of risk monitoring in achieving project success.

## **1.6. Research Hypotheses**

- H1: Risk identification has a significant positive impact on project success.
- H2: Risk analysis significantly contributes to project performance.
- H3: Risk response planning positively affects project success.
- H4: Risk monitoring has a significant effect on the success of oil and gas projects.

## 1.7. Research Model

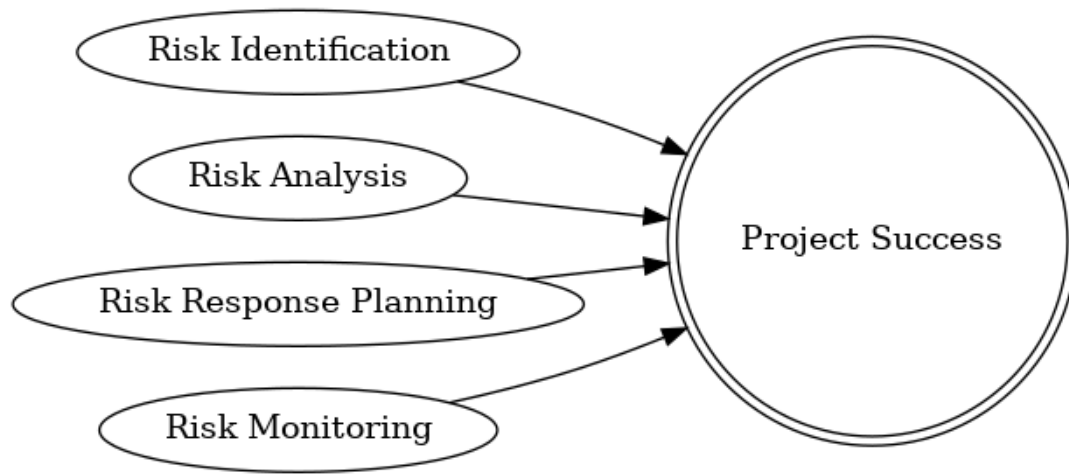

## 1.8. Research Methodology

This study will use a quantitative research approach by distributing questionnaires to project managers, engineers, and supervisors in oil and gas companies. The data collected will be analyzed using statistical tools (e.g., SPSS) to test the hypotheses and answer the research questions.

## 1.9. Scope of The Study

- Geographical Scope: Oil and gas projects in Saudi Arabia and the Gulf region.
- Sector Scope: Upstream and downstream oil and gas operations.

- Time Scope: Projects executed between 2020 and 2025

## **1.10. The Suggested Project Structure**

### **1. Introduction**

- Background and Context
- Problem Statement
- Research Questions and Objectives
- Significance of Study

### **2. Literature Review**

- Overview of Key Concepts
- Theoretical Framework
- Review of Previous Studies
- Gap in Literature

### **3. Research Methodology**

- Research Design
- Population and Sampling
- Data Collection Methods
- Data Analysis Techniques

### **4. Data Analysis and Results**

- Presentation of Findings
- Statistical Interpretation
- Discussion in Relation to Objectives

## **5. Conclusions and Recommendations**

- Summary of Key Findings
- Practical and Theoretical Implications
- Recommendations for Future Research
