

Everyone's Smart University

Project (Spring 2021)

Student Name	ناجي حمد حسين الصيعري	اسم الطالب
Students I.D	2021202836	الرقم الجامعي

Section

Master

Date

Thursday

18 / 03 / 2021.

Course Code

(PMG510)

Project Risk Management

Instructions:

- آخر موعد للتسليم هو يوم السبت 2021-05-08 في تمام الساعة ٩ مساءً.
- الإجابة متاحة باللغة الإنجليزية أو اللغة العربية مع مراعاة أن تكون المصطلحات العلمية باللغة الإنجليزية.
- يتم تسليم المشروع في صيغة ملف pdf مع الالتزام نموذج الجامعة ولن تقبل أي مستندات أخرى.
- يجب مراعاة أقسام البحث الرئيسية (مقدمة Introduction، دراسات علمية سابقة Literature Review، طريقة البحث Methodology، النتائج والمناقشة Results and Discussion، وأخيراً المراجع References. وان كان هناك ملحقات Appendices يتم إضافتها)
- يجب الالتزام بـ Theme موحد كما يلي:
- حجم الخط 12.
- نوع الخط Arial.
- لون الخط أسود.
- المسافة بين الأسطر line spacing 1.5
- عدد صفحات البحث (لا يقل عن ثلاث صفحات ولا يزيد عن ست صفحات).

Instructor's Name: Eng. Mosaab M. Hamed

Project:

Risk Identification and Analysis (Based on the project you chose in APM)

The objective of this report is to identify project risks, prepare a risk probability matrix, and carry out an analysis of selected risks. Referring to the project you select in **Advanced projects management APM course**, your task is to prepare a risk management plan that identifies potential risks in **the selected stage of the project** and identify risk management strategies.

From the course content and readings, you know that the overall purpose of risk planning is to anticipate possible risk events and be ready to take appropriate action when risk events occur—to eliminate or reduce negative impacts on the project.

You may wish to begin this exercise with a brainstorming about potential risks to get candidate risks “on the table” for consideration. And then identify and refine that wording for risks that have some realistic chance of occurring in this stage. For example, potential weather problems present a real obstacle to completing field data collection by the planned completion date. It is also an issue that the project manager will ultimately have to plan for, as opposed to other issues such as a major disaster (e.g., your office burning down), is not a high-enough probability event that requires much time in planning. As described below, you will select several of the identified risks and carry out a risk analysis.

You will use the distilled list of risks to make a risk probability/impact matrix. The matrix will have at least three categories (high/medium/low) for probability and impact.

Remember that it is important to name risks effectively—use words that describe the risk event and point to the impact on the project (e.g., “injury of field technician disrupts data installation work”).

After completion of the risk matrix, document a risk analysis for the selected risks. This detailed documentation for that selected risk will include:

- a description of the risk and potential impacts (schedule, quality of work, cost, etc.) on the project.
- indicators or triggers that would be monitored to help identify the risk as early as possible.
- specific risk response strategies to take.

Using probability and impact matrix calculate the **Expected Monetary Value (EMV)** for all risks that have the impact in terms of cost \$\$.

Best of luck...

المشروع:

التعرف على المخاطر وتحليلها (بحث مبني على مشروعك الذي اخترته في مادة ادارة المشاريع المتقدمة)

الغرض من هذا التقرير هو التعرف على المخاطر المحيطة بالمرحلة التي تختارها المرحلة من مراحل مشروعك (نفس المرحلة التي اخترت التطرق لها في مشروعك لمادة إدارة المشاريع المتقدمة Advanced project management) حيث أن مهمتك هي تحضير خطة متكاملة لإدارة المخاطر تشمل التعريف بالمخاطر المحتملة التي تحيط بتلك المرحلة وتحضير مصفوفة احتمالية المخاطر ومن ثم القيام بالتحليل لهذه المخاطر المختارة وتحديد استراتيجيات ادارة المخاطر المناسبة لكل خطر على حدة.

من محتويات المقرر والمصادر الأخرى المتاحة أصبحت تعلم الان أن الغرض العام لمرحلة التخطيط للمخاطر هي توقع أحداث المخاطر المحتملة والتجهز لاتخاذ ردة الفعل المناسبة عند وقوع الخطر – لمنع أو تقليل الاثار السلبية على المشروع.

قد تحبذ بداية هذا البحث بعصف ذهني عن ماهية المخاطر التي قد تحيط بتلك المرحلة من مراحل مشروعك, وذلك للحصول على قائمة بتلك المخاطر. ومن ثم تحديد وتصفية هذه القائمة للوصول إلى قائمة مختصرة بالمخاطر التي لها فرصة واقعية أكبر في الحدوث. على سبيل المثال: المشاكل الجوية المتوقعة والتي تمثل عقبة حقيقية أمام اكتمال جمع البيانات من المواقع في أو قبل الوقت المحدد، هذه تعتبر مشكلة على مدير المشاريع أن يضعها في الحسبان. من ناحية أخرى، فإن المخاطر غير الواقعية مثل الكوارث الطبيعية والأعاصير (تلك التي تسبب حريقاً بمكتبك وفقدان الأوراق المهمة) ليست لها احتمالية وقوع عالية وبالتالي لاتستدعي تضيق الكثير من الوقت في التخطيط لها. كما سيتبين لك، ستقوم باختيار عدة مخاطر من تلك التي قمت بالتعرف عليها لتحليلها.

ستقوم باستخدام هذه القائمة المختصرة لعمل مصفوفة المخاطر (الاحتمالية/الأثر). المصفوفة ستحتوي على الأقل على ثلاث تصنيفات (عالي/متوسط/منخفض) للإحتمالية والأثر.

لاتنس استخدام أسماء تصف طبيعة المخاطر بصورة فعالة – قم باستخدام كلمات تصف الحادثة الخطرة وتشير الى أثرها على المشروع (مثل: إصابة أحد الفنيين في الموقع مما يؤثر على أعمال التركيب).

بعد انتهاءك من مصفوفة المخاطر، قم بتوثيق تحليلك للمخاطر المختارة. هذا التسجيل المفصل للمخاطر يجب أن يتضمن:

- وصف للخطر واثاره المحتملة (الجدولة، جودة العمل، التكلفة، الخ)
- المؤشرات والمحفزات التي يجب مراقبتها للمساعدة في التعرف على هذا الخطر قبل وقوعه
- تفصيل للاستجابة المقترحة للتصدي لهذا الخطر

باستخدام مصفوفة الاحتمالات والتأثير ، احسب **القيمة النقدية المتوقعة (EMV)** لجميع المخاطر التي لها تأثير من حيث التكلفة \$\$.

مع تمنياتي بالتوفيق..

THE EID AL-FITR DUTY

INTRODUCTION

The combination of risk management processes, together with a description of the framework in place for supporting the process, constitutes a risk management standard¹.

Most risk management publications refer to the benefits of having a common language of risk within the organization. Many organizations manage to achieve this common language and common understanding of risk management processes and protocols at least internally. However, it is usually the case that within a business sector, and sometimes even within individual organizations, the development of a common language of risk can be very challenging¹.

Projects are not without risks, including those related to human health, especially if the work is with a minimum number of team members, such as what is happening during the annual holidays and the National Day.

The project is about the Eid Al-Fitr Duty from 7-05-2021 to 18-05-2021, And run the project under conditions and tight limits of time and team members.

We dealt with in the advanced project management research to a description of the strategies that will be put in place to maintain communication with team members during the Eid Al-Fitr Duty.

There are many risks that may arise in our project, including: -

- 1) Disruption of the medical supply program: - The program may crash due to Internet problems or due to viruses exposed to it.
- 2) Delayed approval of requests from the hospital director: - When any section of the hospital is requested through the program, the hospital director must approve it until it reaches the medical supply department.

- 3) Confusion between departments when dispensing orders, due to the large number of departments compared to the number of employees, for example, the confusion between the children's clinic and the children's section.
- 4) Confusion experienced by team members when working on the day of Eid, which causes them not to do their work efficiently: - Where work in Ramadan is in two shifts in the morning from (10) to (13), and in the evening from (21) until midnight (00), and on the day of Eid, work starts in the morning from 7:30.

LITERATURE REVIEW

Nowadays, risk management is one of the most important research topic in many critical areas. Project goals such as reducing costs and gaining profit can not be accomplished without evaluating and managing the risks².

“The possibility of danger and sufferance of harm or injury” is the definition of risk as per Webster’s New Explorer College Dictionary².

As stated by Raftery, Risk is an abstract concept whose measurement is very difficult. “The possibility or chance of meeting danger, suffering loss or injury” is another definition of risk by The Oxford Advanced Learner’s Dictionary – 5th Edition².

Based on the above, risk management become a significant factor to successful project management².

METHODOLOGY


This research follows the descriptive approach. We focus on studying risk management by gathering data from lessons learned from previous projects.

RESULT AND DISCUTION

No	Description	P	I	EMV
1	Disruption of the medical supply program	0.2	5000	1000
2	Delayed approval of requests from the hospital director	0.3	4000	1200
3	Confusion between departments when dispensing orders	0.2	3000	600
4	Confusion experienced by team members when working on the day of Eid	0.4	5000	2000
TOTAL EMV				4800

Communication has become an important role in the success of projects due to the technological development, and this development must be kept up with and the communication strategies between team members must be constantly updated. With regard to human health and safety, utmost care must be taken in this.

REFERENCES

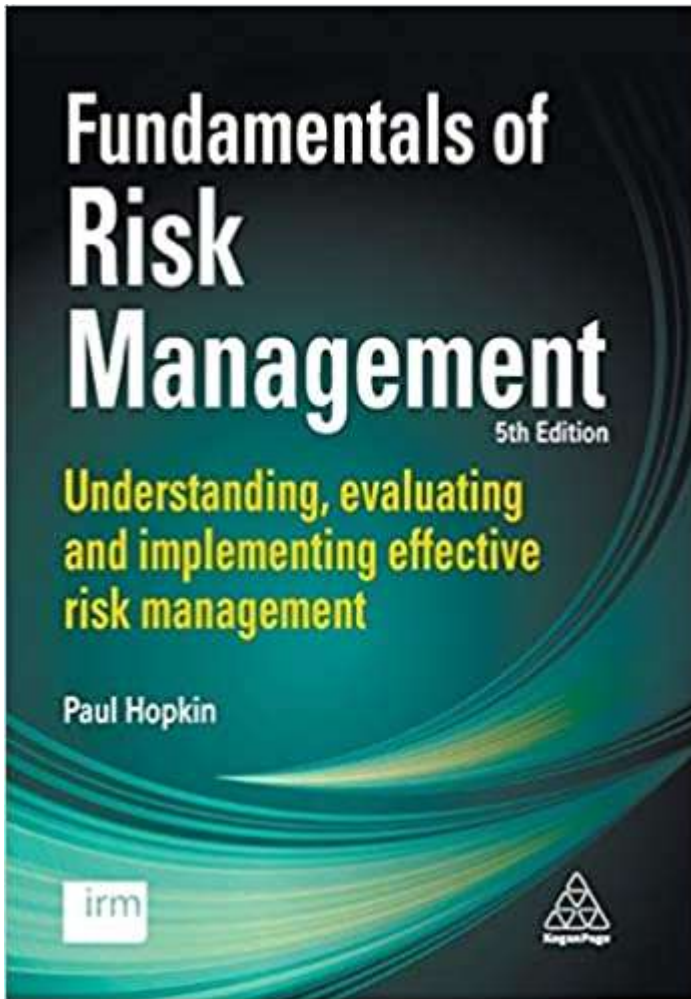

1)

2) All Answers Ltd. November 2018. Literature Review on Risk Management. [online]. Available from: <https://ukdiss.com/examples/risk-management-business.php?vref=1> [Accessed 15 May 2021].
