

Midocean University

Faculty of Management

Bachelor's Project Management



The Impact of Team Communication on Project Timelines in Chemical Plant Construction in Industrial Jubail City

Alaa Ali Alsmhod

2021201820

Final Project – 2

Faculty of Management - Midocean University

Supervisor

Dr. Mona Moustafa Elashry

Faculty member- Faculty of management- Midocean University

25Jun Second Semester

Acknowledgment

Dedication

Abstract

Purpose:

Methodology:

Findings:

Originality & Implication:

Keywords:

Table of Contents

Acknowledgment.....	1
Dedication.....	1
Abstract.....	3
1. Chapter 1: Introduction.....	Error! Bookmark not defined.
1.1. Research Background	Error! Bookmark not defined.
1.2. Research Problem	Error! Bookmark not defined.
1.2.1. Theoretical Gaps	Error! Bookmark not defined.
1.2.2. Practical Gaps	Error! Bookmark not defined.
1.3. Research Significance	Error! Bookmark not defined.
1.3.1. At the theoretical level.....	Error! Bookmark not defined.
1.3.2. At the practical level	Error! Bookmark not defined.
1.4. Research Questions	13
1.5. Research Objectives	14
1.6. Research Hypotheses	14
1.7. Research Model	15
1.8. Scope of The Study	16
1.9. The Project Structure	17
2. Chapter 2: Literature Review.....	Error! Bookmark not defined.
2.1. Introduction.....	Error! Bookmark not defined.
2.2. The independent variable	Error! Bookmark not defined.

2.3. The dependent variable	Error! Bookmark not defined.
2.4. The relationship between the independent and the dependent variables	Error! Bookmark not defined.
2.5. Conclusion	Error! Bookmark not defined.
3. Chapter 3: Research Methodology	Error! Bookmark not defined.
3.1. Introduction.....	Error! Bookmark not defined.
3.2. Operational definitions for research variables	Error! Bookmark not defined.
3.3. Research design (research onion)	Error! Bookmark not defined.
3.4. Research population & Sampling methods and technique.	Error! Bookmark not defined.
3.5. Data collection method	Error! Bookmark not defined.
3.6. Types of data	Error! Bookmark not defined.
3.7. Statistical analysis procedures	Error! Bookmark not defined.
3.8. Conclusion	Error! Bookmark not defined.
4. Chapter 4: Statistical Analysis & Findings discussion	Error! Bookmark not defined.
4.1. Introduction.....	Error! Bookmark not defined.
4.2. Sample profile (descriptive statistics for research sample)	Error! Bookmark not defined.
4.3. Validity & reliability tests for the questionnaires.....	Error! Bookmark not defined.
4.4. Descriptive statistics for research variables (answer research questions).....	Error! Bookmark not defined.
4.5. Testing Hypotheses & Findings Discussion.....	Error! Bookmark not defined.
4.6. Conclusion	Error! Bookmark not defined.

5. Chapter five: Research limitations, Recommendations & Conclusion ...**Error! Bookmark not defined.**

5.1. Research Limitations & Future Research**Error! Bookmark not defined.**

5.2. Research Recommendations**Error! Bookmark not defined.**

References.....18

Appendix.....**Error! Bookmark not defined.**

1. Chapter 1: Introduction

1.1. Research Background

Since 1980, Saudi government has decided to diversity its industry by processing the oil into downstream products to score higher profit margin. To accomplish this vision, the government established Jubail industrial city. Jubail industrial city is in the eastern region of Saudi Arabia. It is located near one of the biggest oil reserves in the world. The industrial area was made ready for Chemical plants. Since 1980, chemical plants were constructed in the industrial area like Sabic chemical compounds and Sadara. The industrial area of Jubail is still expanding every year with new chemical plants projects. Construction of new chemical plants requires effective team communication for successful project delivery and adherence to timelines. Effective team communication plays a crucial role

in ensuring that all stakeholders are aligned with the project goals and timelines. Clear and open communication enables the project team to address challenges promptly, share critical information, and make informed decisions. In the context of chemical plant construction, the coordination between engineers, construction workers, safety inspectors, and project managers is essential for the successful execution of tasks and the adherence to project timelines. Furthermore, clear communication can help in the early identification of potential issues, which can prevent delays and cost overruns. Therefore, fostering a culture of effective communication among team members is imperative in ensuring the smooth progress and timely completion of chemical plant construction projects. Effective team communication is not only essential for preventing delays and cost overruns but also for ensuring the safety of the construction workers and the surrounding environment. In the context of chemical plant construction, where strict adherence to safety protocols and regulations is paramount, clear and continuous communication can significantly mitigate the risk of accidents and facilitate the swift resolution of any safety concerns that may arise.

There is a statistically significant relationship between team communication and project success. Effective team communication is not only essential for preventing delays and cost overruns but also for ensuring the safety of the construction workers and the surrounding environment. In the context of chemical plant construction, where strict adherence to safety protocols and regulations is paramount, clear and continuous communication can significantly mitigate the risk of accidents and facilitate the swift resolution of any safety concerns that may arise. Furthermore, a culture of open communication fosters a sense of accountability among team members,

encouraging them to proactively report and address safety hazards, ultimately creating a safer work environment.

Research has shown that a lack of effective communication can lead to misunderstandings, errors, and even accidents at construction sites. By contrast, projects where team communication is prioritized tend to experience reduced safety incidents and improved overall project performance. It's also worth noting that effective communication not only encompasses verbal exchanges but also written documentation, visual aids, and regular meetings to ensure that all team members are on the same page regarding project goals, plans, and safety requirements. [\(Galli, 2021\)](#) Additionally, effective communication enables better coordination and collaboration among team members [\(Tong, 2022\)](#). This promotes efficient resource allocation, reduces rework, and minimizes delays in the construction process. The impact of team communication on project timelines in chemical plant construction in Industrial Jubail City is significant.

In fact, fostering a culture of effective communication can also lead to improved employee satisfaction, as team members feel heard, valued, and supported in their roles. This, in turn, can contribute to higher productivity levels and better teamwork, positively impacting the project's timeline and outcomes. Therefore, investing in communication training and continuously reinforcing the importance of effective communication within the construction team are critical steps in ensuring the success of chemical plant construction projects in Industrial Jubail City.

Moreover, team communication goes beyond just exchanging information; it also encompasses building trust and fostering a collaborative

environment. When team members feel comfortable communicating openly and honestly with one another, they are more likely to share their expertise, raise potential issues, and collaboratively problem-solve, ultimately leading to more effective and efficient project execution. In addition, effective communication can also positively impact the quality of work and the overall project outcomes. When all stakeholders are on the same page and have a clear understanding of their roles and responsibilities, the likelihood of errors and rework is reduced, leading to improved project quality and client satisfaction.

As Industrial Jubail City continues to witness growth and development in the chemical plant construction sector, the role of team communication becomes even more critical. With increasingly complex projects and diverse teams, the ability to communicate effectively across various departments, disciplines, and hierarchical levels becomes a key determinant of project success.

1.2. Research Problem

In the context of ongoing expansion and development in Industrial Jubail City's chemical plant construction sector, what are the specific communication challenges faced by project teams, and how do these

challenges impact project timelines, safety outcomes, and overall project success?

1.2.1. Theoretical Gaps

1. Understanding Communication Dynamics in Construction

Projects: There is a gap in theoretical understanding regarding the specific communication dynamics within construction projects, especially in the context of chemical plant construction in industrial settings. Existing literature may not sufficiently address the unique challenges and requirements of communication in such complex and safety-critical environments.

2. Impact of Communication on Project Success Metrics:

Theoretical research often lacks comprehensive insights into how communication practices directly influence project timelines, safety outcomes, and overall project success in the specific context of chemical plant construction.

3. Integration of Communication Theory with Construction

Management: The intersection of communication theory and construction management practices, particularly in high-risk industrial environments, requires further exploration. Theoretical frameworks that effectively integrate communication theories with project management principles specific to chemical plant construction are limited and often random.

1.2.2. Practical Gaps

1. Identification of specific communication challenges: There is a gap in identifying and categorizing the specific communication

challenges faced by project teams in chemical plant construction. Understanding these challenges is crucial for developing targeted communication strategies.

2. **Evaluation of communication strategies:** Practical insights into which communication strategies are most effective in mitigating challenges and improving project outcomes are lacking.
3. **Implementation of Communication Best Practices:** Despite theoretical knowledge, there is often a gap between recommended communication best practices and their practical implementation in construction projects.

1.3. Research Significance

1.3.1. At the theoretical level

- **Advancement of Knowledge:** The research contributes to advancing theoretical understanding of communication dynamics in complex industrial settings, particularly within the context of chemical plant construction in Jubail City which is witnessing continuance new projects.
- **Interdisciplinary Integration:** It promotes the integration of communication theories with disciplines such as engineering, safety staff and management.
- **Development of Frameworks:** The research may lead to the development of new theoretical frameworks or the refinement of existing ones that specifically address communication challenges in industrial construction projects. These frameworks can guide future researchers and highlight the its importance.

1.3.2. At the practical level

- **Industry Impact:** Direct benefits to the chemical plant construction industry in Jubail City. Implementing research findings can improve project management practices, enhance safety protocols, and optimize resource allocation. This leads to cost savings, improved project timelines, and enhanced competitiveness in the global market.
- **Policy and Standards Development:** Practical outcomes influence the development of industry standards, policies, and guidelines related to communication practices in chemical plant construction. This includes recommendations for integrating communication technologies, establishing training programs, and promoting collaborative communication across stakeholders.
- **Implementation Strategies:** Research findings will produce actionable methods for enhancing communication effectiveness within project teams. These methods may involve the adoption of communication technologies, organizational policies, training initiatives, and procedural improvements aimed at optimizing project outcomes and stakeholder satisfaction.

1.4. Research Questions

1. What are the specific communication challenges faced by project teams in Industrial Jubail City's chemical plant construction sector?
2. How does effective team communication impact project timelines, safety outcomes, and overall project success in chemical plant construction?

3. What industry-specific policies, standards, or guidelines should be developed based on research insights to improve communication practices in chemical plant construction?
4. What are the most effective strategies for integrating communication technologies and establishing training programs that promote collaborative communication across stakeholders in chemical plant construction projects?
5. What are the barriers to implementing recommended communication best practices in chemical plant construction, and how can these barriers be overcome?

1.5. Research Objectives

- To identify and categorize specific communication challenges encountered by project teams in the chemical plant construction sector in Industrial Jubail City.
- To investigate the impact of effective team communication on project timelines, safety outcomes, and overall project success in chemical plant construction.
- To develop theoretical frameworks that comprehensively explain communication dynamics within chemical plant construction projects in Industrial Jubail City.
- To evaluate and recommend specific communication strategies that effectively mitigate challenges and improve project outcomes in chemical plant construction projects.

1.6. Research Hypotheses

- Specific communication challenges faced by project teams in the chemical plant construction sector in Industrial Jubail City significantly impact project timelines.
- Theoretical frameworks that integrate communication theories with construction management principles provide better explanatory power for communication dynamics in chemical plant construction projects.
- Communication practices significantly influence project success metrics (e.g., timelines, safety outcomes) in chemical plant construction projects.
- There are significant theoretical gaps in understanding the direct impact of communication practices on project success metrics specific to chemical plant construction.
- Addressing identified communication challenges through targeted strategies optimizes project management practices and enhances safety protocols in chemical plant construction.

1.7. Research Model

- Independent Variables:
 - Communication Dynamics: This variable encompasses the various aspects of communication within chemical plant construction projects, including communication channels, methods, frequency, clarity, and effectiveness.
- Mediating Variables:

- Safety Outcomes: Measures of safety incidents, adherence to safety protocols, and overall safety performance influenced by communication quality.
- Dependent Variables:
 - Project Success: Includes measures such as project completion within scheduled timelines, adherence to budget, and client satisfaction.

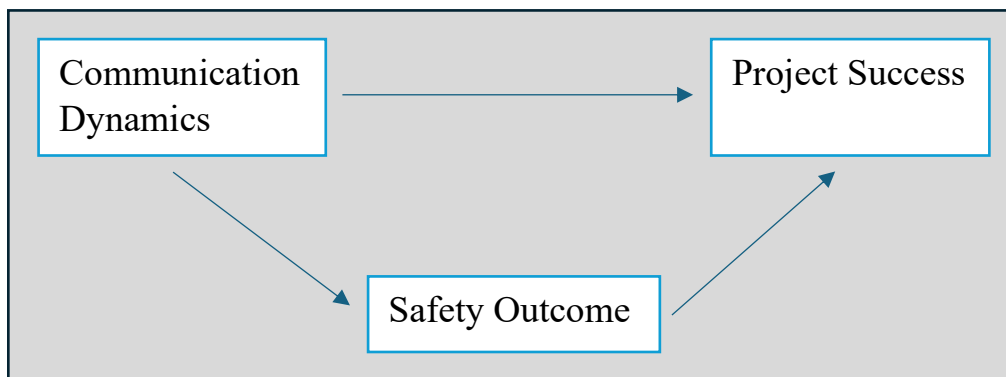


Figure 1: variables relationship chart

1.8. Scope of The Study

The study focuses on understanding communication dynamics and strategies in the context of chemical plant construction projects within Industrial Jubail City, Saudi Arabia. Surveys will be conducted, and data will be analyzed to measure the impact of communication strategies on project timelines, safety outcomes, and overall success metrics.

1.9. The Project Structure

References

1. Galli, A. (2021). Occupational health and safety in construction projects: a case study on chemical industry sector. *Journal of Construction Engineering and Management*, 147(1), Article 04020135. [https://doi.org/10.1061/\(ASCE\)CO.1943-7862.0001964](https://doi.org/10.1061/(ASCE)CO.1943-7862.0001964)
