


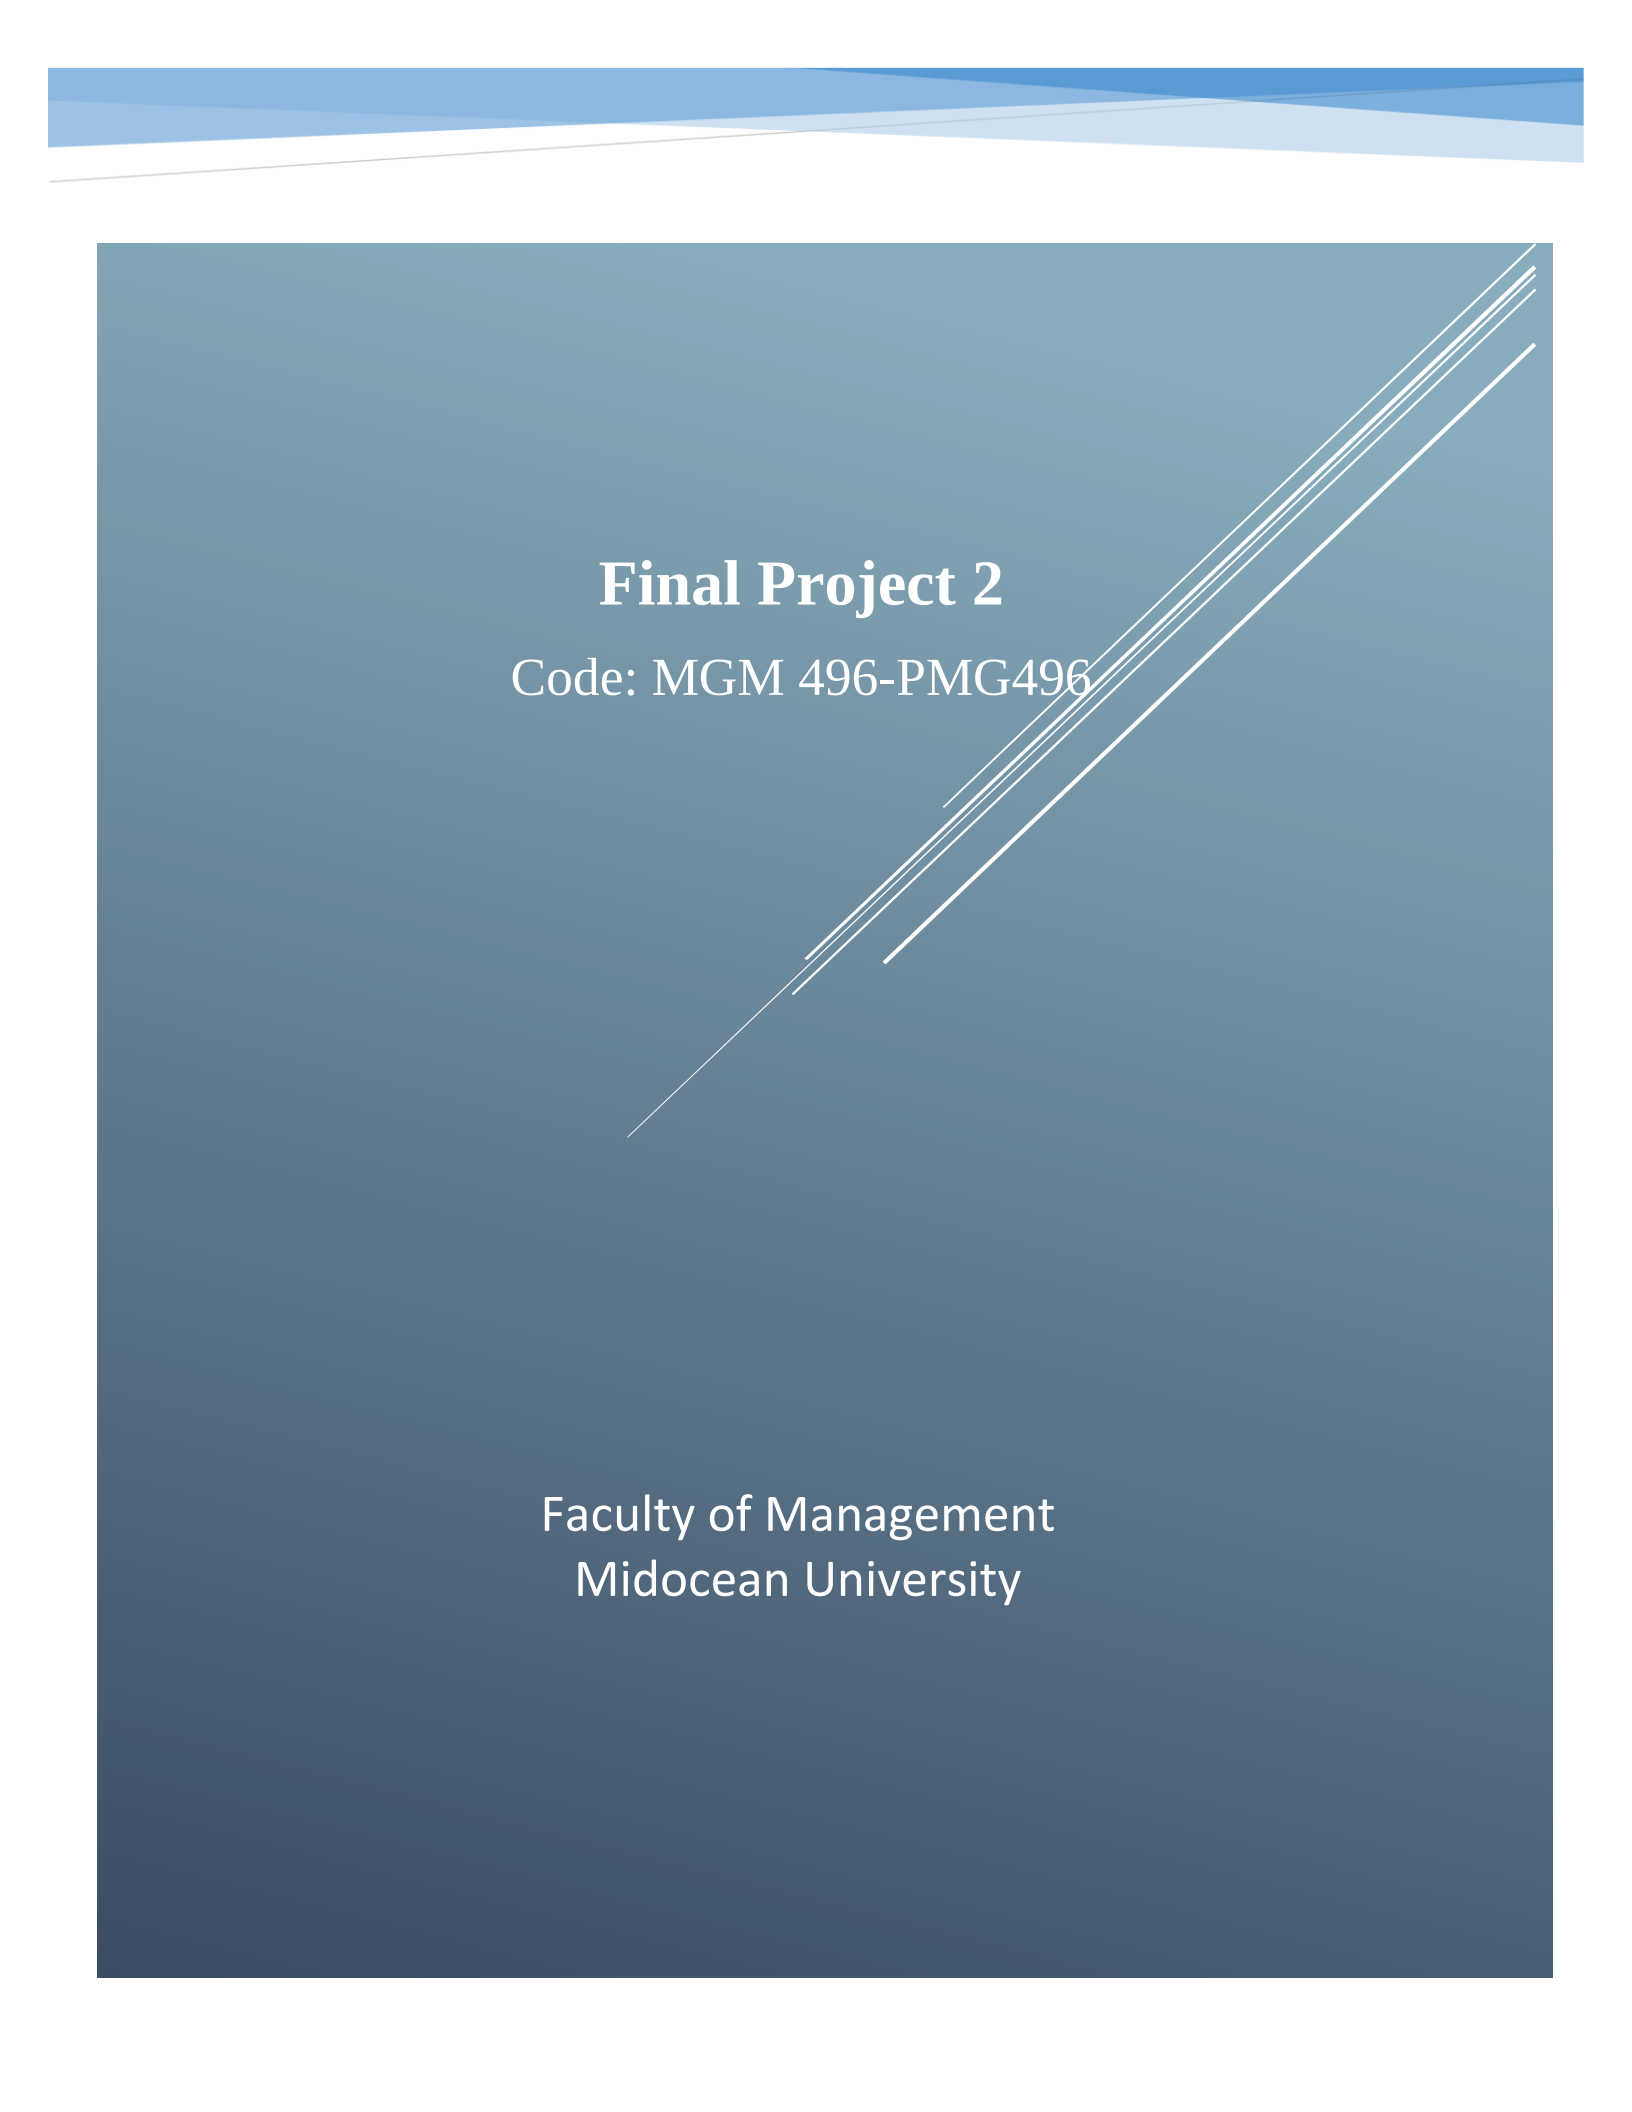

Final Project 2

Code: MGM 496-PMG496

Faculty of Management
Midocean University

Midocean University

Faculty of Management

Department/ Specialization



Project title

**Impact of Risk Management on Project Performance in Saudi Construction:
Case of Nesma & Partners Co.**

Student name

IMAN MAJZOUB

Final Project - 2

Faculty of Management - Midocean University

Supervisor

Dr. ABED ALRAHIM NADER

Faculty member- Faculty of management- Midocean University

19.06.2026 – 12 Semesters



**Impact of Risk Management on Project Performance in Saudi Construction:
Case of Nesma & Partners Co.**

Dedication

This thesis is proudly dedicated to my two beloved sons. You are my greatest source of motivation, and every milestone I achieve is to build a brighter future for us. Your patience, smiles, and presence gave me the strength to push through the long hours of study and hard work.

I also dedicate this milestone to the memory of everyone who believed in my potential, inspiring me to never stop learning, growing, and striving for excellence.

Acknowledgment

I would like to express my deepest gratitude to Midocean University for providing an exceptional academic platform that has truly shaped my professional growth.

My sincere thanks and appreciation go to my esteemed professors and instructors within the Project Management program. Your profound knowledge, invaluable guidance, and unwavering dedication to excellence have not only guided this final thesis project to completion but have also equipped me with the essential skills to succeed in the professional world.

Finally, I am incredibly grateful to my family, colleagues, and peers for their continuous support, encouragement, and understanding throughout this demanding academic journey. Thank you all for being an integral part of this achievement

ABSTRACT

Risk management is a critical governance function in construction projects, aimed at identifying and mitigating uncertainties that affect performance outcomes. This qualitative case study examines the relationship between risk management practices and project performance in the Saudi construction sector.

Secondary data and literature analysis reveal that structured risk governance improves cost control, schedule reliability, and quality outcomes. However, practical challenges such as incomplete risk identification and limited stakeholder communication reduce effectiveness.

The study contributes to project management knowledge and provides recommendations for strengthening risk governance in construction projects.

Keywords: Risk management, construction projects, qualitative case study, Saudi Arabia, project performance.

Risk management is a critical governance function in construction projects, aimed at identifying and mitigating uncertainties that affect performance outcomes. This qualitative and quantitative research examines the relationship between risk management practices and project performance in the Saudi construction sector, focusing on Nesma

& Partners Co. Structured risk governance improves cost control, schedule reliability, and quality outcomes. However, practical challenges such as incomplete risk identification and limited stakeholder communication reduce effectiveness. The study contributes to project management knowledge and provides recommendations for strengthening risk governance in line with Saudi Vision 2030.

Contents

Detailed Table of Contents	9
Chapter 1: Introduction	14
1.1 Research Background	14
1.2 Research Problem.....	15
1.3 Research Objectives.....	15
1.4 Research Questions	16
1.5 Research Significance	16
Theoretical Significance.....	16
Practical Significance	16
Chapter 2: Literature Review	17
2.1 Concept of Risk Management.....	17
2.2 Types of Construction Risks.....	17
Financial Risks	17
Operational Risks.....	18
Contractual Risks.....	18
Safety Risks.....	18
Environmental Risks	18
Table 1: Classification of Construction Risks	19
2.3 Project Performance Indicators.....	19
Figure 1: Triple Constraint Model	20
2.4 Risk Management and Performance	20
Chapter 3: Research Methodology.....	21
3.1 Research Design	21
3.2 Data Collection.....	21
3.3 Data Analysis.....	22
3.4 Ethical Considerations.....	22
Chapter 4: Case Study – Risk Governance in Saudi Construction	23
4.1 Sector Overview.....	23
4.2 Risk Governance Practices	23
Table 2: Risk Management Tools.....	24
4.3 Challenges in Governance.....	24
4.4 Case Context: Nesma & Partners.....	24

Chapter 5: Analysis and Discussion.....	26
5.1 Risk Identification and Performance.....	26
5.2 Risk Assessment and Reliability.....	26
5.3 Risk Mitigation and Quality.....	26
5.4 Discussion.....	27
Chapter 6: Risk Analysis.....	28
6.1 Risk Matrix (5×5 Probability-Impact Grid).....	28
Figure 2: Risk Prioritization Process	28
Chapter 7: Conclusion and Recommendations	29
7.1 Conclusion	29
7.2 Recommendations	29
Chapter 8: Research questionnaire & Objectives.....	29
8.1 Research Question	29
8.2. Research Objectives	31
8.3. Research Hypotheses	32
8.4. Research Model	33
8.5. Suggested Industry / Organization for the Empirical Study.....	34
8.6. Research Methodology	35
8.7. Suggested Structure of the Project.....	36
Chapter 9: Construction Introduction	39
9.1 Research Background.....	39
9.2 Research Problem.....	39
Chapter 10: Literature Review.....	40
10.1 Theoretical Foundations of Risk Management	40
2.2 Construction Risks in the Saudi Context.....	40
2.3 Project Performance and the Triple Constraint	40
Chapter 11: Research Methodology	41
12. References.....	42

Detailed Table of Contents

Chapter 1: Introduction

1.1 Research Background

1.2 Research Problem

1.3 Research Objectives

1.4 Research Questions

1.5 Research Significance

Theoretical Significance

Practical Significance

Chapter 2: Literature Review

2.1 Concept of Risk Management

2.2 Types of Construction Risks

Financial Risks

Operational Risks

Contractual Risks

Safety Risks

Environmental Risks

Table 1: Classification of Construction Risks

2.3 Project Performance Indicators

Figure 1: Triple Constraint Model

2.4 Risk Management and Performance

Chapter 3: Research Methodology

3.1 Research Design

3.2 Data Collection

3.3 Data Analysis

3.4 Ethical Considerations

Chapter 4: Case Study – Risk Governance in Saudi Construction

4.1 Sector Overview

4.2 Risk Governance Practices

Table 2: Risk Management Tools

4.3 Challenges in Governance

4.4 Case Context: Nesma & Partners

Chapter 5: Analysis and Discussion

5.1 Risk Identification and Performance

5.2 Risk Assessment and Reliability

5.3 Risk Mitigation and Quality

5.4 Discussion

Chapter 6: Risk Analysis

6.1 Risk Matrix (5×5 Probability-Impact Grid)

Figure 2: Risk Prioritization Process

Chapter 7: Conclusion and Recommendations

7.1 Conclusion

7.2 Recommendations

Chapter 8: Research questionnaire & Objectives

8.1 Research Question

8.2. Research Objectives

8.3. Research Hypotheses

8.4. Research Model

8.5. Suggested Industry / Organization for the Empirical Study

8.6. Research Methodology

8.7. Suggested Structure of the Project

Chapter 9: Introduction

9.1 Research Background

9.2 Research Problem

Chapter 10: Literature Review

10.1 Theoretical Foundations of Risk Management

10.2 Construction Risks in the Saudi Context

10.3 Project Performance and the Triple Constraint

Chapter 11: Research Methodology

12. References



Chapter 1: Introduction

1.1 Research Background

The construction industry is characterized by complexity, long project durations, and exposure to multiple risk factors. Projects require coordination among stakeholders, technical precision, and significant financial investment. These conditions increase vulnerability to:

- Cost overruns
- Schedule delays
- Quality deviations
- Safety incidents
- Contractual disputes

In Saudi Arabia, the construction sector plays a strategic role in infrastructure development and economic diversification under Vision 2030. Large-scale projects require advanced governance frameworks to ensure successful delivery.

Risk management provides a structured approach to uncertainty. It involves:

- Risk identification
- Risk assessment
- Mitigation strategies
- Continuous monitoring

Effective governance enhances decision-making and operational stability.

This study explores the impact of risk management practices on project performance in the Saudi construction sector.

1.2 Research Problem

Despite established risk frameworks, construction projects frequently experience performance challenges. Organizations document risks but may fail to translate governance into measurable outcomes.

The core research problem is:

To what extent do risk management practices influence project performance in the Saudi construction sector?

This problem reflects:

- Gaps between theory and practice
- Persistent cost and schedule deviations
- Limited empirical research in the Saudi context

Understanding this relationship supports governance improvement and operational efficiency.

1.3 Research Objectives

The objectives of this study are:

1. To examine risk management practices in construction projects

2. To analyze relationships between risk identification and performance
3. To evaluate the impact of risk assessment on schedule reliability
4. To assess the influence of risk mitigation on quality outcomes
5. To provide recommendations for governance improvement

1.4 Research Questions

1. How does risk identification influence project performance?
2. How does risk assessment affect schedule reliability?
3. How does risk mitigation improve quality outcomes?
4. What challenges hinder effective risk governance?

1.5 Research Significance

Theoretical Significance

This research contributes to project management literature by linking risk governance with performance outcomes in the Saudi construction sector.

Practical Significance

Findings provide insights for organizations to strengthen risk strategies and enhance project outcomes.

Chapter 2: Literature Review

2.1 Concept of Risk Management

Risk management is a structured process of identifying, analyzing, and responding to uncertainties. It reduces the likelihood of negative outcomes and supports decision-making.

Key components include:

- Risk identification
- Risk analysis
- Response planning
- Monitoring and control

Effective governance enhances project predictability and performance (Project Management Institute, 2021).

Chapman and Ward (2011) emphasize integration of risk strategies into project planning rather than treating them as documentation requirements.

2.2 Types of Construction Risks

Construction projects face multiple risk categories:

Financial Risks

- Inflation
- Material price volatility

- Currency fluctuations

Operational Risks

- Equipment failure
- Labor shortages
- Technical errors

Contractual Risks

- Disputes
- Scope changes
- Contract interpretation issues

Safety Risks

- Workplace accidents
- Health hazards

Environmental Risks

- Weather conditions
- Regulatory compliance

Early identification reduces project failure rates (Zou et al., 2007).

Table 1: Classification of Construction Risks

Risk Category	Description	Potential Impact
Financial	Economic fluctuations	Cost overruns
Operational	Execution challenges	Schedule delays
Contractual	Disputes and claims	Performance issues
Safety	Workplace hazards	Operational disruptions
Environmental	Regulatory constraints	Compliance risks

Source: Developed by the Researcher

2.3 Project Performance Indicators

Project performance is measured using the triple constraint model:

- Cost performance
- Time performance
- Quality performance

Balanced achievement of these dimensions defines success (Atkinson, 1999).

Figure 1: Triple Constraint Model




Figure 1: Triple constraint model of performance

Source: Project Management Literature

2.4 Risk Management and Performance

Research demonstrates positive relationships between governance and outcomes:

- Early identification reduces financial impacts
- Assessment improves decision-making
- Mitigation enhances quality

Organizations applying structured frameworks experience fewer deviations (Raz & Michael, 2001).

Chapter 3: Research Methodology

3.1 Research Design

A qualitative case study approach is adopted to explore risk governance in Saudi construction. Qualitative research provides in-depth understanding of organizational processes.

This design is appropriate because it:

- Examines real-world practices
- Provides contextual insights
- Supports theoretical exploration

3.2 Data Collection

Secondary sources include:

- Academic journals
- Industry reports
- Company documentation
- Public information

Secondary data ensures reliability and ethical compliance.

3.3 Data Analysis

Descriptive analysis interprets relationships between governance and outcomes. Themes are identified and discussed in relation to theoretical frameworks.

Qualitative analysis emphasizes:

- Pattern identification
- Contextual interpretation
- Theoretical contribution

3.4 Ethical Considerations

The study uses publicly available information only. No confidential data are included.

Chapter 4: Case Study – Risk Governance in Saudi Construction

4.1 Sector Overview

The Saudi construction sector supports infrastructure development and economic growth. Large projects require advanced governance frameworks to manage complexity.

Success depends on:

- Structured planning
- Risk governance
- Stakeholder coordination

4.2 Risk Governance Practices

Organizations apply:

- Risk registers
- Probability-impact matrices
- Mitigation strategies
- Monitoring systems

These tools enable structured evaluation and decision-making.

Table 2: Risk Management Tools

Tool	Purpose	Benefit
Risk Register	Document risks	Visibility
Probability Matrix	Assess impact	Prioritization
Mitigation Plan	Reduce impact	Performance
Monitoring	Track changes	Control

Source: Developed by the Researcher

4.3 Challenges in Governance

Common challenges include:

- Incomplete identification
- Limited communication
- Reactive strategies
- Resource constraints

Addressing these challenges improves effectiveness.

4.4 Case Context: Nesma & Partners

The company operates large-scale projects in infrastructure and industrial sectors. Governance practices support:

- Performance stability
- Decision-making
- Operational efficiency

However, practical challenges require continuous improvement.

Chapter 5: Analysis and Discussion

5.1 Risk Identification and Performance

Early identification reduces unexpected impacts. Structured processes enable organizations to:

- Detect threats
- Plan mitigation
- Improve outcomes

5.2 Risk Assessment and Reliability

Assessment improves reliability by:

- Evaluating probability
- Prioritizing risks
- Allocating resources

Structured frameworks enhance governance.

5.3 Risk Mitigation and Quality

Mitigation enhances quality through:

- Reduced rework
- Safety compliance
- Quality control

These outcomes improve success.

5.4 Discussion

Findings align with literature, confirming that governance improves performance. Challenges require continuous improvement and stakeholder engagement.

Chapter 6: Risk Analysis

6.1 Risk Matrix (5×5 Probability-Impact Grid)

Probability \ Impact Low Medium High Critical

Very Likely	M	H	C	C
Likely	L	M	H	C
Possible	L	M	H	H
Unlikely	L	L	M	H
Rare	L	L	L	M

Legend: L = Low, M = Medium, H = High, C = Critical

Source: Developed by the Researcher

Figure 2: Risk Prioritization Process

1. Identify Risk
2. Assess Probability
3. Assess Impact
4. Prioritize
5. Mitigate
6. Monitor

Figure 2: Risk prioritization process

Source: Risk Management Literature

Chapter 7: Conclusion and Recommendations

7.1 Conclusion

Risk governance significantly influences construction performance.
Structured practices enhance cost control, reliability, and quality outcomes.

7.2 Recommendations

1. Strengthen governance frameworks
2. Enhance communication
3. Implement monitoring systems
4. Integrate risk strategies
5. Provide training

Chapter 8: Research questionnaire & Objectives

8.1 Research Question

How do risk management practices influence project performance in the Saudi construction sector, specifically in Nesma & Partners Co.?

Sub-Questions:

- How does risk identification affect project cost and schedule performance?
- How does risk assessment improve schedule reliability and decision-

making?

- How do risk mitigation strategies influence quality and project success?
- What challenges limit the effectiveness of risk management in construction projects?

8.2. Research Objectives

1. To examine the risk management practices used in construction projects at Nesma & Partners Co.
2. To identify the relationship between risk identification and project performance.
3. To evaluate the effect of risk assessment on schedule reliability.
4. To analyze the influence of risk mitigation on project quality and overall success.
5. To provide recommendations to improve risk governance in Saudi construction projects.

8.3. Research Hypotheses

H1: Effective risk identification has a positive effect on project cost and schedule performance.

H2: Risk assessment has a significant positive relationship with schedule reliability.

H3: Risk mitigation strategies positively influence project quality and overall project performance.

H4: Weak communication and incomplete risk identification negatively affect project performance.

8.4. Research Model


Independent Variable: Risk Management Practices

- Risk Identification
- Risk Assessment
- Risk Mitigation

Dependent Variable: Project Performance

- Cost Performance
- Time / Schedule Performance
- Quality Performance

The model assumes that effective risk management practices positively influence project performance outcomes.

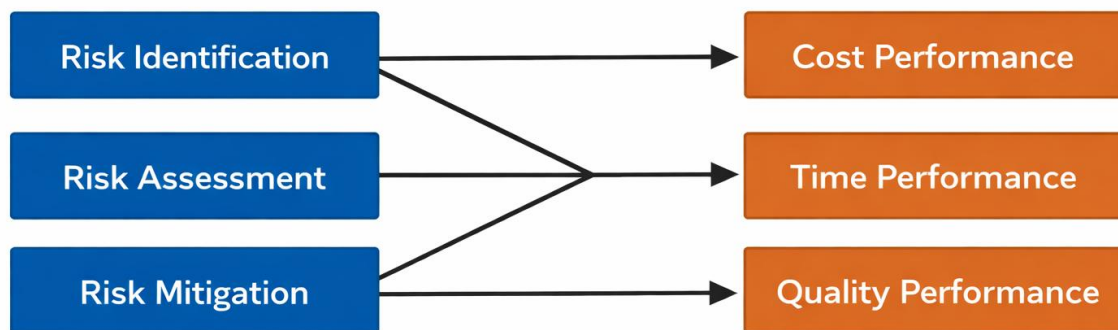

Research Model

8.5. Suggested Industry / Organization for the Empirical Study

The empirical study will focus on Nesma & Partners Co., one of the leading construction companies in Saudi Arabia. The company is involved in major infrastructure, industrial, and building projects that support Saudi Vision 2030. Because the company manages complex projects with multiple stakeholders, it provides a suitable environment for studying risk management practices. The study will investigate how the company identifies, evaluates, and mitigates risks and how these practices affect project performance.

8.6. Research Methodology

The study will adopt a quantitative research approach supported by descriptive analysis. Primary data will be collected through a questionnaire distributed to project managers, engineers, supervisors, and other employees working at Nesma & Partners Co. The questionnaire will measure the extent of risk identification, risk assessment, and risk mitigation, as well as their effect on cost, time, and quality performance.

The sample will be selected using purposive sampling because the respondents must have direct experience in construction projects. The collected data will be analyzed using statistical methods such as descriptive statistics, correlation analysis, and regression analysis to test the hypotheses.

8.7. Suggested Structure of the Project

Chapter 1: Introduction

1.1 Research Background

1.2 Research Problem

1.3 Research Objectives

1.4 Research Questions

1.5 Research Significance

Theoretical Significance

Practical Significance

Chapter 2: Literature Review

2.1 Concept of Risk Management

2.2 Types of Construction Risks

Financial Risks

Operational Risks

Contractual Risks

Safety Risks

Environmental Risks

Table 1: Classification of Construction Risks

2.3 Project Performance Indicators

Figure 1: Triple Constraint Model

2.4 Risk Management and Performance

Chapter 3: Research Methodology

3.1 Research Design

3.2 Data Collection

3.3 Data Analysis

3.4 Ethical Considerations

Chapter 4: Case Study – Risk Governance in Saudi Construction

4.1 Sector Overview

4.2 Risk Governance Practices

Table 2: Risk Management Tools

4.3 Challenges in Governance

4.4 Case Context: Nesma & Partners

Chapter 5: Analysis and Discussion

5.1 Risk Identification and Performance

5.2 Risk Assessment and Reliability

5.3 Risk Mitigation and Quality

5.4 Discussion

Chapter 6: Risk Analysis

6.1 Risk Matrix (5×5 Probability-Impact Grid)

Figure 2: Risk Prioritization Process

Chapter 7: Conclusion and Recommendations

7.1 Conclusion

7.2 Recommendations

Chapter 8: Research questionnaire & Objectives

8.1 Research Question

8.2. Research Objectives

8.3. Research Hypotheses

8.4. Research Model

8.5. Suggested Industry / Organization for the Empirical Study

8.6. Research Methodology

8.7. Suggested Structure of the Project

Chapter 9: Introduction

9.1 Research Background

9.2 Research Problem

Chapter 10: Literature Review

10.1 Theoretical Foundations of Risk Management

10.2 Construction Risks in the Saudi Context

10.3 Project Performance and the Triple Constraint

Chapter 11: Research Methodology

Chapter 9: Construction Introduction

9.1 Research Background

The construction industry is globally recognized for its complexity, high capital requirements, and long-term project lifecycles. In the Kingdom of Saudi Arabia, the sector is undergoing a monumental transformation driven by Vision 2030. Major infrastructure projects, known as 'Giga-projects,' require a level of risk governance that transcends traditional project management.

9.2 Research Problem

Despite the existence of sophisticated risk management frameworks, many construction projects in the region continue to face significant cost overruns and delays. The core research problem is: To what extent do risk management practices influence project performance in the Saudi construction sector?

Chapter 10: Literature Review

10.1 Theoretical Foundations of Risk Management

Risk management is defined as a structured process of identifying, analyzing, and responding to project uncertainties. Modern project management theory views risk through the lens of 'Uncertainty Management.' According to the Project Management Institute (2021), a robust governance framework includes identification, analysis, response planning, and continuous monitoring.

2.2 Construction Risks in the Saudi Context

The Saudi Arabian construction market is unique due to its rapid scaling. Risks in this region include Macro-Economic Risks (oil price fluctuations), Supply Chain Volatility (material price increases), and Regulatory Risks (Saudization requirements). For a company like Nesma & Partners, managing these risks requires a sophisticated governance framework.

2.3 Project Performance and the Triple Constraint

Project performance is measured using the triple constraint model: Cost, Time, and Quality performance. Balanced achievement of these dimensions defines success. In Saudi construction, schedule reliability (Time) is often the most scrutinized metric due to the strict deadlines of national development goals.

Chapter 11: Research Methodology

This study adopts a mixed-methods approach, utilizing a qualitative case study of Nesma & Partners combined with a quantitative survey. Primary data is collected through a questionnaire distributed to project managers and engineers. The collected data is analyzed using statistical methods such as descriptive statistics and correlation analysis to test the hypotheses.

12. References

Atkinson, R. (1999). Project management: cost, time and quality.

Chapman, C., & Ward, S. (2011). How to Manage Project Opportunity and Risk.

Project Management Institute. (2021). PMBOK Guide.

Raz, T., & Michael, E. (2001). Project risk management tools.

Zou, P., Zhang, G., & Wang, J. (2007). Key risks in construction projects.

Atkinson, R. (1999). Project management: Cost, time and quality, two best guesses and a phenomenon. *International Journal of Project Management*, 17(6), 337–342.

Chapman, C., & Ward, S. (2011). How to Manage Project Opportunity and Risk: Why Uncertainty Management Can Be a Much Better Approach than Risk Management. Wiley.

Hair, J. F., Black, W. C., Babin, B. J., & Anderson, R. E. (2019). *Multivariate Data Analysis* (8th ed.). Cengage.

Project Management Institute. (2021). A Guide to the Project Management Body of Knowledge (PMBOK Guide) (7th ed.). PMI.

Raz, T., & Michael, E. (2001). Use and benefits of tools for project risk management. *International Journal of Project Management*, 19(1), 9–17.

Saunders, M., Lewis, P., & Thornhill, A. (2019). *Research Methods for Business Students* (8th ed.). Pearson.

Zou, P. X. W., Zhang, G., & Wang, J. (2007). Understanding the key risks in construction projects in China. *International Journal of Project Management*, 25(6), 601–614.
