



جامعة الجميع الذكية
EVERYONE'S SMART UNIVERSITY

Everyone's Smart University

Project (Spring 2021)

Student Name	Sultan alharbi	اسم الطالب
Students I.D	2021202213	الرقم الجامعي

Section

Master

Date

Thursday

18 / 03 / 2021.

Course Code

(PMG510)

Project Risk Management

Instructions:

- اخر موعد للتسليم هو يوم السبت 2021-05-08 في تمام الساعة ٩ مساءً.
- الإجابة متاحة باللغة الإنجليزية أو اللغة العربية مع مراعاة أن تكون المصطلحات العلمية باللغة الانجليزية.
- يتم تسليم المشروع في صيغة ملف pdf مع الالتزام نموذج الجامعة ولن تقبل أي مستندات أخرى.
- يجب مراعاة أقسام البحث الرئيسية (مقدمة Introduction، دراسات علمية سابقة Literature Review، طريقة البحث Methodology، النتائج والمناقشة Results and Discussion، وأخيراً المراجع References . وان كان هناك ملحقات Appendices يتم إضافتها)
- يجب الالتزام بـ Theme موحد كما يلي:
- حجم الخط 12.
- نوع الخط Arial.
- لون الخط أسود.
- المسافة بين الأسطر line spacing 1.5
- عدد صفحات البحث (لا يقل عن ثلاث صفحات ولا يزيد عن ست صفحات).

Instructor's Name: Eng. Mosaab M. Hamed

Project:

Risk Identification and Analysis (Based on the project you chose in APM)

The objective of this report is to identify project risks, prepare a risk probability matrix, and carry out an analysis of selected risks. Referring to the project you select in **Advanced projects management APM course**, your task is to prepare a risk management plan that identifies potential risks in **the selected stage of the project** and identify risk management strategies.

From the course content and readings, you know that the overall purpose of risk planning is to anticipate possible risk events and be ready to take appropriate action when risk events occur—to eliminate or reduce negative impacts on the project.

You may wish to begin this exercise with a brainstorming about potential risks to get candidate risks “on the table” for consideration. And then identify and refine that wording for risks that have some realistic chance of occurring in this stage. For example, potential weather problems present a real obstacle to completing field data collection by the planned completion date. It is also an issue that the project manager will ultimately have to plan for, as opposed to other issues such as a major disaster (e.g., your office burning down), is not a high-enough probability event that requires much time in planning. As described below, you will select several of the identified risks and carry out a risk analysis.

You will use the distilled list of risks to make a risk probability/impact matrix. The matrix will have at least three categories (high/medium/low) for probability and impact.

Remember that it is important to name risks effectively—use words that describe the risk event and point to the impact on the project (e.g., “injury of field technician disrupts data installation work”).

After completion of the risk matrix, document a risk analysis for the selected risks. This detailed documentation for that selected risk will include:

- a description of the risk and potential impacts (schedule, quality of work, cost, etc.) on the project.
- indicators or triggers that would be monitored to help identify the risk as early as possible.
- specific risk response strategies to take.

Using probability and impact matrix calculate the **Expected Monetary Value (EMV)** for all risks that have the impact in terms of cost \$\$.

Best of luck...

المشروع:

التعرف على المخاطر وتحليلها (بحث مبني على مشروعك الذي اخترته في مادة ادارة المشاريع المتقدمة)

الغرض من هذا التقرير هو التعرف على المخاطر المحيطة بالمرحلة التي تختارها المرحلة من مراحل مشروعك (نفس المرحلة التي اخترت التطرق لها في مشروعك لمادة إدارة المشاريع المتقدمة Advanced project management) حيث أن مهمتك هي تحضير خطة متكاملة لإدارة المخاطر تشمل التعريف بالمخاطر المحتملة التي تحيط بتلك المرحلة وتحضير مصفوفة احتمالية المخاطر ومن ثم القيام بالتحليل لهذه المخاطر المختارة وتحديد استراتيجيات ادارة المخاطر المناسبة لكل خطر على حدة.

من محتويات المقرر والمصادر الأخرى المتاحة أصبحت تعلم الآن أن الغرض العام لمرحلة التخطيط للمخاطر هي توقع أحداث المخاطر المحتملة والتجهز لاتخاذ ردة الفعل المناسبة عند وقوع الخطر – لمنع أو تقليل الآثار السلبية على المشروع.

قد تحبذ بداية هذا البحث بعصف ذهني عن ماهية المخاطر التي قد تحيط بتلك المرحلة من مراحل مشروعك, وذلك للحصول على قائمة بتلك المخاطر. ومن ثم تحديد وتصفية هذه القائمة للوصول إلى قائمة مختصرة بالمخاطر التي لها فرصة واقعية أكبر في الحدوث. على سبيل المثال: المشاكل الجوية المتوقعة والتي تمثل عقبة حقيقية أمام اكتمال جمع البيانات من المواقع في أو قبل الوقت المحدد، هذه تعتبر مشكلة على مدير المشاريع أن يضعها في الحسبان. من ناحية أخرى، فإن المخاطر غير الواقعية مثل الكوارث الطبيعية والأعاصير (تلك التي تسبب حريقاً بمكتبك وفقدان الأوراق المهمة) ليست لها احتمالية وقوع عالية وبالتالي لاتستدعي تضيق الكثير من الوقت في التخطيط لها. كما سيتبين لك، ستقوم باختيار عدة مخاطر من تلك التي قمت بالتعرف عليها لتحليلها.

ستقوم باستخدام هذه القائمة المختصرة لعمل مصفوفة المخاطر (الاحتمالية/الأثر). المصفوفة ستحتوي على الأقل على ثلاث تصنيفات (عالي/متوسط/منخفض) للإحتمالية والأثر.

لاتنس استخدام أسماء تصف طبيعة المخاطر بصورة فعالة – قم باستخدام كلمات تصف الحادثة الخطرة وتشير الى أثرها على المشروع (مثل: إصابة أحد الفنيين في الموقع مما يؤثر على أعمال التركيب).

بعد انتهاءك من مصفوفة المخاطر، قم بتوثيق تحليلك للمخاطر المختارة. هذا التسجيل المفصل للمخاطر يجب أن يتضمن:

- وصف للخطر واثاره المحتملة (الجدولة، جودة العمل، التكلفة، الخ)
- المؤشرات والمحفزات التي يجب مراقبتها للمساعدة في التعرف على هذا الخطر قبل وقوعه
- تفصيل للاستجابة المقترحة للتصدي لهذا الخطر

باستخدام مصفوفة الاحتمالات والتأثير ، احسب **القيمة النقدية المتوقعة (EMV)** لجميع المخاطر التي لها تأثير من حيث التكلفة \$\$.

مع تمنياتي بالتوفيق..

Home renovation


Introduction:

In this project I will talk about my home renovation, and I am going to confining all risks that might face me during this journey by identifying the project risks, prepare a risk probability impact matrix, risks response .

methodology:

the process that will applied in this project 8Rs and 4Ts (figure1), to have a clear idea what is will be the risks and how can we identify and with each of them

figure1

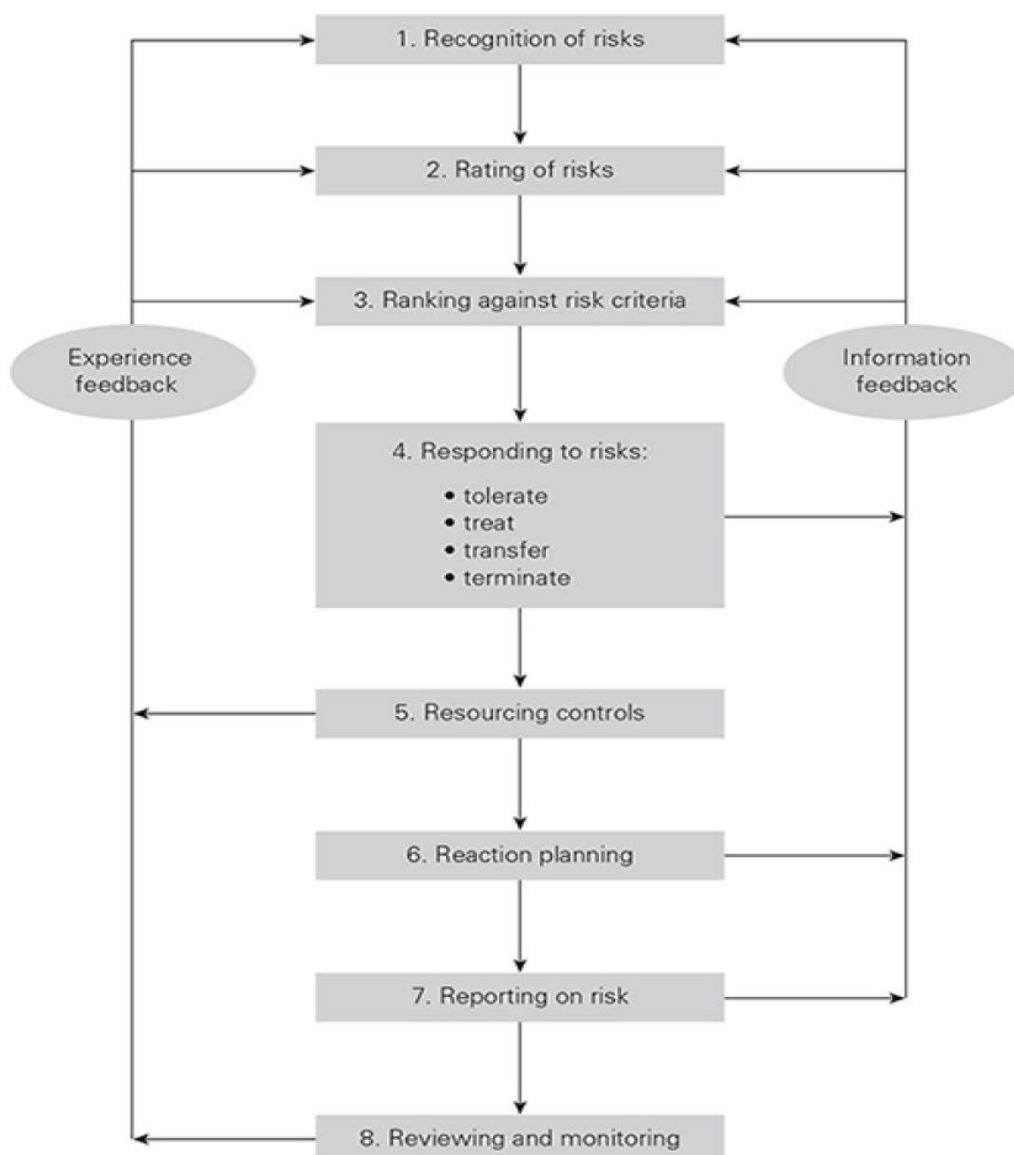

Firstly, we need to identify the risk as shown in the table below :

Table1

#	Risk
1	Unqualified labors (lack of training)
2	Delay kitchen machines (the machines imported from Italy)
3	Increase in the materials price (world economic crisis)
4	Rework (scope changing)
5	work permit (update from Ministry of Municipal, Rural Affairs and Housing)

After aggregation, the potential risk in consolidated risk, the next step is to have analysis by risk matrix below to determine the likelihood and potential consequences of the risk where is the low = 0 to 0.29 , medium = 0.3 to 0.69, and high = 0.7 to 1

Figur 3

Probability	0.7-1	high	high	medium
	0.3-0.69	high	medium	low
	0-0.29	medium	low	low
		0.7-1	0.3-0.69	0-0.29
		Impact		

Table 2

#	Risk	Probability	Impact
1	Unqualified labors (lack of training)	0.3	0.3
2	Delay kitchen machines (the machines imported from Italy)	0.8	0.4
3	Increase in the materials price (world economic crisis)	0.4	0.8
4	Rework (scope changing)	0.4	0.8
5	work permit (update from Ministry of Municipal, Rural Affairs and Housing)	0.4	0.2

Table 3

#	Risk	Probability	Impact	Severity	Response plan	Mitigate Action
1	Unqualified labors (lack of training)	0.3	0.3	Medium	Sing a contract with manpower company	Provide and search for a qualified resource
2	Delay kitchen machines (the machines imported from Italy)	0.8	0.4	High	Re-plan the project schedule	Have a clear info when the devises will arrive to the project site in signed contract
3	Increase in the materials price (world economic crisis)	0.4	0.8	High	contingency budget	Clear scope of quantities work will give a clear budget
4	Rework (scope changing)	0.4	0.8	High	contingency plan (time-budget)	A clear scope must be included in the contract
5	work permit (update from Ministry of Municipal, Rural Affairs and Housing)	0.4	0.2	low	Update the work permit	Have all the updated permits before the work start

Result :

after applying EVM to list of potential risk of the home renovation project , the results shows that the cost of impact is 14500 SAR , and the contingency budget will be 7500 SAR.

#	Risk	Probability	Impact cost SR	Risk contingency
1	Unqualified labors (lack of training)	0.3	3000	900
2	Delay kitchen machines (the machines imported from Italy)	0.8	5000	4000
3	Increase in the materials price (world economic crisis)	0.4	1000	400
4	Rework (scope changing)	0.4	5000	2000
5	work permit (update from Ministry of Municipal, Rural Affairs and Housing)	0.4	500	200
	total		14500	7500

Discussion :

Table 3 shows that there are three high risks must be monitored during the project life cycle , without neglecting other risks to have successful project in the end of journey .

Regarding table 4 it is also clear that is the most impact cost risk is machines delay and rework due to changing in the scope this is most important and have the higher cost .impact to drain the budget.

Refrece :

