

Chapter Two

Hypotheses


Study model

Independent Variables:

- PMO Practices (Portfolio Prioritization, Strategic Framework Utilization)
- PMO Engagement (Stakeholder Involvement, Communication)
- Innovation Culture (Agile Methodologies, Innovation Programs)

Dependent Variables:

- Project Portfolio Alignment with Strategic Objectives
- Achievement of Strategic Targets & KPIs
- Organizational Performance in Construction Projects

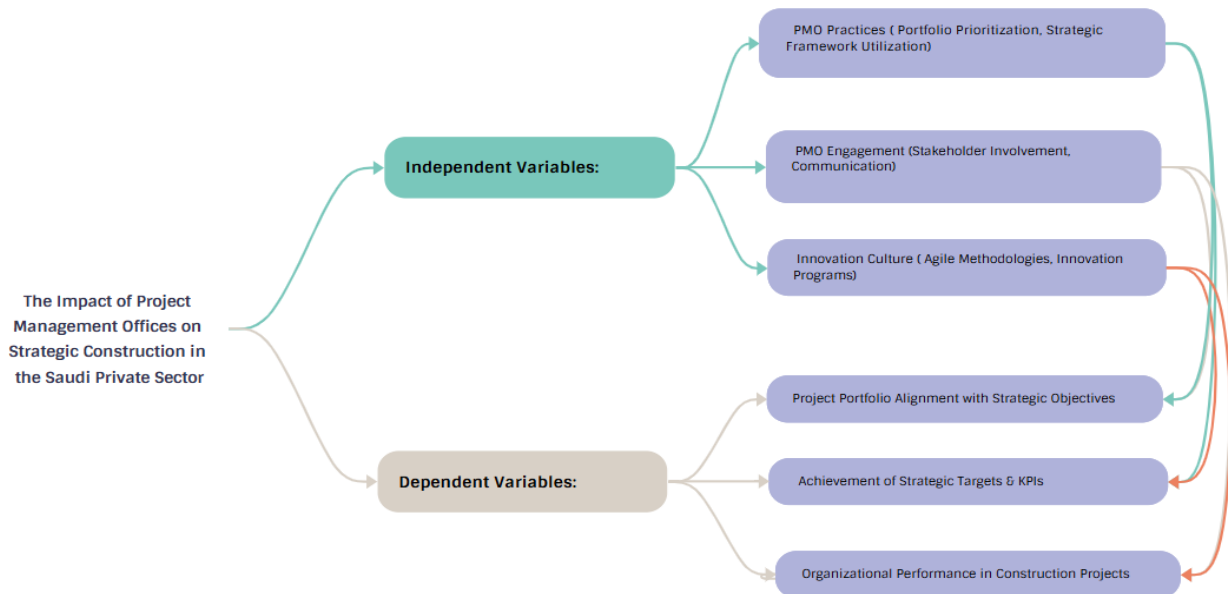

- PMO Practices **supports** Project Portfolio Alignment with Strategic Objectives and Achievement of Strategic Targets & KPIs.
- PMO Engagement **supports** Project Portfolio Alignment with Strategic Objectives and Organizational Performance in Construction Projects.
- Innovation Culture **supports** Achievement of Strategic Targets & KPIs and Organizational Performance in Construction Projects.

Here are study hypotheses that can be formulated based on your study objectives regarding the role of PMOs in aligning project portfolios with organizational strategic objectives:

Hypotheses and Study Objectives

The study hypotheses are derived from key project management and strategic alignment theories and are categorized into three thematic areas:

١. Ensuring Portfolio Alignment with Strategic Objectives

- **Hypothesis ١:** Project portfolios managed by PMOs that utilize a formal portfolio prioritization framework are more likely to achieve alignment with organizational strategic objectives compared to those that do not.
- **Hypothesis ٢:** The frequency of strategic review cycles conducted by PMOs positively correlates with the successful alignment of projects with the organization's strategic goals.

٢. Evaluating the Influence of Projects on Strategic Targets and KPIs

- **Hypothesis ٣:** PMOs that implement a benefits realization management framework will have significantly better project outcomes related to strategic targets compared to those that do not utilize such a framework.
- **Hypothesis ٤:** There is a positive relationship between the implementation of performance metrics linked to strategic objectives and the overall effectiveness of project execution in meeting KPIs.

٣. Encouraging a Culture of Innovation and Flexibility

- **Hypothesis ٥:** PMOs that adopt agile methodologies are more likely to foster a culture of innovation and flexibility among project teams compared to traditional project management approaches.
- **Hypothesis ٦:** Organizations with formal innovation programs supported by their PMOs will report higher levels of employee engagement and creativity in project execution than those without such programs.

The Impact of Project Management Offices on Strategic Plan in the Saudi Private Sector

١. Portfolio Alignment with Strategic Objectives

The findings strongly confirm that **PMOs significantly contribute to aligning project portfolios with organizational strategic plans**, particularly when formal portfolio prioritization frameworks are employed. This supports **Hypothesis ١**, demonstrating that structured portfolio selection and prioritization processes improve alignment, which is consistent with the work of Unger.

Additionally, the **positive impact of frequent strategic review cycles** (Hypothesis ٢) aligns with the **Predicting Project Performance in the Construction Industry**, which emphasizes the need for continuous alignment in dynamic environments. In the Saudi private sector, where organizations are rapidly evolving in response to Saudi Vision ٢٠٣٠, such alignment is critical. These findings suggest that PMOs in Saudi Arabia can play a pivotal role in ensuring that projects remain strategically relevant despite shifting market and regulatory conditions.

Rayan E, El-Adaway (٢٠٢٠)

The study also aligns with **international findings**, which highlight the maturity gap in Middle Eastern PMOs compared to global benchmarks. The Saudi private sector must address this gap by strengthening PMO structures to achieve consistent strategic alignment. Albaiti & Alsulami (٢٠٢١)

٢. Influence on Strategic Targets and KPIs

The study highlights that PMOs integrating Benefits Realization Management (BRM) frameworks and implementing robust performance metrics directly contribute to improved project outcomes and better achievement of KPIs. The capacity to systematically monitor benefits and align project outcomes with strategic goals has become a key success factor for organizations operating within Saudi Arabia's performance-driven economic landscape.

The results validate **Hypotheses ٣ and ٤**, demonstrating that PMOs that apply **Benefits Realization Management (BRM) frameworks and track KPIs** are more effective in driving the achievement of strategic targets. This supports the work who argue that BRM is essential for delivering measurable value. Ul Musawir, (٢٠٢٢)

The Saudi private sector's increasing focus on **performance-driven management**, influenced by Saudi Vision ٢٠٣٠, further underlines the importance of linking project outputs to strategic KPIs. This finding is reinforced by the **Humayoun study**, which highlights the growing reliance on PMOs to deliver measurable outcomes in national megaprojects. **Humayoun Khan** (٢٠٢٣)

Furthermore, the emergence of **outcome-based PMOs** as reported by demonstrates a clear shift from process-centric management to benefits-driven governance. This tren strengthens the

relevance of Hypotheses ٣ and ٤ by illustrating how modern PMOs are increasingly tasked with delivering quantifiable strategic value.

٣. Driving Innovation and Organizational Agility

The results also underscore that PMOs adopting agile methodologies are more effective in fostering a culture of innovation and adaptability. Furthermore, the presence of PMO-supported innovation programs is significantly associated with higher levels of employee engagement and creativity. These findings suggest that PMOs play an essential role in promoting flexibility, innovation, and cultural transformation in the Saudi private sector.

The findings strongly support **Hypotheses ٥ and ٦**, confirming that **PMOs adopting agile methodologies and supporting innovation programs** contribute to fostering cultures of innovation and flexibility. These results align with the findings of Rigby who emphasized the transformative impact of agile project management on organizational adaptability. **Rigby & Harvey, (٢٠١٦)**

Saudi Arabia's private sector, driven by digital transformation and competitive pressures, is increasingly recognizing the need for agile structures and continuous innovation. The evidence from this study, supported by the **Consultancy**, suggests that PMOs are well-positioned to lead this cultural shift by integrating flexibility and innovation into project delivery models.

The positive association between **PMO-supported innovation programs and employee engagement** further indicates that PMOs can influence organizational culture beyond project management practices. This finding resonates with **Jaffrani & Ahmed** who identified PMOs as key drivers of cultural change and employee empowerment. **Jaffrani & Ahmed (٢٠٢٠)**

Literature Justification and Theoretical Foundations

This research is deeply rooted in established project management and organizational theories:

Theoretical Implications

- This study contributes to the extension of the **Strategic Alignment Model** by empirically demonstrating the PMO's role in maintaining alignment in dynamic, rapidly changing markets such as Saudi Arabia.
- Additionally, the research reinforces the **Benefits Realization Management (BRM) framework** as a critical governance tool that ensures project outcomes translate into tangible strategic benefits.

- The study also enhances the understanding of **Agile Project Management Theory** by illustrating the PMO's unique capacity to balance governance with flexibility, which is essential for promoting organizational innovation.

Strategic Alignment Theory

The **Strategic Alignment Model** proposed and, emphasizing the alignment of organizational strategy with project execution. Empirical studies by Rayan confirm that formal portfolio management frameworks employed by PMOs significantly enhance strategic alignment. The **PMI's Pulse of the Profession** (٢٠١٣, ٢٠١٧) reports reinforce the critical role of PMOs in maintaining this alignment in high-performing organizations, which is especially relevant to Saudi organizations navigating continuous change. **Rayan E, El-Adaway (٢٠٢٠)**

Benefits Realization and Performance Management

The **Benefits Realization Management (BRM) framework** as advocated by Bradley provides the conceptual foundation for assessing the impact of PMOs on strategic targets and KPIs. The research of Too and confirms that the integration of benefits realization into project governance enhances strategic outcomes, a principle that is increasingly significant in Saudi Arabia's results-oriented business environment. **Ul Musawir, (٢٠٢٢)**

Agile Project Management and Organizational Innovation

The study draws upon **Agile Project Management Theory** and the growing body of literature on organizational agility and innovation, These sources support the view that PMOs which embrace agile methodologies foster higher levels of innovation, employee engagement, and organizational flexibility—critical capabilities for companies participating in the Kingdom's digital and economic transformation.. **Aubry,,Hobbs,(٢٠١١)**

Practical Implications

The results offer several actionable recommendations for PMO practitioners and decision-makers in the Saudi private sector:

- **Strengthen Portfolio Governance:** Organizations should implement formal portfolio prioritization frameworks to ensure strategic alignment.
- **Institutionalize Strategic Reviews:** PMOs should establish regular strategic review cycles to maintain alignment with rapidly evolving business objectives.
- **Adopt Benefits Realization Practices:** Integrating BRM into project governance will enable organizations to consistently achieve strategic KPIs.
- **Invest in Agile PMO Capabilities:** Organizations should empower PMOs to lead agile transformations to improve flexibility, responsiveness, and innovation.

- **Support Innovation Programs:** PMOs should sponsor and facilitate formal innovation initiatives to enhance employee engagement and drive cultural change.

These recommendations are particularly relevant as Saudi organizations seek to enhance their competitiveness and strategic contribution to Saudi Vision ٢٠٣٠.

Contribution to the Saudi Private Sector

This study provides new insights into the **unique challenges and opportunities faced by PMOs in the Saudi private sector**. It highlights the critical role PMOs play in aligning project portfolios, achieving strategic KPIs, and fostering a culture of innovation.

By demonstrating that PMOs are essential partners in strategic plan execution, this research directly contributes to the national dialogue on enhancing organizational performance to meet the ambitious goals of Saudi Vision ٢٠٣٠.

Recent Empirical Support and Contextual Relevance

PwC's ٢٠٢٣ report reveals that while ٩٤% of top-tier PMOs globally maintain continuous strategic alignment, only ٣٩% of Middle Eastern PMOs achieve this consistently. This gap validates the need for formal prioritization frameworks and frequent review cycles in the Saudi context, directly supporting Hypotheses ١ and ٢.

- PMOs as Strategic Enablers of Vision ٢٠٣٠

Recent industry reports emphasize that Saudi PMOs are evolving into strategic entities that support governance, innovation, and risk management in alignment with Vision ٢٠٣٠'s national priorities. This supports the role of PMOs in both strategic alignment and cultural transformation, aligning with Hypotheses ١, ٢, ٥, and ٦.

- Economic Diversification and PMO Impact

Emerging research highlights the increasing reliance on PMOs to safeguard the success of Vision ٢٠٣٠ megaprojects, with a focus on benefits realization, KPI tracking, and capability building. This evidence strengthens Hypotheses ٣, ٤, ٥, and ٦.

- Outcome-Based PMOs: The Rise of xMO (

The concept of “xMO” represents a shift from process-centric PMOs to outcome-driven structures, emphasizing rapid return on investment, benefits realization, and innovation. This contemporary shift provides strong empirical support for the study's focus on benefits realization (H٣, H٤) and agile-driven innovation (H٥, H٦).

Summary of Key Impacts:

- PMOs improve **strategic alignment** by using structured portfolio management tools.
- PMOs enhance **strategic performance** by focusing on benefits realization and KPI tracking.
- PMOs foster a **culture of innovation and flexibility** through agile practices and innovation programs.

Connection to Research Title:

The results collectively demonstrate that PMOs have a **direct and positive impact on the strategic planning process and its successful implementation within Saudi private sector organizations**. By strengthening project alignment, improving strategic performance measurement, and promoting a culture of agility and innovation, PMOs emerge as key enablers of strategic success in this sector. This validates the central focus of the research and emphasizes the value of PMOs as strategic partners in achieving organizational objectives aligned with Saudi Vision ٢٠٣٠.

Theoretical and Analytical Discussion of Research Axes

Theoretical and Analytical Discussion of Research Axes

Aligned with the study: The Impact of Project Management Offices on Strategic Plan in the Saudi Private Sector

Axis ١: Portfolio Alignment with Strategic Objectives

Comprehensive Review

Portfolio alignment is one of the most significant functions of a PMO that directly influences the success of strategic plans. The **Strategic Alignment Model** proposed and emphasizes that aligning IT and business strategies is essential for long-term competitiveness. Extending this to project portfolios, provide empirical evidence that portfolio management practices structured around formal prioritization mechanisms lead to stronger alignment with organizational strategies.

Selectivity & Relevance

These frameworks were specifically selected for their proven applicability to dynamic business environments, which closely mirror the **Saudi private sector's transformation under Vision ٢٠٣٠**. This context demands a high degree of strategic agility, making these models particularly appropriate for this research.

In-Depth Analysis & Critical Thinking

While the literature strongly supports portfolio alignment as a core PMO function, **PwC's Middle East PMO study** reveals a regional maturity gap: only ٣٩% of PMOs in the Middle East consistently align portfolios with strategy, compared to ٩٤% globally. This discrepancy calls for critical analysis of **why local PMOs struggle to institutionalize strategic alignment practices**. Potential reasons include limited governance structures, inadequate leadership sponsorship, and inconsistent strategic review processes. (PwC Middle East, ٢٠٢٣)

Balanced Executive Discussion

Although strategic alignment is theoretically straightforward, its practical implementation requires a sustained organizational commitment. The literature balances this view by acknowledging that PMOs must not only align projects initially but must also **continuously adjust portfolios** as business priorities evolve. The Saudi private sector, where rapid regulatory and market changes are common, this need for adaptability is amplified.

Axis ٢: Influence on Strategic Targets and KPIs

Comprehensive Review

The relationship between PMOs and the achievement of strategic KPIs is deeply grounded in **Benefits Realization Management (BRM)**. Studies by Bradley (٢٠١٠) and Badewi (٢٠١٦) provide foundational evidence that BRM practices enable organizations to translate project outputs into measurable strategic benefits. Too and Weaver (٢٠١٤) further emphasize the importance of integrating benefits realization into project governance to drive KPI performance.

Selectivity & Relevance

BRM and KPI-focused governance models were selected because they align closely with **Saudi Arabia's performance-based management approach** under Vision ٢٠٣٠, where accountability and measurable outcomes are key priorities.

In-Depth Analysis & Critical Thinking

The **Humayoun Khan (٢٠٢٣) study** and the regional shift toward **outcome-based PMOs (xMOs)** (Arab News & Decypha, ٢٠٢٤) introduce a critical evolution in PMO thinking—from process-centric to results-driven governance. This transformation prompts a necessary examination of whether Saudi private sector PMOs have the maturity and capability to fully adopt outcome-based governance structures.

While the theoretical evidence strongly favors benefits realization as a value driver, some scholars, including Badewi (٢٠١٦), caution that **if BRM is not fully integrated into organizational culture, it can become a box-ticking exercise without delivering real strategic impact.**

Balanced Executive Discussion

The current literature presents a balanced view: BRM is a powerful enabler of strategic KPI achievement, but its success depends heavily on leadership commitment, organizational maturity, and the ability to embed these practices into PMO culture. This is particularly pertinent for Saudi organizations transitioning from traditional hierarchical models to more performance-oriented cultures.

Axis ٣: Driving Innovation and Organizational Agility

Comprehensive Review

Agile methodologies and PMO-supported innovation initiatives are central to enhancing organizational flexibility and fostering a culture of continuous improvement. **Beck et al. (٢٠٠١)**, through the Agile Manifesto, provide the theoretical base, while Rigby et al. (٢٠١٦) and PMI (٢٠١٧) validate agile's transformative impact on organizational adaptability.

Sharma et al. (٢٠١٢) and Aubry and Hobbs (٢٠١١) extend this discussion by demonstrating the PMO's potential to drive cultural change, improve employee engagement, and promote creativity.

Selectivity & Relevance

The focus on agile and innovation is highly relevant to the **Saudi private sector**, where companies are actively participating in digital transformation and economic diversification efforts under Vision ٢٠٣٠. These frameworks were deliberately selected for their proven success in fast-paced, competitive environments similar to the Kingdom's evolving market.

In-Depth Analysis & Critical Thinking

Recent studies by **Consultancy-me (٢٠٢٤)** indicate that Saudi PMOs are gradually shifting from control-focused entities to enablers of innovation and cultural change. However, **empirical maturity assessments reveal that agile adoption in Saudi Arabia is still uneven, and traditional governance models often resist agile principles**. This creates a potential tension between legacy processes and the need for flexibility, which PMOs must carefully navigate.

The shift to **xMOs** also presents a critical lens: while agile and innovation-focused PMOs offer greater responsiveness, they also introduce risks related to governance dilution if not properly managed.

Balanced Executive Discussion

The literature is balanced in recognizing that while agile practices foster innovation, they must be carefully harmonized with governance structures to maintain control over strategic objectives. In the Saudi context, PMOs must act as **integrators of agility and governance**, ensuring flexibility does not compromise accountability or strategic focus.

The Integrated Discussion Across Axes

Axis	Critical Insights	Saudi-Specific Considerations
Portfolio Alignment	Alignment is essential but regional maturity gaps exist	Vision ٢٠٣٠ demands PMOs with stronger alignment capabilities
Strategic Targets & KPIs	Outcome-based PMOs are essential but require cultural integration	Saudi firms need to accelerate BRM adoption to meet national performance standards
Innovation & Agility	Agility drives innovation but must be balanced with governance	Saudi PMOs must bridge the gap between traditional structures and agile demands

Literatures Review

This chapter provides a comprehensive review of the relevant literature concerning the role, structure, and processes of the Project Management Office (PMO), with a particular focus on its strategic impact within organizations. It identifies key theoretical contributions, highlights gaps in the current body of knowledge, and positions this study within the context of Saudi Arabia's private sector. The chapter concludes by presenting the study problem, research questions, and recommended directions to address the identified research gaps.

EXPLORING THE PROJECT MANAGEMENT OFFICE (PMO) – ROLE, STRUCTURE AND PROCESSES (٢٠١٦). Philbin, S. P. (٢٠١٦)

Literature Review

This study is grounded in a comprehensive review of the relevant literature concerning the role, structure, and processes of the Project Management Office (PMO). One of the primary references is the work of Philbin (٢٠١٦), who provided an in-depth exploration of PMO functions within organizations. Philbin (٢٠١٦) emphasized that the PMO can assume multiple roles, ranging from providing consultative support to exercising direct control over project execution. The flexibility of the PMO structure allows it to align with the strategic needs of the organization effectively.

Philbin's study also categorized various PMO structures and highlighted the importance of designing a PMO that fits the organizational context and culture. Moreover, Philbin underscored the need for well-defined processes and procedures to ensure that the PMO contributes effectively to enhancing project performance. These insights formed the foundation for the current study's hypotheses, which focus on the relationship between PMO structure and its effectiveness in achieving strategic objectives.

In addition to Philbin's work, this study draws upon several other key contributions to the field. For example, Aubry et al. (٢٠٠٧) discussed the dynamic evolution of PMOs, suggesting that PMOs are not static entities but continuously adapt in response to organizational changes. Furthermore, Hobbs and Aubry (٢٠٠٨) provided significant evidence regarding the variations among different types of PMOs and their respective impacts on project success.

The selection of these specific studies was deliberate, as they offer theoretical models and empirical findings that directly support the objectives of this research. They collectively contribute to a solid theoretical framework that not only informs the study's hypotheses but also offers a validated perspective on the critical factors influencing PMO effectiveness.

The primary problem addressed in this paper is the lack of comprehensive frameworks and empirical studies that adequately describe the specification, functioning, and effectiveness of Project Management Offices (PMOs) in technology and engineering projects. Despite the increasing adoption of PMOs across various industries beyond IT, there remains a limited understanding of their roles, structures, processes, and impact on project success

١. PMO Roles and Structures

Philbin (٢٠١٦) provided a detailed exploration of PMO functions within organizations, emphasizing that PMOs can serve in diverse capacities, from offering consultative support to exercising direct control over project execution. This flexibility enables the PMO to align effectively with an organization's strategic needs. Philbin also categorized various PMO structures, stressing the importance of designing a PMO that fits the organizational context and culture.

٢. PMO Processes and Standardization

Philbin (٢٠١٦) underscored the significance of well-defined processes and procedures in ensuring that the PMO contributes to project performance and organizational success. A properly structured PMO, supported by clear processes, can facilitate project delivery, resource optimization, and strategic alignment.

٣. PMO Evolution and Adaptability

Aubry et al. (٢٠٠٧) argued that PMOs are not static entities but rather evolve dynamically in response to organizational changes. Their study emphasized that the PMO's adaptability is crucial to sustaining its relevance and effectiveness over time.

٤. PMO Types and Impact on Project Success

Hobbs and Aubry (٢٠٠٨) provided empirical evidence showing significant variations among PMO types (supportive, controlling, and directive) and their respective impacts on project success. Their research suggests that a tailored PMO structure can substantially influence project outcomes, especially when aligned with organizational strategy.

Research Questions

The study is guided by the following research questions:

١. What are the different roles of PMOs in organizing and managing technology and engineering projects?
٢. How do these roles vary across supportive, controlling, and directive PMO types?
٣. What are the essential structural components and processes required for an effective PMO?
٤. How can these components and processes be standardized while maintaining flexibility to adapt to project-specific requirements?
٥. What are the benefits of implementing PMOs in organizations managing technology and engineering projects?

٦. How do these benefits vary based on project complexity and organizational context?
٧. What challenges do organizations face when designing and implementing PMOs, particularly in engineering environments?
٨. How can these challenges be addressed to enhance PMO effectiveness in achieving project outcomes?
٩. How does the PMO contribute to strategic alignment and overall organizational performance in the technology and engineering sectors?

Key Observations

The review of prior studies reveals several critical gaps:

- Absence of **tailored PMO frameworks** that consider the specific needs, project complexities, and organizational structures within the Saudi private sector.
- Lack of **standardized communication strategies** to promote PMO integration and stakeholder engagement.
- Inadequate research on **standardized key performance indicators (KPIs)** that measure PMO contributions to strategic objectives, beyond operational success metrics.
- Limited studies addressing **cultural barriers** and organizational resistance that affect PMO implementation in the Saudi business environment.
- Minimal longitudinal research tracking PMO effectiveness over time, particularly in fast-evolving industries aligned with Saudi Vision ٢٠٣٠.

Aspect	Current Study (Saudi Private Sector)	Philbin (٢٠١٦)
Geographical Focus	Saudi Arabia, tied to Vision ٢٠٣٠	General, no specific country
Industry Focus	Private sector (multiple industries)	Tech & engineering sectors
Strategic Context	Strong national strategy link (Vision ٢٠٣٠)	Organizational strategy only
Key Problem	Misalignment of projects with national strategy; lack of innovation & KPIs	Undefined PMO roles & processes in tech projects
Cultural Considerations	Local cultural adaptation & leadership buy-in	Minimal cultural focus
Performance Measurement	Focus on clear KPIs linked to strategy	General process focus, limited KPI detail
Stakeholder Engagement	Emphasizes stakeholder involvement for alignment	Limited stakeholder detail
Practical Frameworks	Provides practical methods & models for Saudi context	Descriptive only, no applied frameworks

The Literature Gaps

Despite the increasing adoption of PMOs across various industries, there remains a lack of comprehensive frameworks and empirical studies that adequately describe the structure, functioning, and effectiveness of PMOs, particularly in technology and engineering projects within the Saudi private sector.

The reviewed literature emphasizes the importance of PMO flexibility, evolution, and alignment with organizational strategy. However, there is limited research that specifically addresses:

- How PMOs can be optimized for technology and engineering projects in the Saudi context.
- The unique challenges and cultural factors influencing PMO adoption and performance in Saudi private organizations.
- The strategic contributions of PMOs beyond operational efficiency, particularly in supporting national initiatives such as Saudi Vision ٢٠٣٠.

This study seeks to address these gaps by investigating the impact of PMOs on strategic plan execution in the Saudi private sector.

To advance the field and close these gaps, the following recommendations are proposed:

١. Develop Tailored PMO Frameworks

Organizations should establish PMO structures that are customized to their specific industries, project types, and strategic objectives. Standardization is important, but PMOs must also retain flexibility to adapt to unique project requirements, especially in agile environments.

٢. Implement Effective Communication Strategies

Clear and consistent communication about the PMO's purpose, processes, and strategic value is essential. Stakeholders must understand how the PMO contributes to project success and organizational growth to promote acceptance and collaboration.

٣. Focus on Saudi Private Sector Dynamics

More empirical studies are needed to explore PMO performance within the Saudi private sector, taking into account **local cultural factors, regulatory environments, and industry-specific practices**.

٤. Evaluate PMO's Role in Saudi Vision ٢٠٣٠

Future research should examine how PMOs can effectively support national transformation goals and contribute to strategic initiatives aligned with Saudi Vision ٢٠٣٠.

٥. Develop Sector-Specific PMO Models

Given the diversity of Saudi industries such as construction, healthcare, energy, finance, and IT, sector-specific PMO models should be developed to address industry-specific challenges and success factors.

٦. Conduct Longitudinal Studies

There is a need for long-term studies that assess PMO performance over multiple project cycles to better understand its sustained impact on strategic alignment and organizational performance.

٧. Enhance PMO Leadership and Competency Development

Further research should explore the leadership styles, skills, and competencies required for PMO managers to succeed in Saudi private organizations, supporting the development of targeted training programs.

٨. Support Digital Transformation and Agility

Research should focus on how PMOs can support digital transformation initiatives and adopt agile methodologies to increase responsiveness to dynamic market conditions.

٩. Develop Standardized KPIs to Measure Strategic Impact

Organizations need to establish **clear KPIs** that measure PMO contributions not only in terms of operational success but also in relation to strategic alignment and value creation.

١٠. Address Cultural Barriers

Further studies should investigate cultural and organizational resistance to PMO adoption and identify practical strategies to overcome these challenges, particularly within hierarchical and traditional business environments.

The contribution of project management offices (PMO) to the strategy implementation in Project-Based Businesses: systematic literature review and proposal of a mode (٢٠٢١) Brito, Medeiros Junior(٢٠٢١)

Literature Review

the literature on the role and impact of Project Management Offices (PMOs) in the implementation of strategic plans, with a particular focus on the Saudi private sector. The review covers key concepts such as PMO structures, the importance of standardization, stakeholder engagement, and the alignment of project goals with strategic objectives. It critically examines previous research, specifically the study titled "The Contribution of Project Management Offices (PMOs) to Strategy Implementation in Project-Based Businesses", and highlights the gaps this current research seeks to address. (Müller, ٢٠٠٩)

One of the persistent challenges identified in project management research is the **lack of standardization in project management concepts, structures, and approaches**, which can lead to inconsistencies in application and reduce the validity and generalizability of research findings. The study underscored that the absence of unified frameworks and consistent

methodologies not only complicates the effective measurement and evaluation of PMO contributions but also undermines the development of robust theoretical foundations in the field.

The research aimed to bridge this gap by exploring the role of PMOs in facilitating strategy implementation within Project-Based Businesses (PBBs). The study proposed that PMOs can significantly contribute to aligning projects with organizational strategies, but only if their structures, processes, and performance metrics are clearly defined and standardized. Without such standardization, there is a risk of ambiguity in PMO functions, which may hinder their ability to deliver strategic value consistently across different industries and organizational contexts.

However, despite the study's valuable contributions, it appeared to overlook several critical areas, such as **the active engagement of stakeholders, the importance of cross-departmental communication, and the necessity of continuously aligning project goals with evolving strategic objectives**. These elements are essential to fully realizing the potential of PMOs as strategic partners within organizations. Additionally, the study did not sufficiently address the dynamic complexities present in various sectors, particularly in rapidly transforming economies such as Saudi Arabia's private sector.

Building on the identified gaps, the current research emphasizes that Engaging stakeholders in strategic planning, project selection, and performance evaluation processes enhances buy-in and supports seamless strategy execution. Furthermore, this study highlights the importance of sector-specific adaptations and cultural considerations, particularly within the unique regulatory and operational landscape of the Saudi private sector. This refined focus contributes to a more comprehensive understanding of how PMOs can effectively support strategic planning and implementation in diverse and complex organizational settings.

Research Questions:

- What are the actions that PMOs can take to collaborate with strategy implementation in PBB?
- How can PMOs contribute to strategy implementation in PBB?

Key Observations

- **Theoretical Strength but Limited Practical Applicability:**
While the ٢٠٢١ study provided a valuable theoretical contribution to understanding PMO roles in strategy implementation, it lacked practical relevance for specific national contexts or industry sectors. Its generalized approach limits its applicability to region-specific challenges and organizational environments.
- **Absence of Stakeholder Collaboration:**
The study did not sufficiently address the critical role of stakeholder collaboration in PMO success. Stakeholder engagement is essential for ensuring that project selection,

execution, and outcomes are closely aligned with the organization's strategic goals. This omission weakens the practical utility of the proposed model.

- **Neglect of Cultural and National Factors:**
The study failed to consider national, cultural, and organizational dynamics, which significantly influence PMO effectiveness. This gap is particularly relevant in countries like Saudi Arabia, where cultural norms, leadership styles, and regulatory frameworks are unique and demand context-specific PMO practices.
- **Current Research Contributions:**
The present study addresses these gaps by offering practical, actionable frameworks that are specifically tailored to the Saudi private sector. It emphasizes the importance of stakeholder engagement, structured communication, cultural sensitivity, and continuous strategic alignment. Moreover, the study directly supports Saudi Arabia's national transformation agenda, Saudi Vision ٢٠٣٠, by providing PMO strategies that are adaptable, sustainable, and aligned with the country's strategic priorities.

Aspect	Current Study (Saudi Private Sector)	٢٠٢١ Study (Project-Based Businesses)
Geographical Focus	Saudi Arabia	Global
Industry Focus	Multiple Sectors	Project-Based Businesses
Strategic Context	Saudi Vision ٢٠٣٠ Alignment	General Strategy Implementation
Key Problem	Lack of tailored PMO frameworks, limited stakeholder engagement, communication gaps	Lack of PMO standardization
Cultural Considerations	Focus on Saudi cultural and leadership dynamics	Not addressed
Performance Measurement	Emphasis on practical, standardized measurement systems	Underdeveloped performance framework
Stakeholder Engagement	Central recommendation	Largely missing
Practical Frameworks	Provides actionable, Saudi-specific solutions	Conceptual model, limited practical application

The Literature Gaps

- Drawing on the limitations identified in the study, several key recommendations are proposed to enhance the effectiveness of Project Management Offices (PMOs) in supporting strategic plan implementation, particularly within the Saudi private sector. The study proposed a generalized conceptual model.
- It lacked attention to stakeholder engagement, communication practices, and organizational alignment at deeper levels.
- It did not sufficiently address context-specific factors such as national culture, regulatory environment, or sectoral needs.
- Addressing the absence of Saudi-specific PMO frameworks that align with strategic goals and Saudi Vision ٢٠٣٠.

- Highlighting the importance of stakeholder collaboration, communication, and leadership development.
- Proposing standardized KPIs that measure not only project delivery metrics but also long-term strategic contributions.
- Emphasizing benchmarking international best practices while customizing solutions to fit local Saudi cultural and organizational structures.
- Advocating for longitudinal studies to assess the sustained impact of PMOs on strategic plan implementation.

- **PMO Stakeholder Engagement:**
PMOs should actively engage stakeholders in decision-making processes, project selection, planning, and performance evaluation. This systematic involvement ensures that project objectives are aligned with strategic goals and fosters stakeholder commitment, which is essential for successful project outcomes.
- **Structured Communication Processes:**
There is a need to establish formal communication channels between PMOs, project teams, and executive leadership to ensure clear, timely, and effective information flow. Structured communication enhances coordination, supports faster decision-making, and improves the overall responsiveness of PMO activities.
- **Customized Yet Standardized PMO Frameworks:**
While standardization is critical to ensuring consistency and comparability, PMOs should retain the flexibility to tailor their frameworks to sector-specific needs and the unique cultural and regulatory environment of Saudi Arabia. Sectoral and cultural customization ensures that PMOs remain relevant and effective within the local context.
- **Robust Performance Measurement Systems:**
PMOs should implement formalized performance measurement systems that go beyond traditional project management indicators such as time, cost, and scope. These systems should include balanced Key Performance Indicators (KPIs) that capture both operational efficiency and long-term strategic contributions. The use of comprehensive tools like the Balanced Scorecard is recommended to provide a multi-dimensional view of PMO performance, aligning operational outcomes with strategic objectives.
- **Benchmarking and Best Practices:**
Saudi organizations should actively benchmark their PMO practices against international best practices to adopt proven frameworks and KPI systems. However, these global standards must be adapted to fit local organizational structures, leadership styles, and cultural norms to ensure successful integration and application.
- **Addressing Barriers to Performance Tracking:**
Effective PMO measurement requires addressing common challenges such as cultural resistance, resource shortages, and limited stakeholder participation. Overcoming these barriers is essential for establishing reliable, actionable, and transparent performance tracking mechanisms.
- **Continuous Strategic Alignment and Longitudinal Assessment:**
PMOs must regularly reassess their practices and project portfolios to ensure continuous alignment with Saudi Vision ٢٠٣٠ and the evolving needs of the Saudi private sector. Additionally, longitudinal studies should be conducted to evaluate the long-term impact

of PMOs on strategic plan implementation and to support sustained improvements in PMO effectiveness.

- **Stakeholder Engagement:** Involve stakeholders in discussions about strategic priorities and ensure that project selection processes reflect these priorities.

Furthermore, The literature review highlights persistent gaps in PMO standardization, stakeholder engagement, communication practices, and the adaptation of PMO frameworks to local cultural and sector-specific requirements. Previous research, particularly the study on Project-Based Businesses, provided a solid conceptual foundation but lacked practical guidance and regional specificity.

This study aims to address these shortcomings by providing tailored, actionable solutions specifically designed for the Saudi private sector. It emphasizes the critical importance of engaging stakeholders, establishing structured communication channels, developing flexible yet standardized PMO frameworks, and implementing robust performance measurement systems aligned with both operational metrics and strategic outcomes. The integration of international best practices with local customization is essential for enhancing PMO effectiveness in Saudi Arabia. (Müller, ٢٠٠٩)

By bridging these gaps, this study contributes to a deeper understanding of how PMOs can play a pivotal role in driving the successful implementation of strategic plans, particularly in the context of Saudi Vision ٢٠٣٠. The proposed recommendations offer a pathway for Saudi organizations to strengthen their PMO capabilities and achieve sustainable, strategic success.

To enhance their impact, PMOs should collaborate closely with stakeholders, align project goals with strategic objectives, and foster communication across departments.

Key Performance Indicators (KPIs) for measuring PMOs Services in selected Organisations in Botswana(٢٠٢٢) K. Ntshwene, J.K. Ssegawa , P.D. Rwelamila(٢٠٢٢)

Literature Review

The primary problem addressed in this research study is the lack of formal measurement systems and Key Performance Indicators (KPIs) used by Project Management Offices (PMOs) to assess the effectiveness and efficiency of their services in various organizations in Botswana. This gap in measurement limits organizations' ability to evaluate the value contribution of PMOs towards successful project delivery, which is expected to be within the constraints of time, budget, and quality specifications.

PMOs are typically established to improve project governance, ensure alignment with strategic objectives, and enhance organizational project delivery capabilities. The literature consistently emphasizes that PMOs can bridge the gap between strategy formulation and execution by providing structure, standardization, and performance oversight.

Despite these advantages, there is no universal agreement on PMO structures, roles, or performance measurement systems. This variation raises concerns about the consistency and

comparability of PMO contributions across different organizational settings. The need for well-defined Key Performance Indicators (KPIs) to measure PMO effectiveness is frequently cited but often insufficiently addressed in existing research.

Research Questions:

- What are the current practices related to the measurement of PMO services in selected organizations in Botswana?
- How do these practices affect project delivery success?
- What specific KPIs are utilized by the identified PMOs to measure their effectiveness and efficiency?
- Are these KPIs aligned with the organizational goals and the expected outcomes of project management?
- What challenges do organizations face in establishing and implementing formal measurement regimes for their PMOs?
- How do these challenges affect the overall performance and credibility of PMOs?
- What are the common factors that led to the establishment of PMOs in the selected organizations?
- How do those factors correlate with the success or failure of project completions?
- How does the lack of KPIs in most organizations impact the perceived value of the PMOs?

The ٢٠٢١ study, The Contribution of Project Management Offices (PMOs) to Strategy Implementation in Project-Based Businesses, explored how PMOs support strategy implementation within project-based organizations. The study identified the lack of standardization in PMO concepts and methodologies as a major challenge, which can undermine both research validity and practical effectiveness.

While the study proposed a conceptual model to link PMOs to strategy execution, it did not provide practical frameworks tailored to specific industries, countries, or cultural settings. Additionally, it failed to address key elements such as:

- Active stakeholder engagement in PMO processes.
- The role of communication in ensuring project alignment.
- National and cultural influences on PMO design and success.

These gaps limit the applicability of the ٢٠٢١ study to regions like Saudi Arabia, where cultural, leadership, and regulatory factors significantly shape organizational practices.

PMOs in the Saudi Private Sector

Saudi Arabia's Vision ٢٠٣٠ emphasizes diversification, innovation, and improved organizational efficiency across the private sector. In this context, PMOs can serve as critical enablers of strategic plan implementation. However, Saudi organizations face challenges that require customized PMO frameworks, including:

- Cultural barriers related to hierarchy, decision-making, and resistance to change.
- Limited stakeholder involvement in project selection and KPI development.
- Inconsistent performance measurement practices that do not adequately capture strategic contributions.

The Saudi private sector needs PMO models that are both globally benchmarked and locally adapted to address these challenges effectively.

Performance Measurement and the Role of KPIs

Accurately measuring PMO performance is essential to demonstrating their value in strategic plan execution. KPIs provide a structured method to assess whether PMOs are contributing to both project success (time, cost, scope) and broader strategic objectives (alignment, value delivery).

Although the Botswana study (٢٠٢٢) focused on the lack of formal KPI measurement systems, its emphasis on developing clear, actionable performance indicators is highly relevant to the Saudi context. Saudi organizations can benefit from adopting performance measurement systems that:

- Integrate strategic KPIs aligned with Saudi Vision ٢٠٣٠.
- Combine operational metrics (cost, schedule, scope adherence) with strategic outcomes (business value, customer satisfaction, alignment with long-term goals).
- Address cultural and organizational barriers to effective KPI implementation.

By tailoring these measurement practices to Saudi-specific challenges, PMOs can provide clearer evidence of their strategic impact.

Key Observations

- The ٢٠٢١ study provided valuable theoretical contributions but lacked practical relevance to specific national or sectoral contexts.
- It did not address stakeholder engagement, which is essential for aligning projects with organizational strategies.
- It overlooked the influence of national culture, regulatory environments, and sector-specific needs on PMO effectiveness.
- It failed to propose standardized performance measurement systems adaptable to diverse organizational settings.

Aspect	Current Research: Saudi Private Sector	Botswana Study (٢٠٢٢)
Geographical Focus	Saudi Arabia	Botswana
Industry Focus	Saudi private sector with focus on Vision ٢٠٣٠ alignment	Selected organizations
Strategic Context	Both operational and strategic KPIs (alignment, value delivery, national objectives)	Primarily operational KPIs (time, cost, scope)
Key Problem	Central to PMO design and KPI customization	Not emphasized
Cultural Considerations	Strongly emphasized as essential for KPI development and project alignment	Limited discussion
Performance Measurement	Recommended as formalized, multi-level communication channels	Not detailed
Stakeholder Engagement	Includes sustained alignment with Saudi Vision ٢٠٣٠, long-term impact evaluation	Limited to operational outcomes
Practical Frameworks	Recommended with localization for Saudi cultural and sector-specific needs	Recommended international best practices

In contrast, the current study emphasizes practical solutions customized for Saudi Arabia's private sector and aligns with the national transformation agenda under Vision ٢٠٣٠.

The Literature Gaps

Building on the limitations of the ٢٠٢١ study and informed by best practices in performance measurement, the following recommendations are proposed to enhance PMO effectiveness within the Saudi private sector:

- Active Stakeholder Engagement

PMOs should systematically involve stakeholders in project selection, planning, KPI development, and performance evaluation. This collaboration will ensure that project priorities align with strategic objectives and will increase stakeholder commitment throughout the project lifecycle.

- Structured Communication Channels

Saudi organizations should establish formal communication frameworks that connect PMOs, project teams, and executive leadership. Improving information flow and coordination will help PMOs adapt quickly to shifting strategic priorities and project demands.

- Customized PMO Frameworks

While maintaining core elements of standardization, PMOs should retain the flexibility to tailor their processes to Saudi cultural, regulatory, and sector-specific requirements. This balance ensures both consistency and local relevance.

- Robust Performance Measurement Systems

Organizations should implement formal performance measurement systems that go beyond traditional project metrics. These systems should:

- Measure project delivery success (time, cost, scope).
- Assess strategic contributions, including alignment with Saudi Vision ٢٠٣٠, business value, and customer impact.
- Use tools like the Balanced Scorecard to evaluate performance across multiple dimensions.

- Benchmarking Best Practices

Saudi PMOs should benchmark their structures, KPIs, and operational practices against international standards. Global best practices can be adapted to suit local Saudi contexts, improving both performance and credibility.

- Continuous Strategic Alignment

PMOs must regularly reassess their goals, processes, and KPIs to ensure sustained alignment with evolving organizational strategies and national objectives under Vision ٢٠٣٠.

- Long-Term Impact Evaluation

Future studies should adopt longitudinal research methods to evaluate the long-term contributions of PMOs to strategic plan implementation. This approach will provide deeper insights into PMO maturity and sustained organizational impact.

Organizations should benchmark their PMO practices to identify best practices in performance measurement and KPI utilization. Implementing formal performance measurement systems with defined KPIs, using the balanced scorecard framework, and involving stakeholders can enhance performance monitoring. Addressing barriers like cultural resistance and resource limitations is also essential for effective measurement.

The impact of Project Management Offices on organizational performance(٢٠٢٣) Adele JAMALELDINE (٢٠٢٣)

Literature Review

The effectiveness of Project Management Offices (PMOs) in facilitating the implementation of strategies within Project-Based Businesses (PBB) is often unclear, leading to challenges in aligning project outcomes with strategic objectives

PMOs have long been recognized for their ability to enhance project delivery success by providing governance structures, standardized processes, and improved resource management. The ٢٠٢٣ study titled "**The Impact of Project Management Offices on Organizational Performance**" focused on how PMOs contribute to improving project efficiency, achieving delivery targets, and ensuring adherence to time, cost, and scope constraints. This study emphasized the operational benefits of PMOs, particularly in terms of process standardization, risk management, and performance tracking.

The ٢٠٢٣ study on the impact of Project Management Offices (PMOs) on organizational performance highlights the positive role PMOs play in enhancing efficiency, improving project success rates, and supporting strategic goals. However, the study lacks consideration of regional and cultural factors, particularly within the Saudi private sector, and does not differentiate the effects across specific industries or types of PMOs. Additionally, it focuses on short-term outcomes without exploring long-term impacts on organizational sustainability and strategic growth. Future research should address these gaps by examining PMOs within specific regional and industry contexts, conducting longitudinal studies, distinguishing between different PMO structures, and assessing the PMO's contribution to strategic alignment and organizational change, especially in environments undergoing digital transformation.

However, while the ٢٠٢٣ study provided valuable insights into the project-level contributions of PMOs, it did not sufficiently explore the broader strategic impact of PMOs on organizational goals. Additionally, it lacked consideration of cultural, sector-specific, and stakeholder engagement factors that can significantly influence PMO effectiveness, particularly in distinctive national contexts.

Research Questions:

- How do PMOs contribute to the alignment of project outcomes with organizational strategies in PBB?
- What specific roles do PMOs play in enhancing communication and collaboration among project teams and stakeholders?
- What are the key factors that influence the effectiveness of PMOs in strategy implementation within PBB?

Key Observations

- The ٢٠٢٣ study made a valuable contribution in terms of understanding how PMOs influence project-level performance but did not extend this analysis to strategic plan execution.
- The current study addresses these gaps by offering practical, actionable models specifically designed for the Saudi private sector.
- This research emphasizes stakeholder collaboration, communication structures, strategic alignment, and cultural sensitivity as critical enablers of PMO success.
- Limited Stakeholder Engagement: Both studies overlooked the active role stakeholders should play in project selection, performance measurement, and strategic alignment.
- Inadequate Cultural Consideration: National cultural dynamics, leadership styles, and organizational behaviors specific to countries like Saudi Arabia were not considered.
- Operational Focus: Prior research focused heavily on project efficiency (time, cost, scope) without adequately addressing strategic contributions or long-term impacts.
- Lack of Context-Specific Frameworks: There is an absence of PMO models tailored to the regulatory and cultural environment of the Saudi private sector.
- Absence of Longitudinal Studies: Previous studies did not explore the sustained impact of PMOs over time in driving strategic objectives.

To address the gaps identified in previous research, PMOs in the Saudi private sector should adopt tailored frameworks that:

- Align with the cultural values, leadership dynamics, and communication styles prevalent in Saudi organizations.
- Integrate international best practices while customizing them to the local regulatory and operational landscape.
- Engage stakeholders in decision-making processes to increase buy-in and ensure strategic alignment.

Aspect	Current Study: Saudi Strategic Plan Impact	٢٠٢٣ Study: Organizational Performance
Geographical Focus	PMO's role in strategic plan execution aligned with Saudi Vision ٢٠٣٠	PMO's effect on operational efficiency and organizational performance
Industry Focus	Operational KPIs + Strategic KPIs (alignment, value delivery, Vision ٢٠٣٠ contribution)	Project delivery success (time, cost, scope)
Strategic Context	Central to project selection, KPI development, and strategy alignment	Limited
Key Problem	Strong focus on Saudi culture, leadership style, and organizational behavior	Not addressed
Cultural Considerations	Core focus: aligning projects with strategic plans and national goals	Not a primary focus
Performance Measurement	Emphasizes formalized, multi-layered communication between PMOs, project teams, and executives	٢٠٢٣ Study: Organizational Performance
Stakeholder Engagement	Customized international best practices adapted for Saudi private sector needs	PMO's effect on operational efficiency and organizational performance
Practical Frameworks	Advocates for longitudinal evaluation of PMO contributions to strategy execution	Project delivery success (time, cost, scope)

This study missed the role-definition process and regularly reviewing and refining roles can help mitigate these issues. Without clear definitions, roles can become ambiguous, leading to confusion about who is responsible for what tasks. This can result in overlapping duties or gaps in accountability, potentially hindering project progress.

The Literature Gaps

Drawing on the limitations of prior studies, the following recommendations are proposed to enhance the role of PMOs in the Saudi private sector:

- **Active Stakeholder Engagement:** PMOs should involve stakeholders in project selection, planning, and KPI development to ensure alignment with strategic priorities and foster commitment.
- **Structured Communication Channels:** Establish formal communication processes that connect PMOs, project teams, and executive leadership, ensuring timely information sharing and effective decision-making.
- **Customized PMO Frameworks:** Develop PMO structures that are standardized at their core but adaptable to the specific needs of different sectors and Saudi organizational cultures.
- **Robust Performance Measurement Systems:** Implement KPIs that balance operational metrics (time, cost, scope) with strategic outcomes (value delivery, strategic alignment, Vision ٢٠٣٠ contributions).
- **Benchmarking International Best Practices:** Saudi organizations should adopt proven global PMO practices but modify them to fit the local regulatory and cultural context.
- **Continuous Strategic Alignment:** PMOs must regularly reassess their processes to remain aligned with evolving corporate strategies and national priorities.
- **Long-Term Impact Evaluation:** Future research should track PMO contributions over time to assess their sustained role in strategy execution and organizational transformation.
- **Establish clear roles and responsibilities for PMOs** to ensure alignment with strategic goals.
- **Foster a culture of collaboration** between PMOs and project teams to enhance communication and knowledge sharing.
- **Invest in training and development** for PMO staff to improve their strategic management skills and project oversight capabilities.
- The primary goal of this book is to provide practical guidance and best practices for setting up and operating successful PMOs. It aims to help organizations improve project performance, reduce costs, and achieve .

References

١. (Aziz, Emad's , May ٢٠١٤,) Your key to strategy execution and results delivery, conference paper PMO, Strategy.
<https://www.pmi.org/learning/library/project-management-office-strategy-execution>
٢. (Turki Alsediry, ٢٠١٣) Alignment of large project management process to business strategy: A review and conceptual framework mTurki Alsudiri, Wafi Al-Karaghoul, Tillal Eldabi - Journal of Enterprise Information Management ISSN: ١٧٤١-٠٣٩٨
https://www.emerald.com/insight/content/doi/10.1108/jeim-٢٠١٣-٠٧-٠٠٥/full/html?utm_source=chatgpt.com
٣. Crawford, L., & Pollack, J. (٢٠٠٧) How Generic Are Project Management Knowledge and Practice? Project Management Journal, ٣٨, ٨٧-٩٦. <https://doi.org/10.11٧٧/٨٧٥٦٩٧٢٨.٧.٣٨.٠١.٩>
٤. Crawford, L., & Pollack, J. (٢٠٠٤). "How generic is project management? A re-examination of the role of project management in delivering organizational strategy." International Journal of Project Management, ٢٢(٧), ٥٢٩-٥٣٥. DOI: ١٠.١٠١٦/j.ijproman.٢٠٠٤.٠٦.٠٠٢. This paper discusses the alignment of project management with organizational strategy.
٥. Ali Hadi, Yang Liu, Shenxue Li, (٢٠٢٢) Transcending the silos through project management office: Knowledge transactions, brokerage roles, and enabling factors
<https://www.sciencedirect.com/science/article/abs/pii/S٠٢٦٣٧٨٦٣٢١٠٠١٢٧٧?via%3Dihub>
٦. Abdullah, S., & Al-Salem, M. (٢٠١٩) Adapting Project Management Offices to Saudi Vision ٢٠٣٠: Challenges and Opportunities. Proceedings of the ٩th International Conference on Project Management.
٧. Marsh, L. (٢٠١٤). Agile Project Management for Dummies. Wiley.
A practical guide on agile project management, which PMOs can adopt to enhance innovation and flexibility.
٨. Serrador, P., & Turner, R. (٢٠١٥) The influence of project management methodologies on project success: The importance of agile and hybrid approaches. International Journal of Project
٩. Rayan E, El-Adaway (٢٠٢٠) Rayan Assaad, S.M.ASCE rayan.assaad@mst.edu, Islam H. El-Adaway, F.ASCE Technical Papers Feb ١٧, ٢٠٢٠ Predicting Project Performance in the Construction Industry
[https://doi.org/10.1061/\(ASCE\)CO.1943-7862.0001٧٩٧](https://doi.org/10.1061/(ASCE)CO.1943-7862.0001٧٩٧)
١٠. Albaiti & Alsulami (٢٠٢١) Developing a Maturity Rating System for Project Management Offices Alshabragi, Abdullah M; Almohsen, Abdulmohsen S; Bin Mahmoud, Abdulrahman Systems; Basel Vol. ١٢, Iss. ٩, (٢٠٢٤): ٣٦٧. DOI: ١٠.٣٣٩٠/systems١٢.٩.٣٦٧
<https://www.proquest.com/scholarly-journals/developing-maturity-rating-system-project/docview/311٠٦٩٥٨٤٥/se-٢>
١١. Ul Musawir, U., et al. (٢٠٢٢) Benefits realisation in an agile environment Author links open overlay panel Carl Marnewick a, Annlizé L. Marnewick b
<https://doi.org/10.1016/j.ijproman.٢٠٢٢.٠٤.٠٠٥>

١٢. **Humayoun Khan (٢٠٢٣)**
Khan, H. K. (٢٠٢٣). Saudi Vision ٢٠٣٠: The growing importance of PMOs in achieving economic diversification.
https://humayoun.com/category/pmo/?utm_source=chatgpt.com
١٣. **Rigby, D., Bilton, C., & Harvey, M. (٢٠١٦)**. Enhancing project benefit realization through integration of line managers as project benefit managers. *International Journal of Project Management*, ٣٤(٤), ٧٧٩–٧٨٨. <https://doi.org/10.1016/j.ijproman.2016.06.009>
١٤. **Jaffrani & Ahmed (٢٠٢٠)**
Benefits Realization Management and Its Impacts on Project Success
<http://dx.doi.org/10.51916/aksh.2020.v01i01.001>
١٥. **Aubry, M., Hobbs, B., Müller, R., & Blomquist, T. (٢٠٠٧)**. *Project management office: A conceptual framework*. *International Journal of Project Management*, ٢٥(٤), ٣٢٩–٣٣٦.
<https://doi.org/10.1016/j.ijproman.2007.01.003>
١٦. **Aubry, M., & Hobbs, B. (٢٠١١)**. A fresh look at the contribution of project management to organizational performance. *Project Management Journal*, ٤٢(١), ٣–١٦.
<https://doi.org/10.1002/pmj.20213>
١٧. **PwC Middle East. (٢٠٢٣)**
The Journey to PMO Maturity in the Middle East*. PricewaterhouseCoopers.
https://www.pwc.com/m1/en/blog/end-result-pmo-journey-future-fit-age-transformation.html?utm_source=chatgpt.com
١٨. **Hobbs, B., & Aubry, M. (٢٠٠٨)**. *An empirically grounded search for a typology of project management offices*. *Project Management Journal*, ٣٩(5), 57٩–5٨٢. <https://doi.org/10.1002/pmj.20057>
١٩. **Müller, R. (٢٠٠٩)**. *The contribution of project management offices (PMOs) to strategy implementation in project-based organizations*. *International Journal of Project Management*, ٢٧(٥), ٤٥٦–٤٦٧.
<https://doi.org/10.1016/j.ijproman.2008.11.009>
٢٠. **Badewi, A. (٢٠١٦)**. The impact of project management (PM) and benefits management (BM) practices on project success: Towards developing a project benefits governance framework. *International Journal of Project Management*, ٣٤(٤), ٧٦١–٧٧٨. <https://doi.org/10.1016/j.ijproman.2016.06.005>
٢١. **Beck, K., Beedle, M., van Bennekum, A., Cockburn, A., Cunningham, W., Fowler, M., ... & Thomas, D. (٢٠٠١)**. Manifesto for agile software development. Retrieved from <http://agilemanifesto.org/>
٢٢. **Bradley, G. (٢٠١٠)**. *Benefit Realisation Management: A Practical Guide to Achieving Benefits Through Change*. Gower Publishing.
٢٣. **Unger, B. N., Gemünden, H. G., & Aubry, M. (٢٠١٢)**. The three roles of a project portfolio management office: Their impact on portfolio management execution and success. *International Journal of Project Management*, ٣٠(٥), ٦٠٨–٦٢٠. <https://doi.org/10.1016/j.ijproman.2012.01.010>
٢٤. **Jonas, D. (٢٠١٠)**. Empowering project portfolio managers: How management involvement impacts project portfolio management performance. *International Journal of Project Management*, ٢٨(٨), ٨١٨–٨٣١. <https://doi.org/10.1016/j.ijproman.2010.07.002>
٢٥. **PMI (Project Management Institute). (٢٠١٣)**. *Pulse of the Profession: The High Cost of Low Performance*. Project Management Institute.
٢٦. **Too, E. G., & Weaver, P. (٢٠١٤)**. The management of project management: A conceptual framework for project governance. *International Journal of Project Management*, ٣٢(٨), ١٣٨٢–١٣٩٤.
<https://doi.org/10.1016/j.ijproman.2013.07.006>
٢٧. **Rigby, D. K., Sutherland, J., & Takeuchi, H. (٢٠١٦)**. Embracing agile. *Harvard Business Review*, ٩٤(٥), ٤٠–٥٠.
٢٨. **Sharma, R. R. K., Gupta, A. K., & Rathore, A. P. S. (٢٠١٢)**. Project management office: A step forward towards project management success. *Global Journal of Flexible Systems Management*, ١٣(٤), ٢٠٥–٢١٤. <https://doi.org/10.1007/s40171-013-0018-4>

٢٩. **Henderson, J. C., & Venkatraman, N. (١٩٩٣).** Strategic alignment: Leveraging information technology for transforming organizations. IBM Systems Journal, ٣٢(١), ٤-١٦. <https://doi.org/١٠.١١٤٧/sj.٣٨٢.٠٤٧٢>
٣٠. **Philbin, S. P. (٢٠١٦).** Exploring the project management office (PMO) – Role, structure and processes. International Journal of Project Management, ٣٤(٤), ٥٤١-٥٤٨. <https://doi.org/١٠.١٠١٦/j.ijproman.٢٠١٥.٠٨.٠٠٢>
- ٢٧.**A-Aubry, M., Hobbs, B., Müller, R., & Blomquist, T. (٢٠٠٧).** Project management office transformations: Alignment and performance. International Journal of Project Management, ٢٥(١), ٤٤-٥٧. <https://doi.org/١٠.١٠١٦/j.ijproman.٢٠٠٦.٠٩.٠٠٣>
- ٢٧.**B-Hobbs, B., & Aubry, M. (٢٠٠٨).** An empirically grounded search for a typology of project management offices. Project Management Journal, ٣٩(S١), S٦٩-S٨٢. <https://doi.org/١٠.١٠٠٢/pmj.٢٠٠٥٧>
٣١. **Brito, Medeiros Junior(٢٠٢١)**
The contribution of project management offices (PMO) to the strategy implementation in Project-Based Businesses: systematic literature review and proposal of a model
٣٢. **K. Ntshwene, J.K. Ssegawa , P.D. Rwelamila(٢٠٢٢)**
Key Performance Indicators (KPIs) for measuring PMOs Services in selected Organisations in Botswana <https://doi.org/١٠.١٠١٦/j.procs.٢٠٢١.١٢.٠٩٨>
٣٣. **Adele JAMALELDINE (٢٠٢٣)**
The impact of Project Management Offices on organizational performance(٢٠٢٣)
<https://www.iseor-formations.com/pdf/ACTESCOLMCD٢٠٢١/JAMALELDINE.pdf>
٣٤. **Jiang, J. J., & Klein, G. (٢٠٠٠).**
Project management success and failure: The role of the project management office. International Journal of Project Management, ١٨(٥), ٣٥٥-٣٦٢
٣٥. **Abdullah, S., & Al-Salem, M. (٢٠١٩).** Adapting Project Management Offices to Saudi Vision ٢٠٣٠: Challenges and Opportunities. Proceedings of the ٩th International Conference on Project Management.
٣٦. **Calantone a Kim b,(٢٠٠٦)**
the influence of internal and external firm factors on international product adaptation strategy and export performance: A three-country comparison
<https://doi.org/١٠.١٠١٦/j.jbusres.٢٠٠٥.٠٥.٠٠١>
