

PROJECT FEASIBILITY STUDY

PMG201

Prepared by
Dr. Manal Elsayed

Dr. Manal Elsayed

Lecture No. 6



Prepared by

Dr. Manal Elsayed

Dr. Manal Elsayed

Planning the Project

OVERVIEW

1. The Contents of a Project Plan – The “Project Charter”.
2. The Planning Process – Overview.
3. The Planning Process – Nuts and Bolts.
4. More on the Work Breakdown Structure and Other Aids .
5. Multidisciplinary Teams – Balancing Pleasure and Pain.

Introduction

If problems arise during the life of a project, our first hunch **حَدَسْنَا الْأَوَّل** would be that the project was not properly planned. Most of the time our hunch would be correct. وهذا سيكون صحيح. Inadequate planning is more the case than the exception.



Project Planning

Basic objective:

To create a plan to **meet the commitments** of the project.

Create a path that, if followed, will lead to a **successful project.**

Planning involves

Defining the **LC life cycle** process to be followed, estimates, detailed schedule, plan for quality, etc.

Main output

A project management plan, and
project schedule.



Key Planning Tasks


- Define suitable processes for executing the project.
- Estimate effort.
- Define project milestones and create a schedule.
- Define **quality objectives** and a **quality plan**.
- Identify risks and make plans to mitigate them.
- Define **measurement plan**, project-tracking procedures, training plan, team organization, etc.




Life Cycle Process

- Various LC models - waterfall, iterative, prototyping; diff models شلال ، تكراري ، نماذج أولية suit different projects نماذج الفرق
- During planning can select the model that is best for the project.
- This gives the overall process which has to be fine-tuned to suit the project needs
- Usually done **by process tailoring** - changing the process to suit the project
- Tailoring finally results in adding, deleting, modifying some process steps

Agile

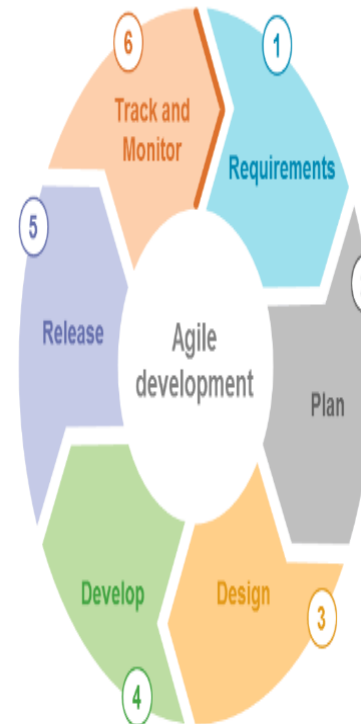


Waterfall

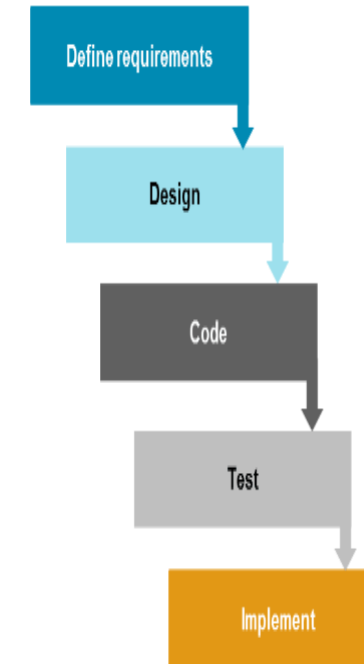

1. The Contents of a Project Plan The Project Charter

It is a document that serves to formally announce the selection and approval of the project, as well as grant the project manager the authority to meet project objectives using organizational resources. It also includes the main goals of the project, and the designation of roles and responsibilities.

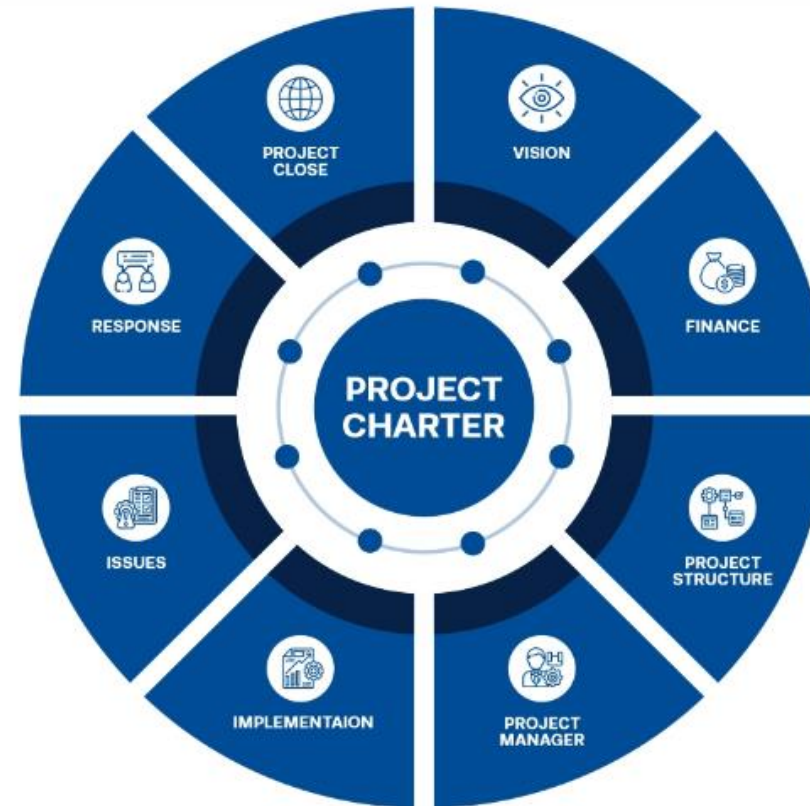

The **project plan** fall into one of the following nine categories:

1. *Overview.*
2. *Objectives.*
3. *General approach.*
4. *Contractual aspects.*
5. *Schedules.*
6. *Resource requirements .*
7. *Personnel.*
8. *Risk management.*
9. *Evaluation methods.*



1- Overview

- This section contains a brief description of the project and its deliverables. This section should include the *Business Case* for the project.
- **The Business Case includes the strategic reasons for the project**, its expected **profitability** and **competitive effects** as well as the **desired scope** and any other technical results. The main **goal of the Business Case** is to communicate to project team members (and others) the reasons why the organization is undertaking the project.




2. Objectives.

This is a **more detailed description** of the project's scope, its deliverables and outcomes. Another approach to describing a project's objectives **is the project mission statement**. While somewhat similar to the Business Case, the **focus** of the mission statement is to communicate to project team members (and others) **what will be done to achieve the project's overall objectives**. To foster team understanding of the project as a whole.



3 .General approach.

In this section, the technological and managerial approaches to the work are described. Also noted are plans that go beyond the organization ' s standard management practices. For example, some firms do not allow the use of consultants or subcontractors without special approval.

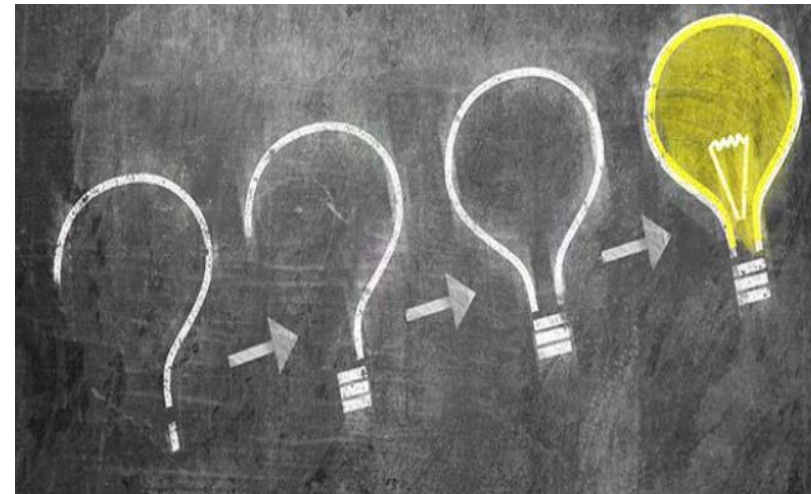

4. *Contractual aspects*

This section contains a **complete description of all agreements made with the client or any third party.**

This list would include all reporting requirements; the technical specifications of all deliverables; agreements on delivery dates.

If relevant, it may contain agreements to comply with legal, environmental, and other constraints on the project work and outputs.



5. Schedules

An outline of all schedules and milestones. Each task in the project is listed in a project WBS. Listed with each task is the time required to perform it. The project schedule is constructed from these data and is included in this section.



6. Resource requirements

Estimates of project expenses, both capital and operating, are included here. The costs associated with each task are shown, and overhead and fixed charges are listed. In addition, cost monitoring and cost control procedures are described here. The details of materiel acquisition are also detailed in this section.



7. Personnel.

This section covers **the details of the project work force**. It notes any special skill requirements, necessary training. Combined with the schedule, it notes the time-phasing of all personnel requirements.



8. Risk management

Planners should list the major and minor disasters that may strike projects. The argument is made that crises cannot be predicted.

The only uncertainty, however, is which of the crises will occur and when. In any case, dealing with crises does not require a which - and - when prediction. Contingency plans to deal with such potential crises should be a standard part of the project plan.



9. *Evaluation methods.*

Descriptions of all project evaluation procedures and quality standards are found in this section. Also included are procedures to ensure compliance with all corporate requirements for monitoring, collecting, and storing data on project performance.



2. The Planning Process—Overview

- A great deal has been written about planning. Some of the literature focuses on the strategic aspect of planning — choosing and planning projects that contribute to the organization ' s goals.
- Another body of writing is directed at the techniques of how to plan rather than what to plan.
- As far as we can determine, the way that planning techniques vary in these different cases has more to do with nomenclature than substance. الطريقة التي تختلف بها تقنيات التخطيط في هذه الحالات المختلفة لها علاقة بالتسميات أكثر من الجوهر.



**PLANNING TOOLS AND
TECHNIQUES..**

The following planning process that has been divided into **EIGHT** distinct steps.

1. **Develop and evaluate the concept** of the project. Describe what it is you wish to develop, including its basic performance characteristics, and decide if getting such a deliverable is worthwhile.
2. **Carefully identify the actual capabilities that the project's deliverable must have to be successful.**
3. **Create a system** (product or service), which is to say, build a prototype deliverable تسليم النموذج الأولي.
4. Test the prototype to see if it does, in fact, **have the desired capabilities. If necessary, cycle back to step 3** to modify the prototype and retest it. Continue until the deliverable meets the preset requirements.



5. Integrate the deliverable into the system for which it was designed.
6. Validate the deliverable — which answers the question, “does it still work properly?”
7. If the deliverable has been validated, let the client test it. Can the client operate the system? If not, instruct the client.
8. If the client can operate (and accepts) the deliverable, make sure that the client understands all standard operating and maintenance requirements. Then shake the client’s hand, present the client with a written copy of maintenance and operating instructions, give the client the bill, and leave.
قدم للعميل نسخة مكتوبة من تعليمات الصيانة والتشغيل ،
وأعط العميل الفاتورة ، وغادر

planning
process



3. The Planning Process—Nuts and Bolts

This section deals with the problem of determining and listing the various tasks that must be accomplished in order to complete a project. The important matters of generating a project budget and developing a precise project schedule are left to coming chapters, though much of the raw material for doing those important things will come from the planning process described here.



The Planning Process—Nuts and Bolts cont. ...


The project launch meeting sets the project scope, demonstrates managerial commitment to the project, and initiates the project plan.

The result is a WBS that lists all the tasks required to carry out the plan together with task resource requirements, durations, predecessors, and identification of the people responsible for each task.




4. More on the Work Breakdown Structure and Other Aids

The process of building a WBS is meaningful. The PM and individual team members may differ on the technical approach to working on the task, the type and quantity of resources needed, or the duration for each subtask. If so, negotiation is apt to accompany the planning process. As usual, participatory management and negotiation often lead to improved project performance and better ways of meeting the project's goals.

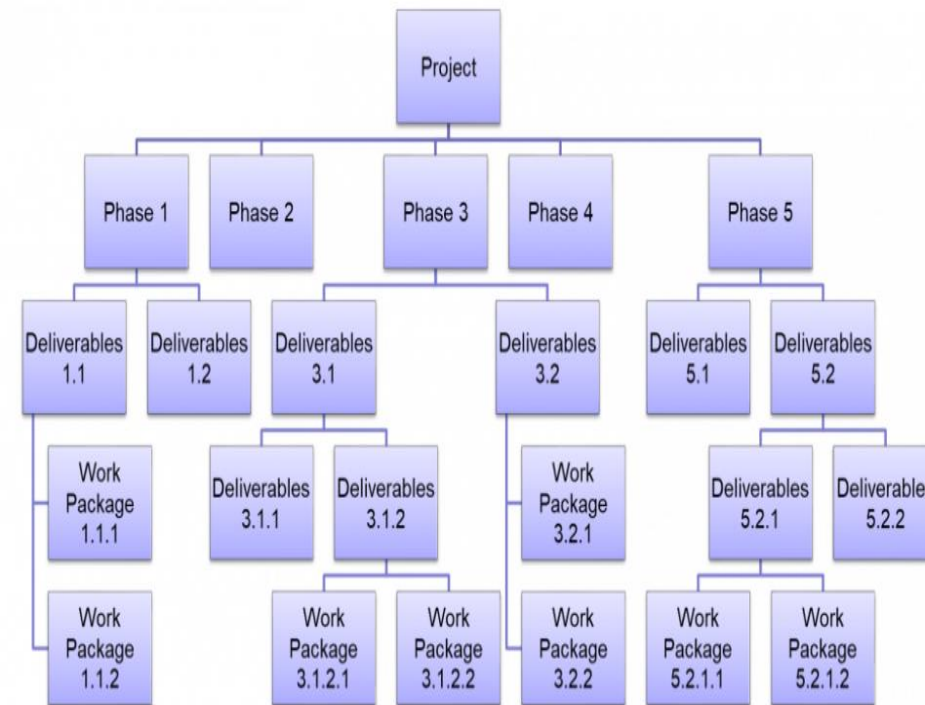

More on the Work Breakdown Structure and Other Aids cont.

1. All project activities will be identified and arranged in successively finer detail, that is, by levels.
2. For each activity, the type and quantity of each required resource (including personnel) are identified.
3. For each activity, predecessors كل ما سبق and task duration are estimated.
4. All project milestones المعالم are identified and located on the project schedule following their predecessor activities.
5. For each activity, the individual or group assigned to perform the work is identified.

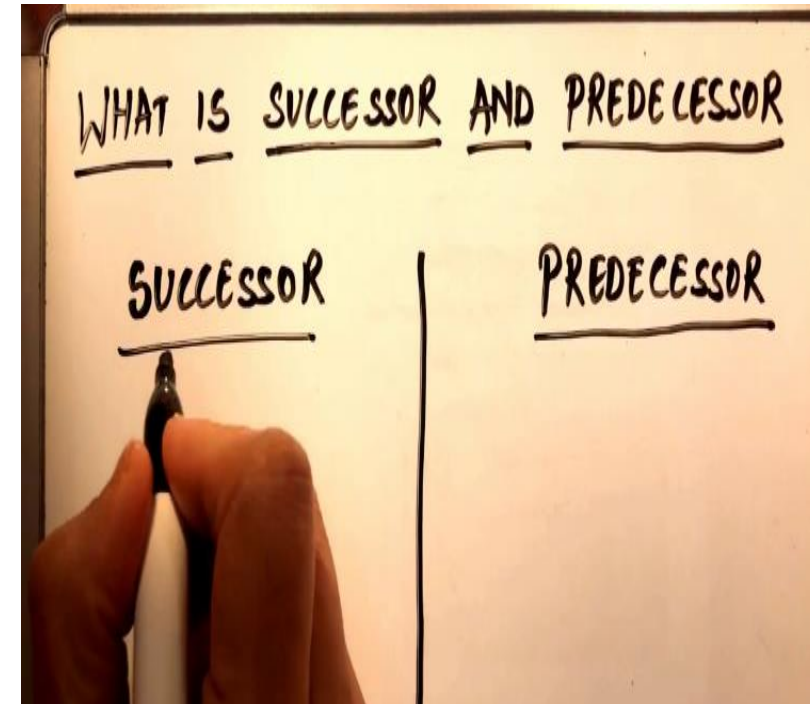


More on the Work Breakdown Structure and Other Aids cont.

6. If project milestones, task durations, and predecessors are combined, the result is **the project master schedule.**

7. **The master schedule allows** the PM to compare actual and planned task durations and resource usage at any level of activity.

The need for such comparisons provide the information about project **performance should be monitored.** This gives the PM the ability to control the project and **take corrective action** if the project is not proceeding according to plan.

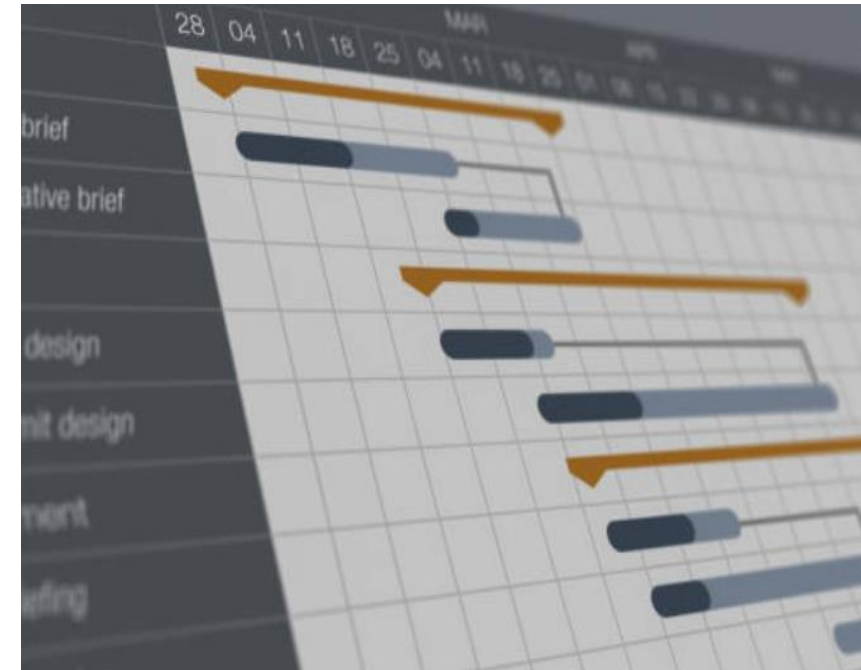

5. Multidisciplinary Teams, Balancing Pleasure and Pain

Integration Management

Integration management is an organized approach that ensures all processes within a project are synchronized and executed efficiently, and resources remain on track to achieve the project goals. It helps project managers to balance stakeholder expectations and customer needs while optimizing tasks and resources, steering the project toward success.


what can be achieved through integration management:

- Processes and tasks can be organized and listed out.
- Team members can be allocated responsibilities.
- Shared resources and their overlapping schedules are managed.
- Work efficiency within teams is enhanced.



Interface Coordination , Interface Management

- One of the PM ' s more difficult problems is coordinating the work of different functional groups interacting as team members.
- The team members come from different functional areas and often are not used to dealing with one another directly.
- For the most part, they have no established dependencies on each other and being co - members of a team is not sufficient to cause them to associate — unless the team has a mission that makes it important for the members to develop relationships.

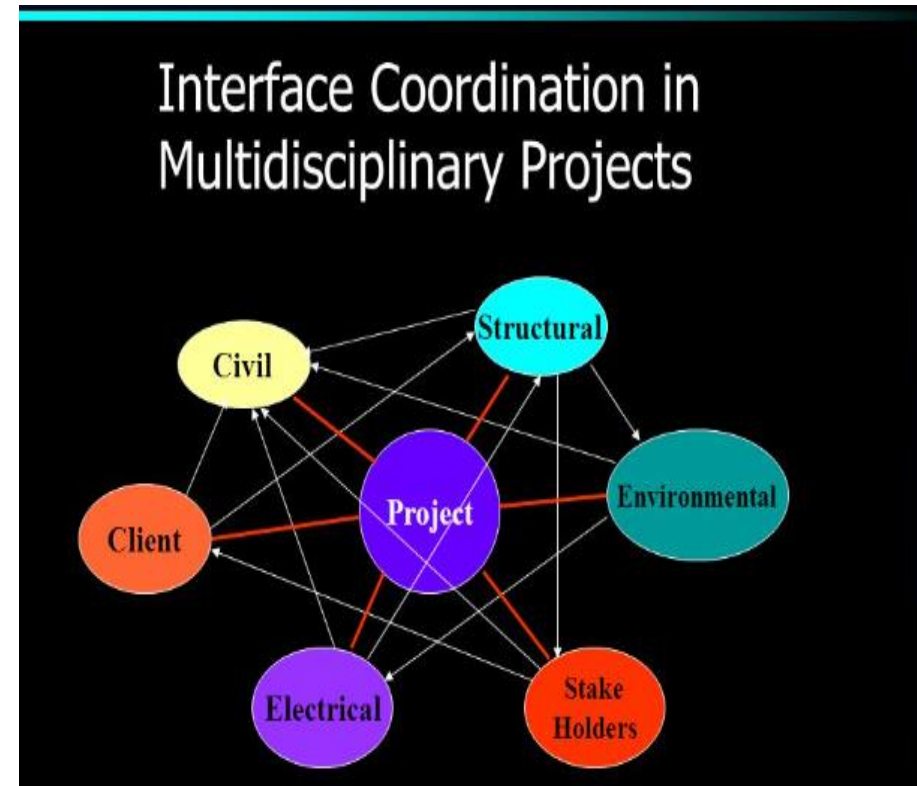


The Design Structure Matrix

The Design Structure Matrix (DSM) is a **general method** for representing and analyzing system models in a variety of application areas. A DSM is a **square matrix** that shows **relationships between elements in a system**.

DSM has two main advantages:

- It provides a simple and concise way to **represent** a complex system.
- It is amenable to powerful **analyses**, such as clustering and sequencing. *قابلة للتحليلات القوية، مثل التجميع والتسلسل.*

	task 1	task 2	task 3	task 4	task 5	task 6
task 1		X			X	
task 2			X	X		
task 3	X					X
task 4						X
task 5				X		
task 6						

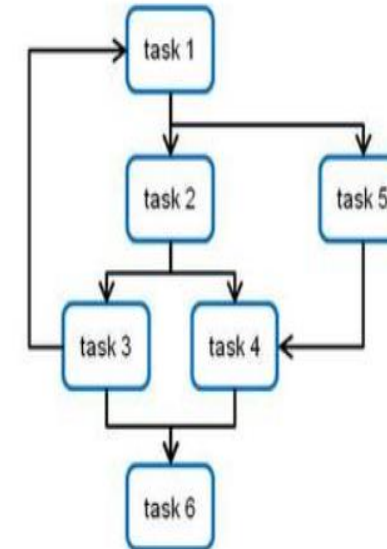

Comments on Empowerment and Work Teams

Some of the more important advantages of empowerment are:

1. Teams generate high - quality solutions to appropriate problems.
2. Micromanagement is avoided.
3. The team is given accountability for some part of the project deliverable.
4. Synergistic solutions are frequent.
5. The PM has a tool for timely team evaluation and feedback.





مجموعة جامعة
الجميع الذكية
للتعليم القابضة

MIDOCEAN
UNIVERSITY



Thank You

