



جامعة الجميع الذكية
EVERYONE'S SMART UNIVERSITY

Everyone's Smart University

Project (Spring 2021)

Student Name	ناصر المقرن Nasser Almugren	اسم الطالب
Students I.D	2021201349	الرقم الجامعي

Section

Master

Date

Thursday

18 / 03 / 2021.

Course Code

(PMG510)

Project Risk Management

Instructions:

- اخر موعد للتسليم هو يوم السبت 2021-05-08 في تمام الساعة ٩ مساءً.
- الإجابة متاحة باللغة الإنجليزية أو اللغة العربية مع مراعاة أن تكون المصطلحات العلمية باللغة الانجليزية.
- يتم تسليم المشروع في صيغة ملف . pdf مع الالتزام نموذج الجامعة ولن تقبل أي مستندات أخرى.
- يجب مراعاة أقسام البحث الرئيسية (مقدمة Introduction، دراسات علمية سابقة Literature Review، طريقة البحث Methodology، النتائج والمناقشة Results and Discussion، وأخيراً المراجع References . وان كان هناك ملحقات Appendices يتم إضافتها)
- يجب الالتزام بـ Theme موحد كما يلي:
- حجم الخط 12.
- نوع الخط Arial.
- لون الخط أسود.
- المسافة بين الأسطر line spacing 1.5
- عدد صفحات البحث (لا يقل عن ثلاث صفحات ولا يزيد عن ست صفحات).

Instructor's Name: Eng. Mosaab M. Hamed

Project:

Risk Identification and Analysis (Based on the project you chose in APM)

The objective of this report is to identify project risks, prepare a risk probability matrix, and carry out an analysis of selected risks. Referring to the project you select in **Advanced projects management APM course**, your task is to prepare a risk management plan that identifies potential risks in **the selected stage of the project** and identify risk management strategies.

From the course content and readings, you know that the overall purpose of risk planning is to anticipate possible risk events and be ready to take appropriate action when risk events occur—to eliminate or reduce negative impacts on the project.

You may wish to begin this exercise with a brainstorming about potential risks to get candidate risks “on the table” for consideration. And then identify and refine that wording for risks that have some realistic chance of occurring in this stage. For example, potential weather problems present a real obstacle to completing field data collection by the planned completion date. It is also an issue that the project manager will ultimately have to plan for, as opposed to other issues such as a major disaster (e.g., your office burning down), is not a high-enough probability event that requires much time in planning. As described below, you will select several of the identified risks and carry out a risk analysis.

You will use the distilled list of risks to make a risk probability/impact matrix. The matrix will have at least three categories (high/medium/low) for probability and impact.

Remember that it is important to name risks effectively—use words that describe the risk event and point to the impact on the project (e.g., “injury of field technician disrupts data installation work”).

After completion of the risk matrix, document a risk analysis for the selected risks. This detailed documentation for that selected risk will include:

- a description of the risk and potential impacts (schedule, quality of work, cost, etc.) on the project.
- indicators or triggers that would be monitored to help identify the risk as early as possible.
- specific risk response strategies to take.

Using probability and impact matrix calculate the **Expected Monetary Value (EMV)** for all risks that have the impact in terms of cost \$\$.

Best of luck...

المشروع:

التعرف على المخاطر وتحليلها (بحث مبني على مشروعك الذي اخترته في مادة ادارة المشاريع المتقدمة)

الغرض من هذا التقرير هو التعرف على المخاطر المحيطة بالمرحلة التي تختارها المرحلة من مراحل مشروعك (نفس المرحلة التي اخترت التطرق لها في مشروعك لمادة إدارة المشاريع المتقدمة Advanced project management) حيث أن مهمتك هي تحضير خطة متكاملة لإدارة المخاطر تشمل التعريف بالمخاطر المحتملة التي تحيط بتلك المرحلة وتحضير مصفوفة احتمالية المخاطر ومن ثم القيام بالتحليل لهذه المخاطر المختارة وتحديد استراتيجيات ادارة المخاطر المناسبة لكل خطر على حدة.

من محتويات المقرر والمصادر الأخرى المتاحة أصبحت تعلم الان أن الغرض العام لمرحلة التخطيط للمخاطر هي توقع أحداث المخاطر المحتملة والتجهز لاتخاذ ردة الفعل المناسبة عند وقوع الخطر – لمنع أو تقليل الآثار السلبية على المشروع.

قد تحبذ بداية هذا البحث بعصف ذهني عن ماهية المخاطر التي قد تحيط بتلك المرحلة من مراحل مشروعك, وذلك للحصول على قائمة بتلك المخاطر. ومن ثم تحديد وتصفية هذه القائمة للوصول إلى قائمة مختصرة بالمخاطر التي لها فرصة واقعية أكبر في الحدوث. على سبيل المثال: المشاكل الجوية المتوقعة والتي تمثل عقبة حقيقية أمام اكتمال جمع البيانات من المواقع في أو قبل الوقت المحدد، هذه تعتبر مشكلة على مدير المشاريع أن يضعها في الحسبان. من ناحية أخرى، فإن المخاطر غير الواقعية مثل الكوارث الطبيعية والأعاصير (تلك التي تسبب حريقاً بمكتبك وفقدان الأوراق المهمة) ليست لها احتمالية وقوع عالية وبالتالي لاتستدعي تضيق الكثير من الوقت في التخطيط لها. كما سيتبين لك، ستقوم باختيار عدة مخاطر من تلك التي قمت بالتعرف عليها لتحليلها.

سنقوم باستخدام هذه القائمة المختصرة لعمل مصفوفة المخاطر (الاحتمالية/الأثر). المصفوفة ستحتوي على الأقل على ثلاث تصنيفات (عالي/متوسط/منخفض) للإحتمالية والأثر.

لاتنس استخدام أسماء تصف طبيعة المخاطر بصورة فعالة – قم باستخدام كلمات تصف الحادثة الخطرة وتشير الى أثرها على المشروع (مثل: إصابة أحد الفنيين في الموقع مما يؤثر على أعمال التركيب).

بعد انتهاءك من مصفوفة المخاطر، قم بتوثيق تحليلك للمخاطر المختارة. هذا التسجيل المفصل للمخاطر يجب أن يتضمن:

- وصف للخطر واثاره المحتملة (الجدولة، جودة العمل، التكلفة، الخ)
- المؤشرات والمحفزات التي يجب مراقبتها للمساعدة في التعرف على هذا الخطر قبل وقوعه
- تفصيل للاستجابة المقترحة للتصدي لهذا الخطر

باستخدام مصفوفة الاحتمالات والتأثير ، احسب **القيمة النقدية المتوقعة (EMV)** لجميع المخاطر التي لها تأثير من حيث التكلفة \$\$.

مع تمنياتي بالتوفيق..

E – Insurance project

Brief:


E-Insurance, the insurance ecommerce or digital insurance is a large project with many phases, approaches, and stakeholders.

In the Saudi market, we are still at the beginning of this industry and we are mainly adopting the E-sales of insurance and some customer services. The electronic sales have many channels and models and each one has its own risk.

Therefore, will mentioned some of the risks about the initial process of E-Insurance which is the electronic sales.

Project's Process:

In order to simplify the project's risk, will divide the projects in six main process and specify the major risks.

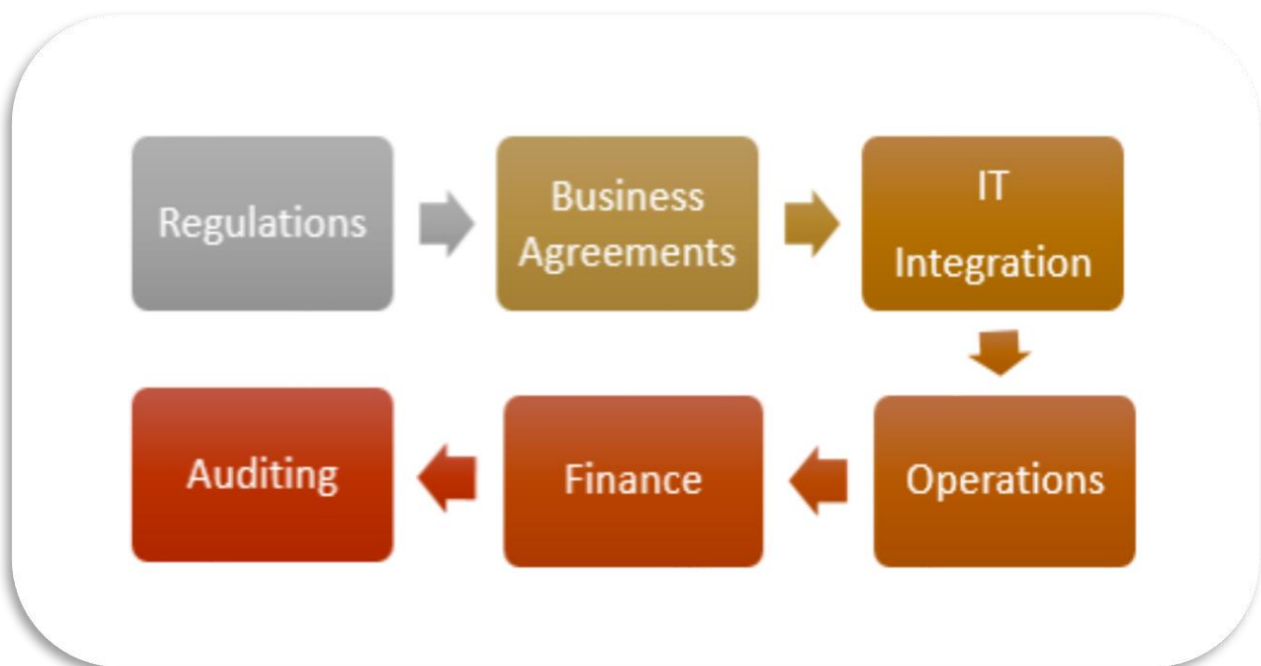

The process is representing the department too.

Risks Analysis:


Risks can be vary and have different level and prospective. A straightforward technique is to list the risks and calculate and the probabilities and the impacts. Such process can be used like 8Rs and 4Ts to simplify the study.

Function	Risk
Regulations	- New regulations against this project
Business Agreements	- unprofessional business partner - Unfair contract - Business partner internal issues - Agree on the wrong products
IT integration	- Lack of knowledge - Lack of source - Lack of budget - Technical issues - Data issue
Operation	- Delay on Issuing policies - Cancelling policies / un-canceling - Wrong Modification - Bad customer services - Not handling the complaint
Finance	- Mistakes in calculations - Mistakes in reports - Delay in issuing invoices - Bad money collections
Auditing	- Inefficient auditing - Low quality reports

Probability vs Impact

Function Risk	Probability	Impact
Regulations	0.1	0.9
Business Agreements	0.2	0.7
IT integration	0.5	0.7
Operation	0.5	0.3
Finance	0.2	0.3
Auditing	0.4	0.4

Probability	0.7-1	high	high	medium
	0.3-0.69	high	medium	low
	0-0.29	medium	low	low
		0.7-1	0.3-0.69	0-0.29
		Impact		

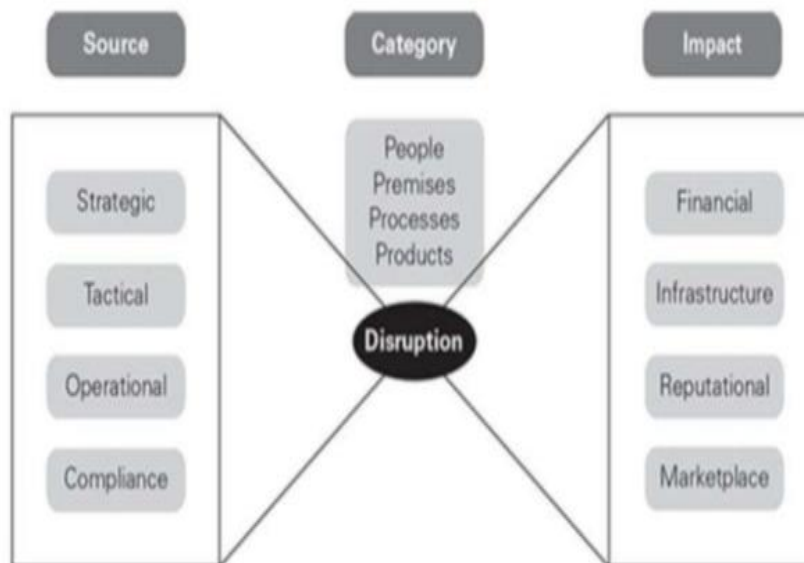

Function	Probability	Impact	Severity	Response plan	Mitigate Action
Regulations	0.1	0.9	M	Work very closely with the regulator	Be the first who follow to gain the advantage
Business Agreements	0.2	0.7	M	Choose the business partner based on real figures	No waste for time and budget
IT integration	0.5	0.7	H	Out sourcing	Find the experienced one
Operation	0.5	0.3	M	Invest in technology	Minimize the human involvement
Finance	0.2	0.3	L	Maximizing Auditing	Minimizing process
Auditing	0.4	0.4	M	Technology	Invest in technology

EMV Simulation:

The project Simulation cost is SAR 1,000,000.

Therefore, calculate based on the simulated cost.

Function	Probability	Impact Cost in SAR	Risk contingency
Regulations	0.1	272,727.27	27,272.73
Business Agreements	0.2	212,121.21	42,424.24
IT integration	0.5	212,121.21	106,060.61
Operation	0.5	90,909.09	45,454.55
Finance	0.2	90,909.09	18,181.82
Auditing	0.4	121,212.12	48,484.85
Total		1,000,000	287,878.79

The Conclusion:

This project has different kind of risks and each reach has its own character. Severity is one main measurement in our study and based on that we can choose the appropriate way to deal with.

In some conditions, we can avoid the risk while in other we can only minimize it. However, the risk management is necessary in any project and investing in that will back to you with real profit.

Reference:

- Slides
- Project samples
- Real project case
