



جامعة الجميع الذكية
EVERYONE'S SMART UNIVERSITY

Everyone's Smart University

Project (Spring 2021)

Student Name	Hassan Ali Alsadeer	اسم الطالب
Students I.D	2021200464	الرقم الجامعي

Section

Master

Date

Thursday

18 / 03 / 2021.

Course Code

(PMG510)

Project Risk Management

Instructions:

- اخر موعد للتسليم هو يوم السبت 2021-05-08 في تمام الساعة ٩ مساءً.
- الإجابة متاحة باللغة الإنجليزية أو اللغة العربية مع مراعاة أن تكون المصطلحات العلمية باللغة الانجليزية.
- يتم تسليم المشروع في صيغة ملف . pdf مع الالتزام نموذج الجامعة ولن تقبل أي مستندات أخرى.
- يجب مراعاة أقسام البحث الرئيسية (مقدمة Introduction، دراسات علمية سابقة Literature Review، طريقة البحث Methodology، النتائج والمناقشة Results and Discussion ، وأخيراً المراجع References . وان كان هناك ملحقات Appendices يتم إضافتها)
- يجب الالتزام بـ Theme موحد كما يلي:
- حجم الخط 12.
- نوع الخط Arial.
- لون الخط أسود.
- المسافة بين الأسطر line spacing 1.5
- عدد صفحات البحث (لا يقل عن ثلاث صفحات ولا يزيد عن ست صفحات).

Instructor's Name: Eng. Mosaab M. Hamed

Project:

Risk Identification and Analysis (Based on the project you chose in APM)

The objective of this report is to identify project risks, prepare a risk probability matrix, and carry out an analysis of selected risks. Referring to the project you select in **Advanced projects management APM course**, your task is to prepare a risk management plan that identifies potential risks in **the selected stage of the project** and identify risk management strategies.

From the course content and readings, you know that the overall purpose of risk planning is to anticipate possible risk events and be ready to take appropriate action when risk events occur—to eliminate or reduce negative impacts on the project.

You may wish to begin this exercise with a brainstorming about potential risks to get candidate risks “on the table” for consideration. And then identify and refine that wording for risks that have some realistic chance of occurring in this stage. For example, potential weather problems present a real obstacle to completing field data collection by the planned completion date. It is also an issue that the project manager will ultimately have to plan for, as opposed to other issues such as a major disaster (e.g., your office burning down), is not a high-enough probability event that requires much time in planning. As described below, you will select several of the identified risks and carry out a risk analysis.

You will use the distilled list of risks to make a risk probability/impact matrix. The matrix will have at least three categories (high/medium/low) for probability and impact.

Remember that it is important to name risks effectively—use words that describe the risk event and point to the impact on the project (e.g., “injury of field technician disrupts data installation work”).

After completion of the risk matrix, document a risk analysis for the selected risks. This detailed documentation for that selected risk will include:

- a description of the risk and potential impacts (schedule, quality of work, cost, etc.) on the project.
- indicators or triggers that would be monitored to help identify the risk as early as possible.
- specific risk response strategies to take.

Using probability and impact matrix calculate the **Expected Monetary Value (EMV)** for all risks that have the impact in terms of cost \$\$.

Best of luck...

المشروع:

التعرف على المخاطر وتحليلها (بحث مبني على مشروعك الذي اخترته في مادة ادارة المشاريع المتقدمة)

الغرض من هذا التقرير هو التعرف على المخاطر المحيطة بالمرحلة التي تختارها المرحلة من مراحل مشروعك (نفس المرحلة التي اخترت التطرق لها في مشروعك لمادة إدارة المشاريع المتقدمة Advanced project management) حيث أن مهمتك هي تحضير خطة متكاملة لإدارة المخاطر تشمل التعريف بالمخاطر المحتملة التي تحيط بتلك المرحلة وتحضير مصفوفة احتمالية المخاطر ومن ثم القيام بالتحليل لهذه المخاطر المختارة وتحديد استراتيجيات ادارة المخاطر المناسبة لكل خطر على حدة.

من محتويات المقرر والمصادر الأخرى المتاحة أصبحت تعلم الان أن الغرض العام لمرحلة التخطيط للمخاطر هي توقع أحداث المخاطر المحتملة والتجهز لاتخاذ ردة الفعل المناسبة عند وقوع الخطر – لمنع أو تقليل الاثار السلبية على المشروع.

قد تحبذ بداية هذا البحث بعصف ذهني عن ماهية المخاطر التي قد تحيط بتلك المرحلة من مراحل مشروعك, وذلك للحصول على قائمة بتلك المخاطر. ومن ثم تحديد وتصفية هذه القائمة للوصول إلى قائمة مختصرة بالمخاطر التي لها فرصة واقعية أكبر في الحدوث. على سبيل المثال: المشاكل الجوية المتوقعة والتي تمثل عقبة حقيقية أمام اكتمال جمع البيانات من المواقع في أو قبل الوقت المحدد، هذه تعتبر مشكلة على مدير المشاريع أن يضعها في الحسبان. من ناحية أخرى، فإن المخاطر غير الواقعية مثل الكوارث الطبيعية والأعاصير (تلك التي تسبب حريقاً بمكتبك وفقدان الأوراق المهمة) ليست لها احتمالية وقوع عالية وبالتالي لاتستدعي تضيق الكثير من الوقت في التخطيط لها. كما سيتبين لك، ستقوم باختيار عدة مخاطر من تلك التي قمت بالتعرف عليها لتحليلها.

ستقوم باستخدام هذه القائمة المختصرة لعمل مصفوفة المخاطر (الاحتمالية/الأثر). المصفوفة ستحتوي على الأقل على ثلاث تصنيفات (عالي/متوسط/منخفض) للإحتمالية والأثر.

لاتنس استخدام أسماء تصف طبيعة المخاطر بصورة فعالة – قم باستخدام كلمات تصف الحادثة الخطرة وتشير الى أثرها على المشروع (مثل: إصابة أحد الفنيين في الموقع مما يؤثر على أعمال التركيب).

بعد انتهاءك من مصفوفة المخاطر، قم بتوثيق تحليلك للمخاطر المختارة. هذا التسجيل المفصل للمخاطر يجب أن يتضمن:

- وصف للخطر واثاره المحتملة (الجدولة، جودة العمل، التكلفة، الخ)
- المؤشرات والمحفزات التي يجب مراقبتها للمساعدة في التعرف على هذا الخطر قبل وقوعه
- تفصيل للاستجابة المقترحة للتصدي لهذا الخطر

باستخدام مصفوفة الاحتمالات والتأثير ، احسب **القيمة النقدية المتوقعة (EMV)** لجميع المخاطر التي لها تأثير من حيث التكلفة \$\$.

مع تمنياتي بالتوفيق..

Risk Management on The Project

Introduction:

Risk Analysis and Management is a key project management practice to ensure that the least number of surprises occur while your project is underway. While we can never predict the future with certainty, we can apply a simple and streamlined risk management process to predict the uncertainties in the projects and minimize the occurrence or impact of these uncertainties. This improves the chance of successful project completion and reduces the consequences of those risks.


Project team members at various levels identify and handle risks in different flavors. However, this will be ineffective without a structured risk management framework, as this leads to:

- Incomplete impact evaluation, leading to loss of:
 - Knowledge of the overall impact on the project objectives, like scope, time, cost, and quality
 - Identification of secondary or new risks arising from the already identified risks.
- Lack of transparency and a communication gap within and outside the team

Thus, it is very important for any project organization to set up an effective risk management framework. Instituting such a practice as a project team culture ensures:

- Conscious and focused risk identification and management.
- Project progress as desired, with the least number of deviations or surprise, and in line with project and organizational objectives.
- Early and effective communication of project issues to organization and project stakeholders.
- An effective team building tool, as team buy-in and acceptance is assured.

Risk Management Process:

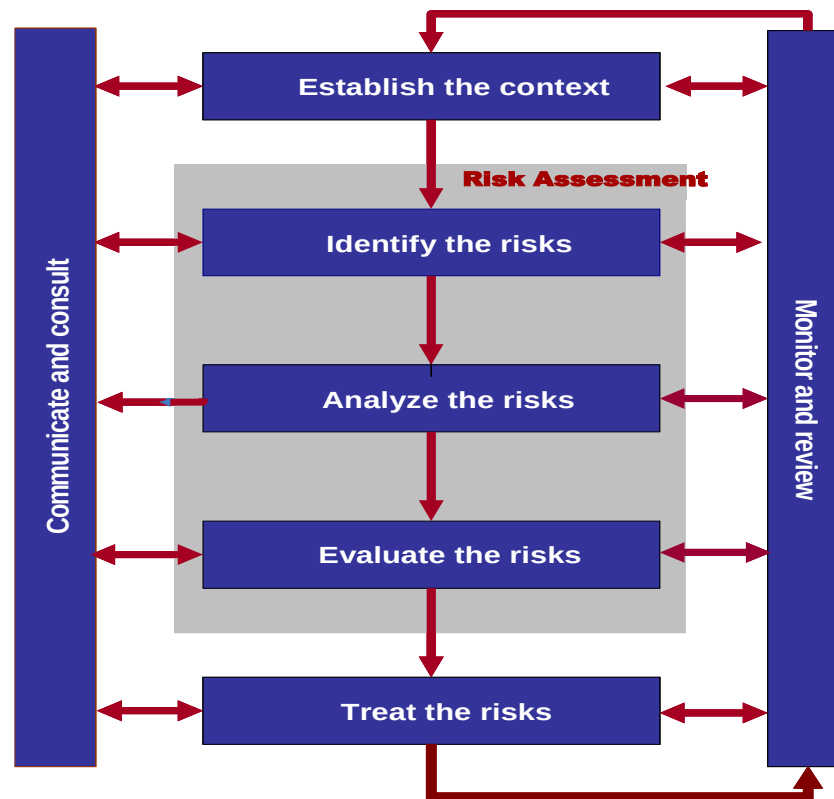

Risk Management Plan

The organization-mandated risk management framework is reviewed and tailored to define the project risk management plan when the project is initiated. The risk management plan includes these definitions and guidelines:

- List of possible risk sources and categories
- Impact and probability matrix
- Risk reduction and action plan
- Contingency plan
- Risk threshold and metrics.

Risk Identification:

Risks are to be identified and dealt with as early as possible in the project. Risk identification is done throughout the project life cycle, with special emphasis during the key milestones.

1) Risk Sources

Risk Source	Description
Risk repository	The risk repository is the history data containing the list of risks identified for completed projects. The risk repository can be used to arrive at a list of potential risks for the project. This risk repository can also be filtered based on risk sources, categories, and projects.
Checklist analysis	The risk identification checklist is a questionnaire that helps identify gaps and potential risks. It is developed based on experience and project type.
Expert judgement	Risk identification is also done by brainstorming with or interviewing experienced project participants, stakeholders, and subject matter experts.
Project status	The project status includes project status meeting reports, status reports, progress reports, and quality reports. These reports provide the current project progress, issues faced, and threshold violations. These provide insight into the status of the project and potential new risks.

2) Risk Category

Risk Category	Extended categories
Technical	Requirements, Technology, Interfaces, Performance, Quality, etc.
External	Customer, Contract, Market, Supplier, etc.
Organizational	Project Dependencies, Logistics, Resources, Budget, etc.
Project Management	Planning, Schedule, Estimation, Controlling, Communication, etc.

3) Risk Analysis:

Risk analysis involves examining how project outcomes and objectives might change due to the impact of the risk event.

Once the risks are identified, they are analyzed to identify the qualitative and quantitative impact of the risk on the project so that appropriate steps can be taken to mitigate them. The following guidelines are used to analyze risks.

Probability of Risk Occurrence Used by the Project Team to Determine for Each Project Risk the Level of Probability.

Probability	Description
1.0	Certain to Occur
0.8	Highly likely
0.6	Likely
0.4	Low Likelihood
0.2	Very Unlikely
0.0	No Probability of Occurring

4) Calculating Expected Value for Each Risk

Each identified risk event on the project was assigned a probability and impact value. An expected value was then calculated for each risk event using the following formula:

$$\text{Expected Value (EV)} = \text{Probability} \times \text{Impact Rating}$$

Expected value provides a scale to assess the importance of each risk event relative to other risk events. Using the probability and impact scales defined by the project team, the maximum expected value a risk event could have is 10 (1.0 probability x 10 impact). For simplicity, not all identified risk events on the project are shown below.

Risk #	Risk Event	Probability (0-1.0)	Impact (0-10)	Expected Value
1	The loss of key project personnel	0.4	10.0	4.0
2	Cost increases due to underestimates	0.5	8.0	4.0
3	Missing key project requirements	0.9	10.0	9.0
4	Increases in cost due to scope change	0.2	9.0	1.8
5	A lack of space to support on the project server.	0.7	9.0	6.3
6	The inability to automatically transfers existing project data	0.6	9.0	5.4
7	The inability to automatically feed actual cost data	0.5	10.0	5.0
8	System launches without the necessary training	0.8	7.0	5.6

Conclusion:

Successful project teams include risk management as part of their project plan. The probability of success on any project is much higher when the project team follows a structured risk management process. On project, use of risk management helped ensure successful completion of the project.

References:

- Graves, Roger. 2000. Qualitative Risk Assessment. PM Network (October).
- Lukas, Joseph. 1995. Managing Risks on Capital Projects. AACE Transactions.
- Lukas, Joseph. 2001. Manage Project Risks with Success. Inside Project Management.
- McKim, Robert. 1992. Risk Management—Back to Basics. Cost Engineering.
- Project Management Institute Standards Committee. 2000. A Guide to the Project Management Body of Knowledge. PMBOK® Guide. 2000 Edition. Newtown Square, PA: Project Management Institute.
- Royer, Paul. 2000. Risk Management: The Undiscovered Dimension of Project Management.
